

Job Name: 25-4490P1 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/23/2026 12:05:42 PM

Tech: Jared - A
PC: Celina Goff



Structure ID: MH 1-2 (7)

P2 MH048RS36 MH RISER

- P5) 24" - CASTING HEIGHT - 7"
- P4) 24" - GRADE RING - 4"
- P3) 48" - ECC CONE w/ 24" HOLE - 30"
- P2) 48" - MH RISER - 36"
- P1) 48" - MH BASE - 30"
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) CASTING - HOE MC-375 F/C Sanitary
- 2) 48" - Conseal CS-102 1.00" (Double)
- 2) 24" - Conseal CS-102 1.00" (Double)
- 2) PSX - 12-08 NYLO
- 8) MH Step ML-10-TDS-NCR - 10"

- Structure Notes:
- 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.
 - 2. PER ASTM C478 SPECIFICATIONS.
 - 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 - 4. REINFORCING PER ASTM A615 (GRADE 60).
 - CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.



0 lb
270 lb
2050 lb
2515 lb
3330 lb
1440 lb
0 lb
0 lb
271 lb
0 lb
0 lb
16 lb
0 lb

Structure Total: 9892 lb


Rim: 880.4' Rim to Invert: 8.75' Slack: 0" Sump: 2" Step Position: 236.5°

Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

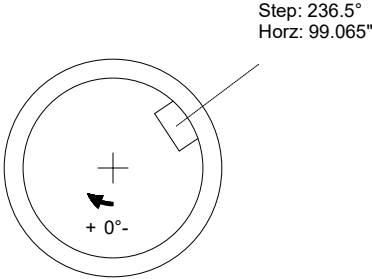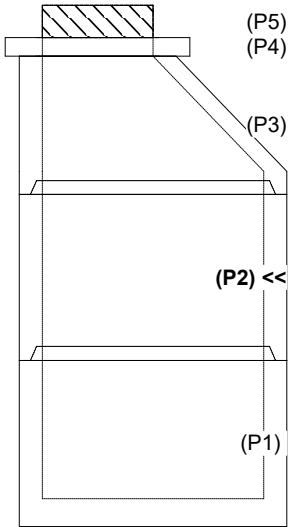

INSIDE WALL DIMENSIONS

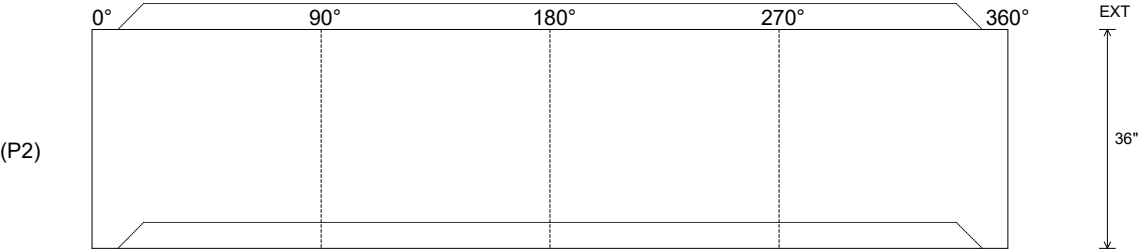

Coating (Int): Seam Up: Tongue Wall Thickness: 5" Height (Int): 36" Weight (Net): 2515 lb
Coating (Ext): Seam Dn: Groove Floor Height: 0" Height (Ext): 36" Volume (Net): 0.64cu.yd
