

Job Name: 25-4490P1 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100
7/23/2026 12:04:55 PM

Tech: Jared - A
PC: Celina Goff



Structure ID: MH 1-3 (6)

P3 MH048CN42



ECC CONE w/ 24" HOLE

- P5) 24" - CASTING HEIGHT - 7"
- P4) 24" - GRADE RING - 6"
- P3) 48" - ECC CONE w/ 24" HOLE - 42"
- P2) 48" - MH RISER - 60"
- P1) 48" - MH BASE - 30"
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) CASTING - HOE MC-375 F/C Sanitary
- 2) 48" - Conseal CS-102 1.00" (Double)
- 2) 24" - Conseal CS-102 1.00" (Double)
- 3) PSX - 12-08 NYLO
- 11) MH Step ML-10-TDS-NCR - 10"

- Structure Notes: .
- 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.
 - 2. PER ASTM C478 SPECIFICATIONS.
 - 3. CONCRETE = 4,000 PSI AT 28 DAYS.
 - 4. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
 - RISER/WALLS (As .12)
 - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

0 lb
405 lb
3200 lb
4192 lb
3282 lb
1440 lb
0 lb
0 lb
271 lb
0 lb
0 lb
24 lb
0 lb

Structure Total: 12814 lb

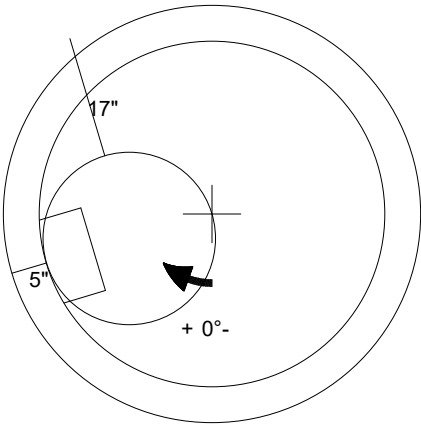

48" - ECC CONE w/ 24" HOLE - 42" - (P3)

Coating (Int):	Seam Up: Flat	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb
Coating (Ext):	Seam Dn: Groove			Volume (Net): 0.5cu.yd
