

Job Name: 25-4490P1 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100		Tech: Jared - A			
					7/23/2026 12:03:42 PM		PC: Celina Goff			
Structure ID: MH 1-3-10 (11)										
P1 MH048BA30					MH BASE					
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING - 4" P3) 48" - ECC CONE w/ 24" HOLE - 42" P2) 48" - MH RISER - 48" P1) 48" - MH BASE - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-06 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3200 lb 3353 lb 3282 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 24 lb 0 lb Structure Total: 11840 lb		Structure Notes: 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 889.74' Rim to Invert: 10.67' Slack: 0.04" Sump: 3" Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	879.07'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"
Invert 2	879.17'	168°	85.032"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"
Invert 3	879.17'	215°	108.821"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)


UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3282 lb Volume (Net): 0.84cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-4490P1 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/23/2026 12:03:42 PM		Tech: Jared - A PC: Celina Goff				
Structure ID: MH 1-3-10 (11)											
P1 MH048BA30		MH BASE									
P5) 24" - CASTING HEIGHT - 7" P4) 24" - GRADE RING - 4" P3) 48" - ECC CONE w/ 24" HOLE - 42" P2) 48" - MH RISER - 48" P1) 48" - MH BASE - 30" 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12-06 NYLO 10) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 3200 lb 3353 lb 3282 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 24 lb 0 lb		Structure Notes: . 1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Structure Total: 11840 lb					INVERT CHANNEL DRAWING						
Rim: 889.74' Rim to Invert: 10.67' Slack: 0.04" Sump: 3" Step Position: 90°											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	879.07'	0°	0"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	0"	0"	
Invert 2	879.17'	168°	85.032"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"	
Invert 3	879.17'	215°	108.821"	6" PVC SDR35	6.25"	PSX 12-06 NYLO	12"	12.129"	1.2"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											


RIGHT-SIDE UP VIEW (int. dimensions)

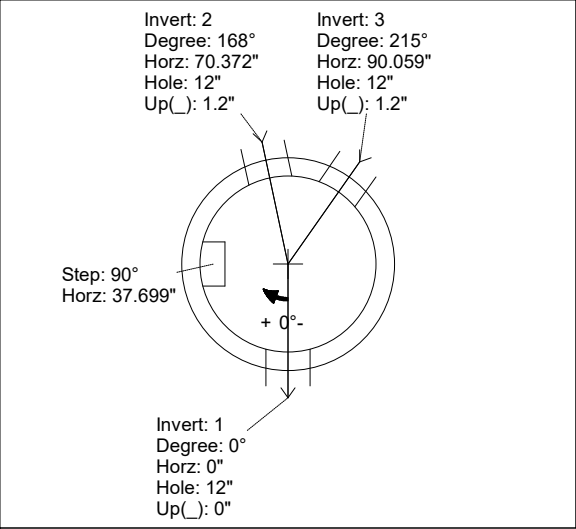

UPSIDE-DOWN VIEW (int. dimensions)

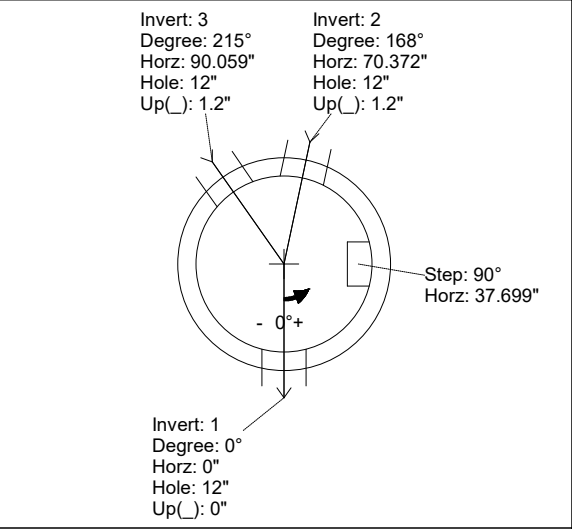

INSIDE WALL DIMENSIONS

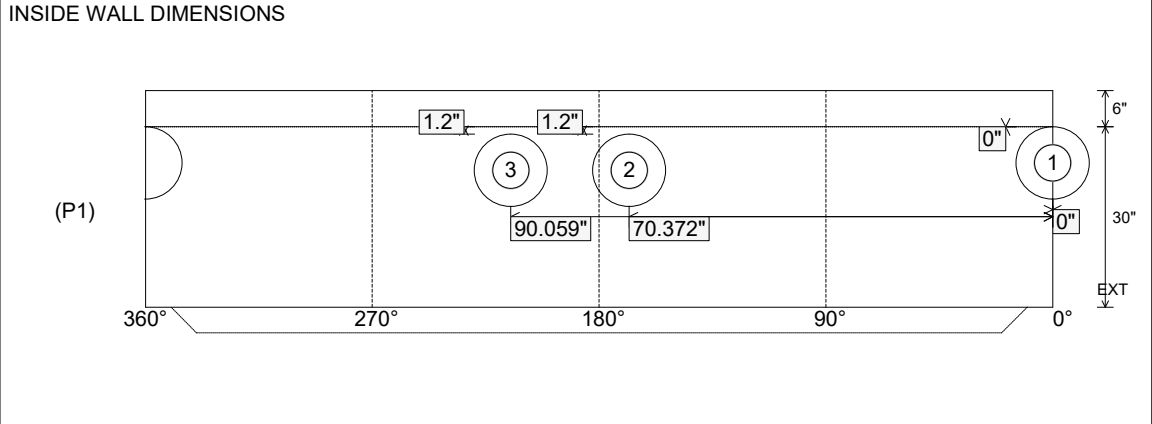

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3282 lb Volume (Net): 0.84cu.yd
----------------------------------	---------------------------------	--	--	--
