

Job Name: 25-4490P1 Heartland Meadows Subdivision
Job Location: Elizabethtown, KY 40165
Contractor: Kauffeld Brothers Construction

Plant: 100

7/23/2026 12:04:59 PM

Tech: Jared - A
PC: Celina Goff



Structure ID: MH 1-4-11 (12)

P2 MH048CN42

ECC CONE w/ 24" HOLE



- P3) 24" - CASTING HEIGHT - 7"
- P2) 48" - ECC CONE w/ 24" HOLE - 42"
- P1) 48" - MH BASE - 36"
- 1) 48" - MH INVERT CHANNEL - FULL HEIGHT
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) CASTING - HOE MC-375 F/C Sanitary
- 1) 48" - Conseal CS-102 1.00" (Double)
- 1) 24" - Conseal CS-102 1.00" (Double)
- 2) PSX - 12-08 NYLO
- 6) MH Step ML-10-TDS-NCR - 10"

0 lb
3200 lb
3749 lb
1440 lb
0 lb
0 lb
271 lb
0 lb
0 lb
0 lb
16 lb
0 lb

8676 lb

Structure Notes: .
1. HOE MC-375 F/C "SANITARY" PROVIDED BY ICAST.
2. PER ASTM C478 SPECIFICATIONS.
3. CONCRETE = 4,000 PSI AT 28 DAYS.
4. REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

Structure Total: 8676 lb

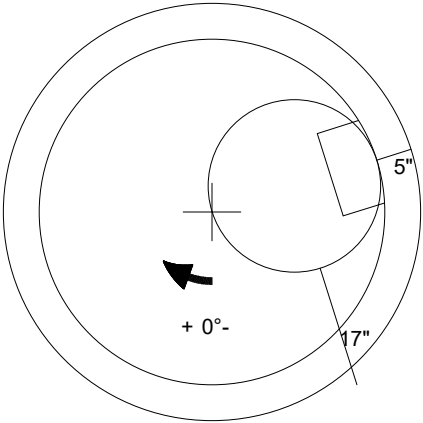

48" - ECC CONE w/ 24" HOLE - 42" - (P2)

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
----------------------------------	----------------------------------	--------------------	-------------------	---
