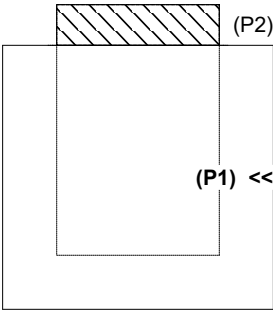


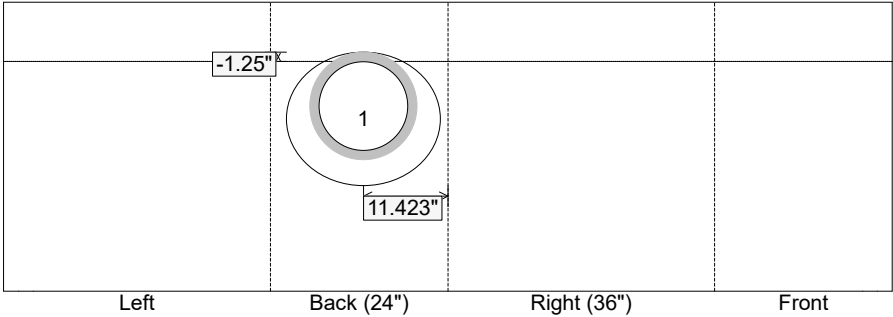
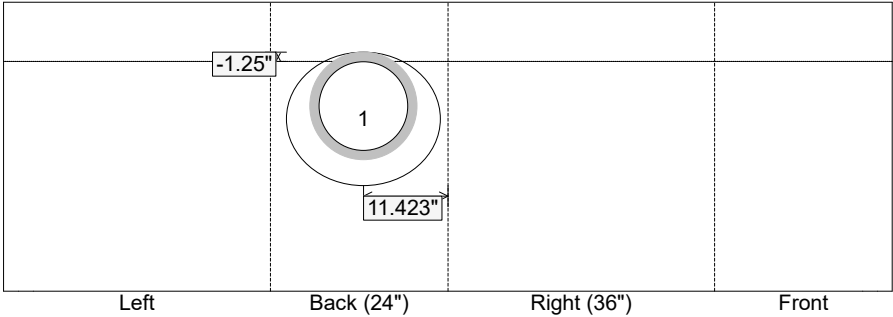


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction				Plant: 100 7/30/2026 10:23:06 AM		Tech: Jared - A PC: Celina Goff				
Structure ID: CB 1-15 (88)										
P1 BX2436-08BVF BOX BASE 8inW, 8inF, Variable Ht										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18						0 lb 4362 lb 394 lb 0 lb 0 lb ----- 0 lb Structure Total: 4756 lb		Structure Notes: 1. HOE 470 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.		
Rim: 872.88' Rim to Invert: 3.14' Slack: 0.68" Sump: 0" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	869.74'	210°	24.041"	12" HDPE	14.5"	Hole 18	18"	20.785"	-1.25"	-9.5"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimensions)										
										
INSIDE WALL DIMENSIONS										
										
Coating (Int): Coating (Ext):			Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 31" Height (Ext): 39"		Weight (Net): 4362 lb Volume (Net): 1.11cu.yd	
