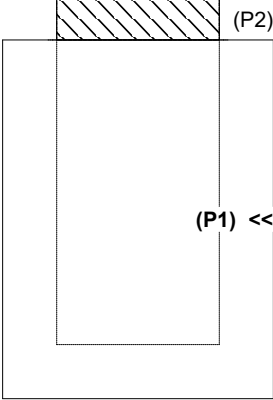

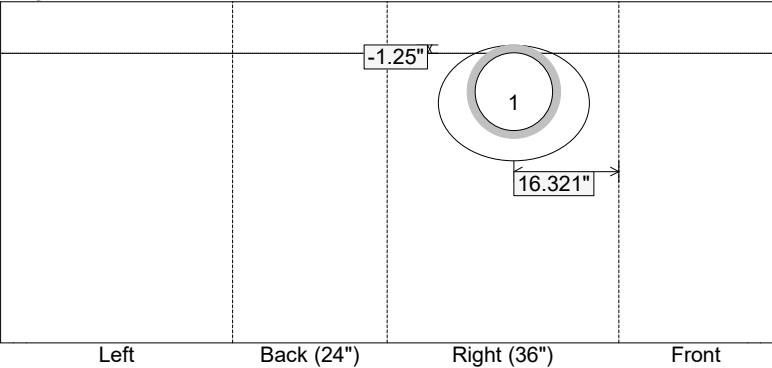


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction				Plant: 100 7/30/2026 10:22:47 AM		Tech: Jared - A PC: Celina Goff					
Structure ID: CB 2-34 (50)											
P1		BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht							
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 45" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18"				0 lb 5765 lb 394 lb 0 lb 0 lb ----- 6159 lb		Structure Notes: . 1. HOE 470 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 887.62'				Rim to Invert: 4.27'		Slack: 0.24"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	883.35'	130°	31.033"	12" HDPE	14.5"	Hole 18	18"	23.497"	-1.25"	-9"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) Invert: 1 Degree: 130° Horz: 16.321" Hole: 18" Up(): -1.25"  UPSIDE-DOWN VIEW (int. dimenions) Invert: 1 Degree: 130° Horz: 16.321" Hole: 18" Up(): -1.25"  INSIDE WALL DIMENSIONS (P1) 											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 45" Height (Ext): 53"		Weight (Net): 5765 lb Volume (Net): 1.47cu.yd	
