



Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:22:23 AM		Tech: Jared - A PC: Celina Goff					
Structure ID: CI 1-1 (13)												
P1 BX2436-08BVF		BOX BASE 8inW, 8inF, Variable Ht										
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 40" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 18					0 lb 5307 lb 394 lb 0 lb 0 lb ----- 5701 lb		Structure Notes: . 1. HOE 470 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C913 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. NO INVERT CHANNEL. 5. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 903.24'					Rim to Invert: 3.89'		Slack: 0.68"		Sump: 0"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset		
Invert 1	899.35'	270°	26"	12" HDPE	14.5"	Hole 18	18"	18"	-1.25"	0"		
Invert 2												
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

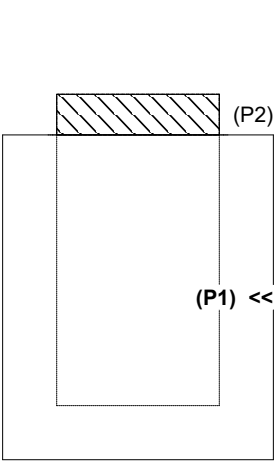


RIGHT-SIDE UP VIEW (int. dimensions)



UPSIDE-DOWN VIEW (int. dimensions)

INSIDE WALL DIMENSIONS

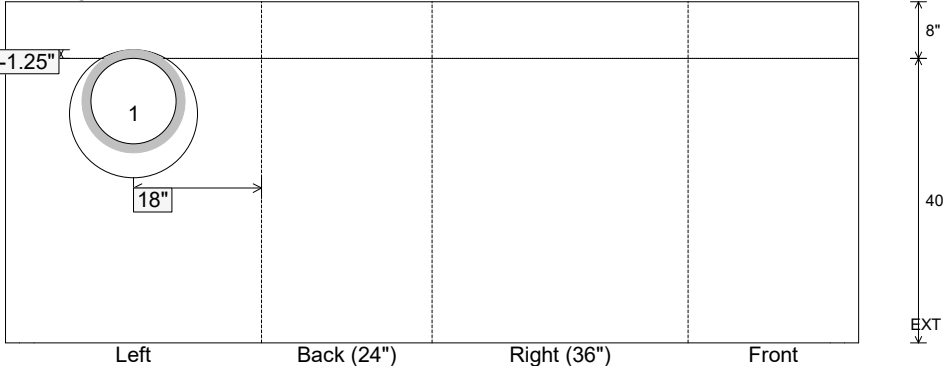

Left Back (24") Right (36") Front

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 40" Height (Ext): 48"	Weight (Net): 5307 lb Volume (Net): 1.36cu.yd
----------------------------------	-------------------------------	--	--	--
