




Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A			
Job Location: Elizabethtown, KY 40165					7/30/2026 10:22:36 AM		PC: Celina Goff			
Contractor: Kauffeld Brothers Construction										
Structure ID: CI 2-22 (31)										
P1 MH048BAVF			MH BASE Custom Ht							
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 48" P1) 48" - MH BASE Custom Ht - 28" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 24					0 lb 1935 lb 3156 lb 3089 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 8542 lb		Structure Notes: 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 878.11' Rim to Invert: 7.75' Slack: 0.6" Sump: 1.6" Step Position: 267°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	870.36'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

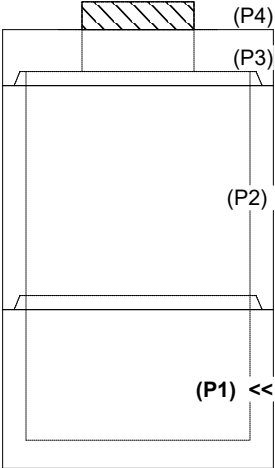





Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 28" Height (Ext): 34"	Weight (Net): 3089 lb Volume (Net): 0.79cu.yd
----------------------------------	---------------------------------	--	--	--
