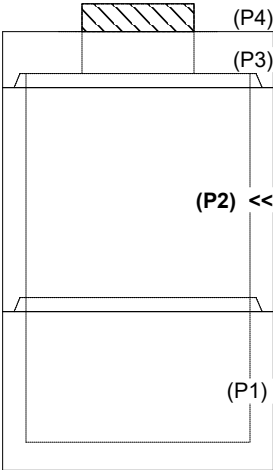

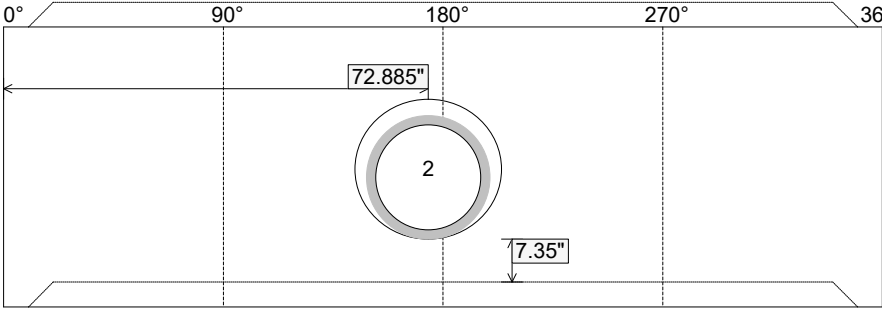


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:20:21 AM		Tech: Jared - A PC: Celina Goff				
Structure ID: CI 2-22 (31)											
P2 MH048RS48S		MH RISER SPECIAL									
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 48" P1) 48" - MH BASE Custom Ht - 28" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 24						0 lb 1935 lb 3156 lb 3089 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 8542 lb		Structure Notes: . 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 878.11'		Rim to Invert: 7.75'		Slack: 0.6"		Sump: 1.6"		Step Position: 267°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1											
Invert 2	873.66'	174°	88.069"	18" HDPE	21.2"	Hole 24	24"	25.133"	7.35"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
		Invert: 2 Degree: 174° Horz: 72.885" Hole: 24" Up(): 7.35" 									
INSIDE WALL DIMENSIONS											
		0° 90° 180° 270° 360° EXT 48"									
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3156 lb Volume (Net): 0.81cu.yd		
