


Job Name: 25-4490P2 Heartland Meadows Subdivision Job Location: Elizabethtown, KY 40165 Contractor: Kauffeld Brothers Construction					Plant: 100 7/30/2026 10:22:38 AM		Tech: Jared - A PC: Celina Goff			
Structure ID: CI 2-24 (33)										
P1 MH048BAVF			MH BASE Custom Ht							
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 60" P1) 48" - MH BASE Custom Ht - 55" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 24 1) Hole - 18					0 lb 1935 lb 4192 lb 4693 lb 362 lb 0 lb 0 lb 0 lb 0 lb ----- Structure Total: 11182 lb		Structure Notes: . 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 878.73' Rim to Invert: 11' Slack: 0.6" Sump: 1.6" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	867.73'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133", 3.246"	0"	0"
Invert 2	867.73'	109°	55.17"	12" HDPE	14.5"	Hole 18	18"	18.451"	0.35"	0"
Invert 3	867.73'	226°	114.389"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

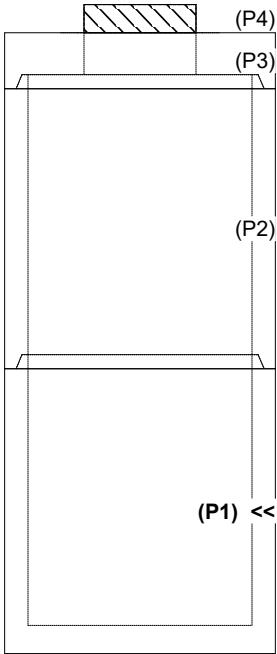

(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

Invert: 2
Degree: 109°
Horz: 45.658"
Hole: 18"
Up(): 0.35"

Invert: 3
Degree: 226°
Horz: 94.667"
Hole: 24"
Up(): 0"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 24"
Up(): 0"


UPSIDE-DOWN VIEW (int. dimenions)

Invert: 3
Degree: 226°
Horz: 94.667"
Hole: 24"
Up(): 0"

Invert: 2
Degree: 109°
Horz: 45.658"
Hole: 18"
Up(): 0.35"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 24"
Up(): 0"

INSIDE WALL DIMENSIONS

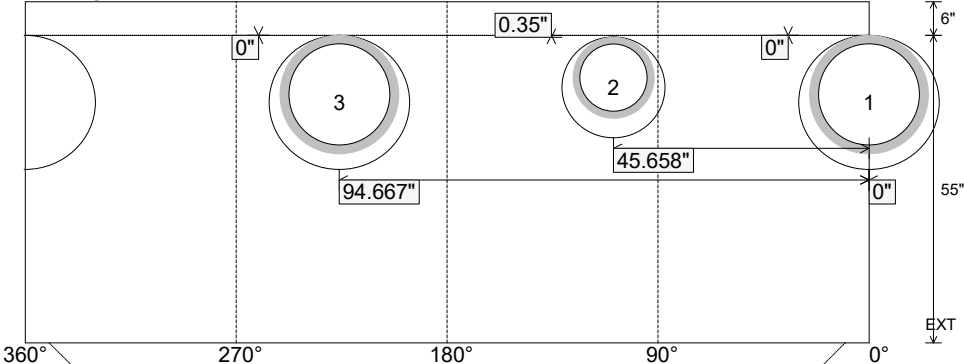

0" 0.35" 0" 0" 55" 6" EXT

360° 270° 180° 90° 0°

94.667" 45.658"

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 55" Height (Ext): 61"	Weight (Net): 4693 lb Volume (Net): 1.2cu.yd
----------------------------------	---------------------------------	--	--	---
