



Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A			
Job Location: Elizabethtown, KY 40165					7/30/2026 10:22:38 AM		PC: Celina Goff			
Contractor: Kauffeld Brothers Construction										
Structure ID: CI 2-25 (34)										
P1 MH048BAVF					MH BASE Custom Ht					
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 48" P1) 48" - MH BASE Custom Ht - 38" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 24"					0 lb 1935 lb 3353 lb 3584 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 9235 lb		Structure Notes: 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 875.04' Rim to Invert: 8.54' Slack: 0.08" Sump: 1.6" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	866.5'	0°	0"	18" HDPE	21.2"	Hole 24	24"	25.133"	0"	0"
Invert 2	866.5'	225°	113.883"	18" HDPE	21.2"	Hole 24	24"	25.133", 1.591"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

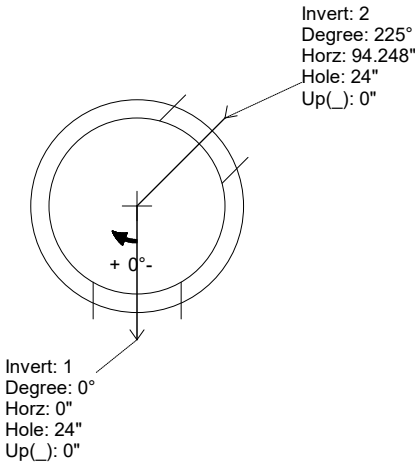

UPSIDE-DOWN VIEW (int. dimenions)

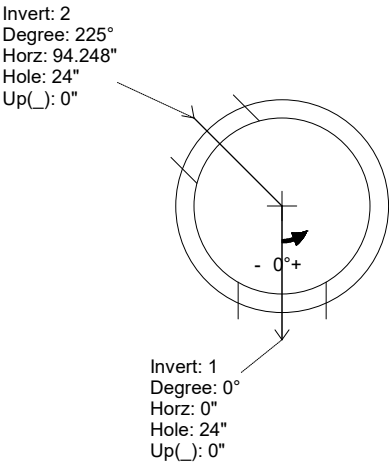

INSIDE WALL DIMENSIONS

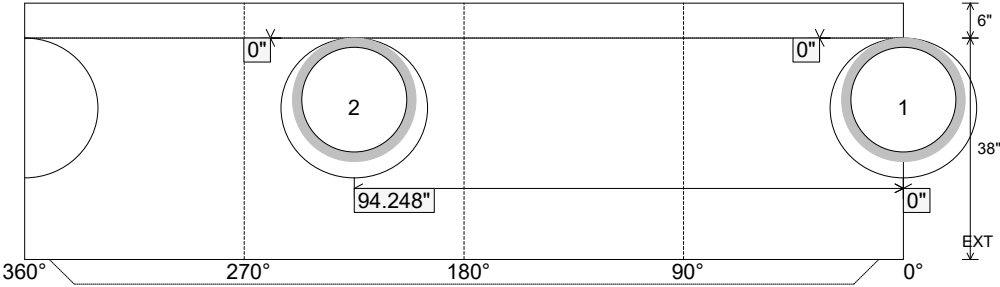

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 38" Height (Ext): 44"	Weight (Net): 3584 lb Volume (Net): 0.92cu.yd
----------------------------------	---------------------------------	--	--	--
