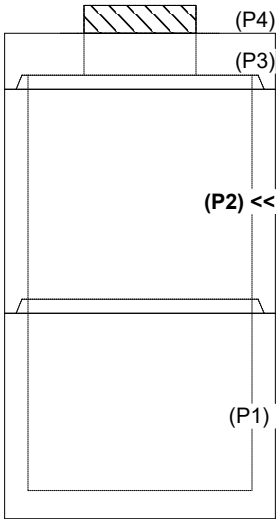

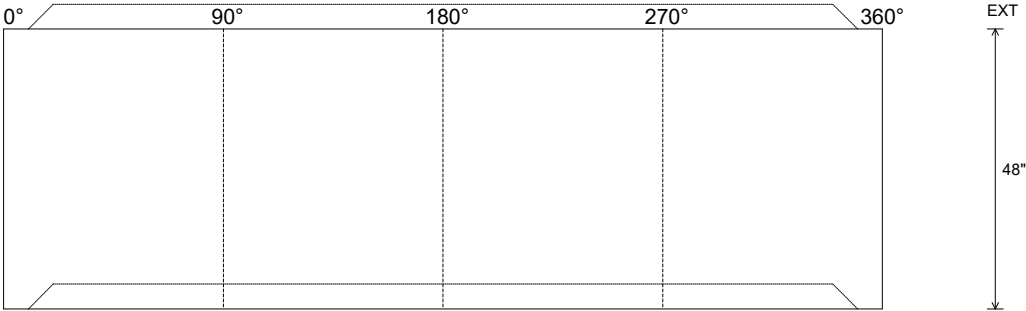


Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A				
Job Location: Elizabethtown, KY 40165					7/30/2026 10:20:23 AM		PC: Celina Goff				
Contractor: Kauffeld Brothers Construction											
Structure ID: CI 2-25 (34)											
P2 MH048RS48S			MH RISER SPECIAL								
P4) 24" x 30" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x30" Hole - 12" P2) 48" - MH RISER SPECIAL - 48" P1) 48" - MH BASE Custom Ht - 38" 1) CASTING - HOE 360 L Vane Set (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 30" - Conseal CS-102 1.00" 2) Hole - 24					0 lb 1935 lb 3353 lb 3584 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 9235 lb		Structure Notes: . 1. HOE 360 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 875.04' Rim to Invert: 8.54' Slack: 0.08" Sump: 1.6" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 48" Height (Ext): 48"		Weight (Net): 3353 lb Volume (Net): 0.86cu.yd		
