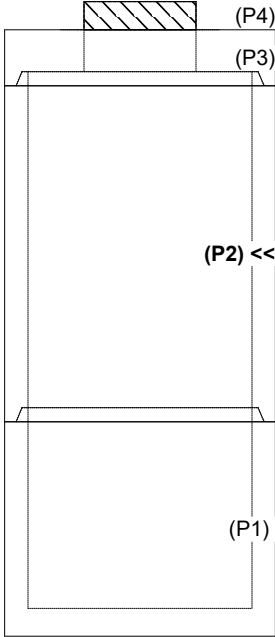




Job Name: 25-4490P2 Heartland Meadows Subdivision					Plant: 100		Tech: Jared - A				
Job Location: Elizabethtown, KY 40165					7/30/2026 10:20:24 AM		PC: Celina Goff				
Contractor: Kauffeld Brothers Construction											
Structure ID: CI 2-27 (36)											
P2 MH048RS72S					MH RISER SPECIAL						
P4) 24" x 36" - CASTING HEIGHT - 6" P3) 48" - MH FLAT TOP w/24"x36" Hole - 12" P2) 48" - MH RISER SPECIAL - 72" P1) 48" - MH BASE Custom Ht - 40" 1) CASTING - HOE 470 SET LV (F/G/H) 2) 48" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 30					0 lb 1300 lb 5030 lb 3534 lb 394 lb 0 lb 0 lb 0 lb ----- Structure Total: 10258 lb		Structure Notes: 1. HOE 470 FLAT SET PROVIDED BY ICAST. 2. PER ASTM C478 SPECIFICATIONS. 3. CONCRETE = 4,000 PSI AT 28 DAYS. 4. REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 870.72' Rim to Invert: 10.72' Slack: 0.54" Sump: 1.9" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
					EXT 72"						
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 72" Height (Ext): 72"		Weight (Net): 5030 lb Volume (Net): 1.28cu.yd	
