

Job Name: 25-4508 - Georgetown Commons Target
Job Location: Georgetown, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

5/28/2026 11:26:54 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: 10 (13)

P2 MH060LD13-24X36RECT

MH FLAT TOP w/24"x36" Hole F/G

P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 60" - MH FLAT TOP w/24"x36" Hole F/G - 13"
P1) 60" - MH BASE Custom Ht T/n - 55"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 60" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
2) Hole - 38

0 lb
3499 lb
7255 lb
394 lb
0 lb
0 lb
0 lb

0 lb

Structure Total:



11148 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL..
4. CASTING BY ICAST (HOE 470 SET LV (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

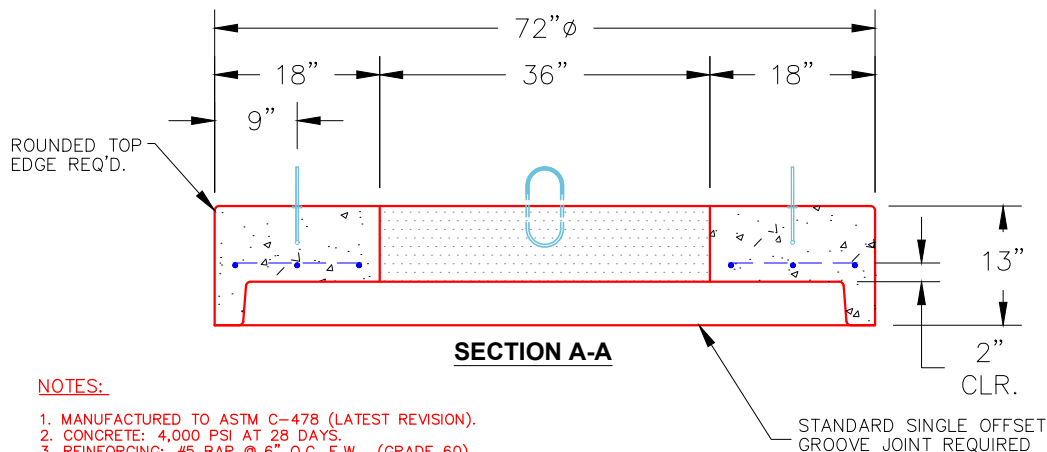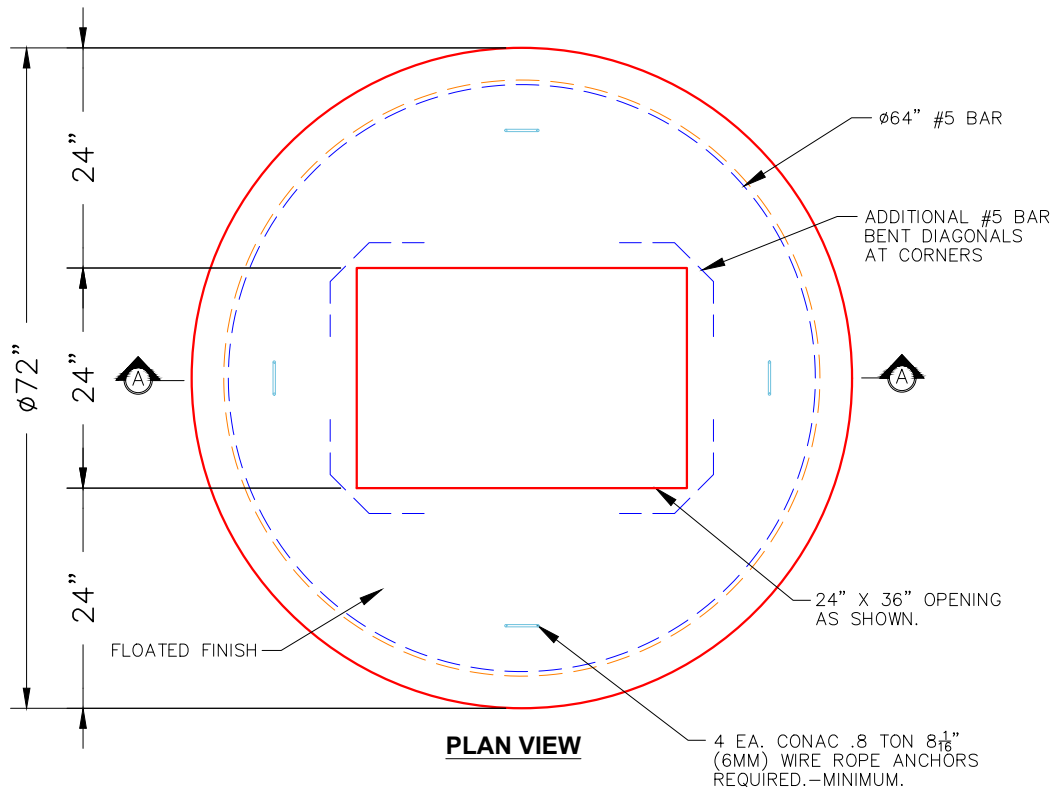

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 3499 lb
Volume (Net): 0.89cu.yd
