



Job Name: 25-4508 - Georgetown Commons Target Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.				Plant: 100 5/28/2026 11:25:36 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: 100 (23)										
P1 BX2430-08BA30				BOX BASE 8inW, 8inF T/n						
P3) 24" x 30" - CASTING HEIGHT - 6" P2) 24" x 30" - BOX RISER 8inW F/G - 24" P1) 24" x 30" - BOX BASE 8inW, 8inF T/n - 30" 1) CASTING - HOE 360 Set (F/G/H) 2) 24" x 30" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16				0 lb 2256 lb 3709 lb 362 lb 0 lb 0 lb 0 lb ----- Structure Total: 6326 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 360 SET (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 874.66' Rim to Invert: 4.91' Slack: 0.17' Sump: 1.25" Step Position:										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	869.75'	270°	23"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"
Invert 2	869.75'	0°	20"	12" HDPE	14.5"	Hole 16	16"	16"	0"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

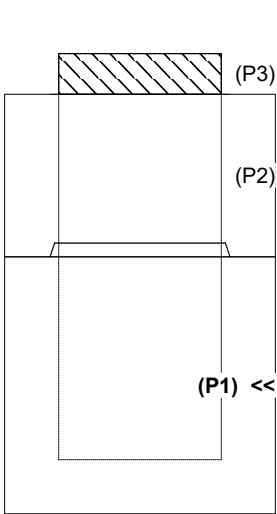

UPSIDE-DOWN VIEW (int. dimensions)

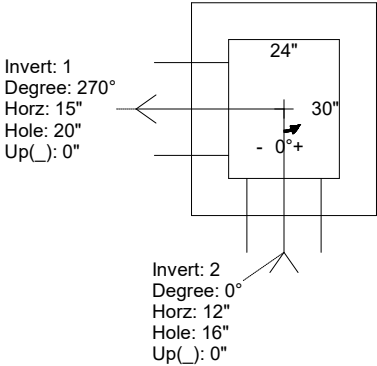

INSIDE WALL DIMENSIONS

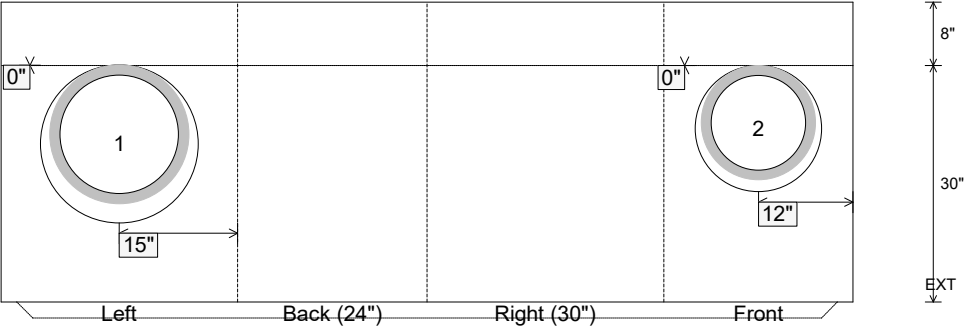

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 30" Height (Ext): 38"	Weight (Net): 3709 lb Volume (Net): 0.95cu.yd
----------------------------------	---------------------------------	--	--	--
