

Job Name: 25-4508 - Georgetown Commons Target
Job Location: Georgetown, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

5/28/2026 11:26:56 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: 102 (25)

P2 MH048LD12-24X30RECT

MH FLAT TOP w/24"x30" Hole F/G

P3) 24" x 30" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/24"x30" Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 51"
1) CASTING - HOE 360 Set (F/G/H)
1) 48" - Conseal CS-102 1.00"
1) 24" x 30" - Conseal CS-102 1.00"
2) Hole - 30
1) Hole - 16

0 lb
1935 lb
4175 lb
362 lb
0 lb
0 lb
0 lb
0 lb



6473 lb

Structure Total:

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 360 SET (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

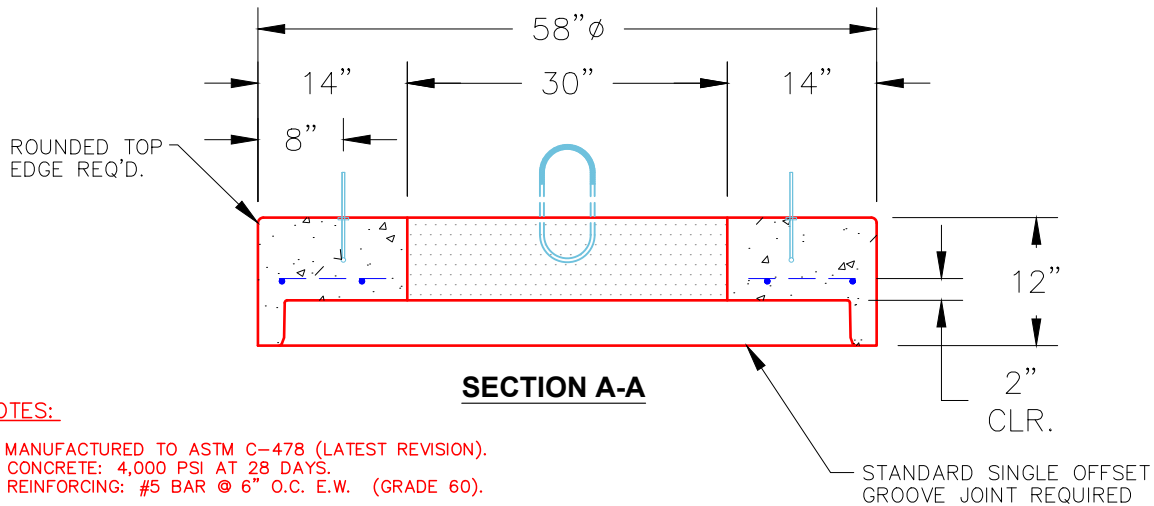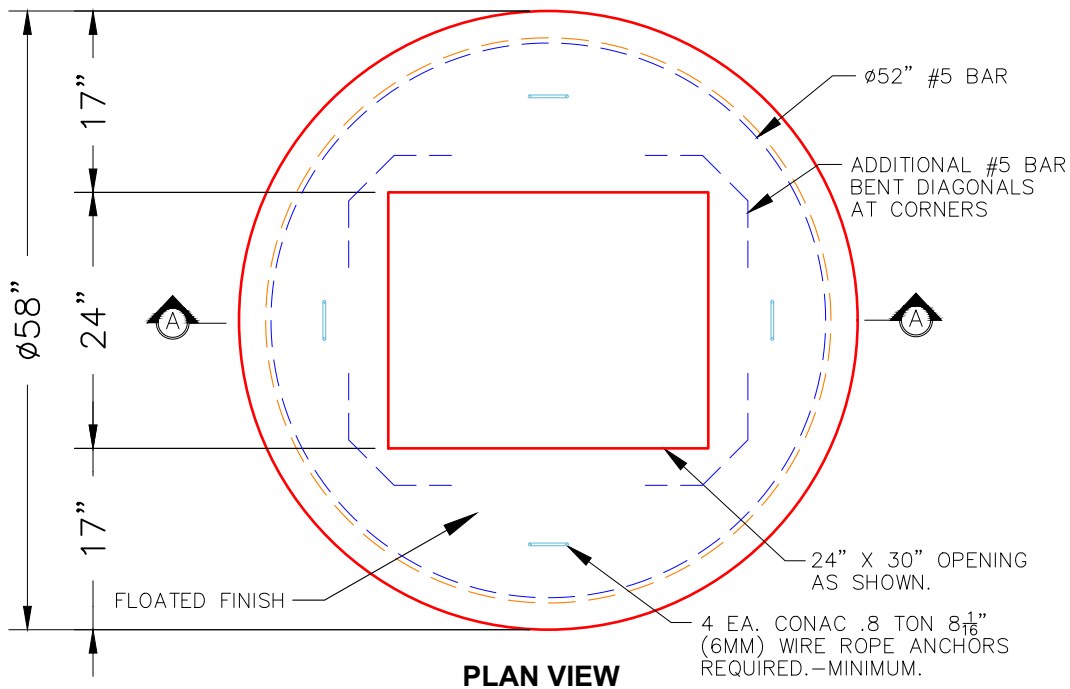

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1935 lb
Volume (Net): 0.49cu.yd
