

Job Name: 25-4508 - Georgetown Commons Target
Job Location: Georgetown, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

5/28/2026 11:26:57 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: 105 (27)

P2 MH048LD12ECC

MH FLAT TOP w/ 24" ECC Hole F/G

- P3) 24" - CASTING HEIGHT - 7"
P2) 48" - MH FLAT TOP w/ 24" ECC Hole F/G - 12"
P1) 48" - MH BASE Custom Ht T/n - 69"
1) CASTING - HOE MC-375 F/C Storm
1) 48" - Conseal CS-102 1.00"
2) Hole - 30
1) Hole - 16
6) MH Step ML-10-TDS-NCR - 10"

0 lb
1561 lb
5433 lb
271 lb
0 lb
0 lb
0 lb
0 lb
0 lb



Structure Total: 7265 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE MC-375 F/C STORM).

REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

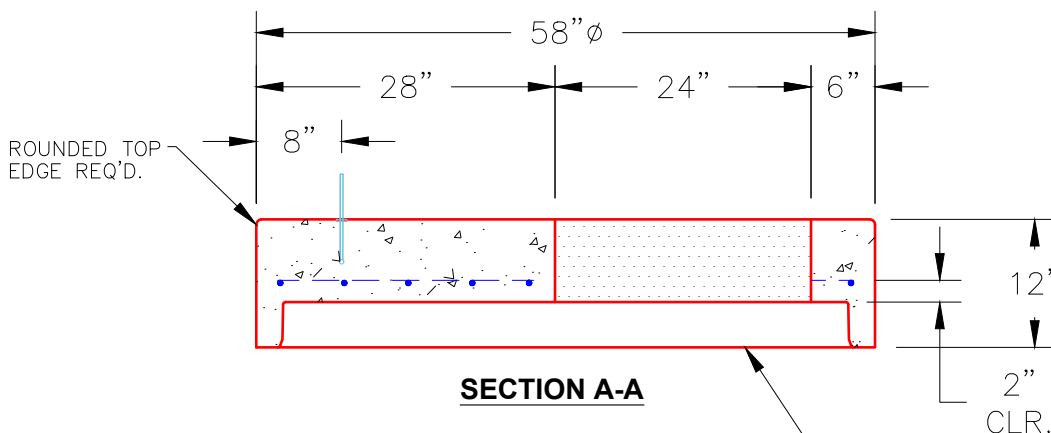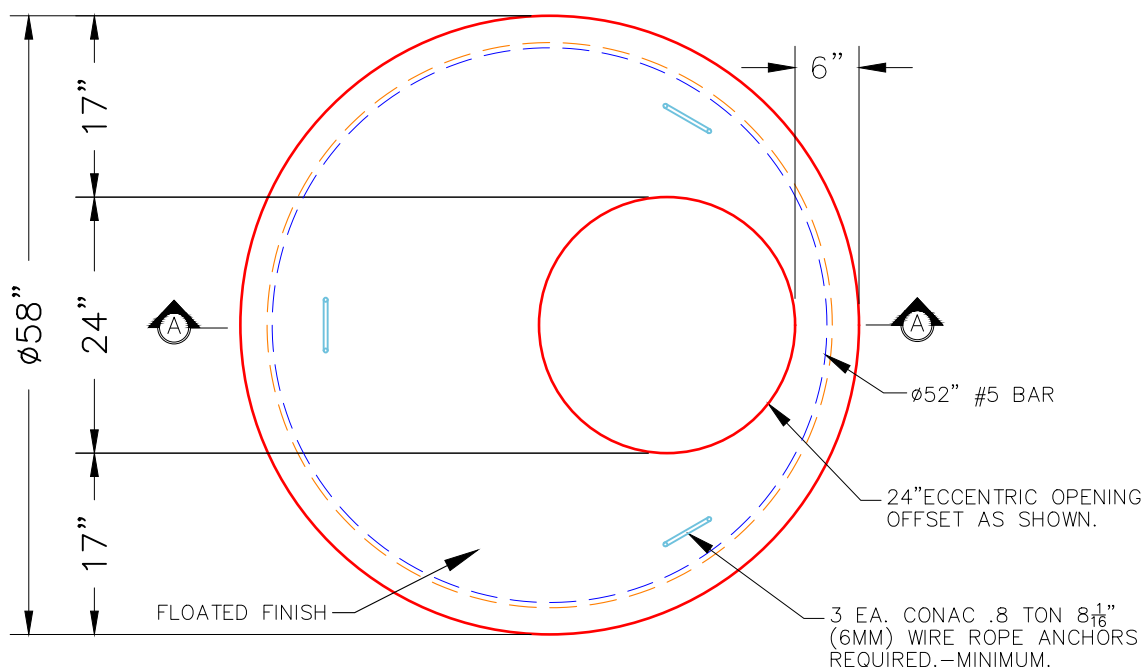

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 12"

Weight (Net): 1561 lb
Volume (Net): 0.42cu.yd
