

Job Name: 25-4508 - Georgetown Commons Target
Job Location: Georgetown, KY
Contractor: Winwater Hartford KY Co.

Plant: 100

5/28/2026 11:26:57 AM

Tech: Jared - F

PC: A. Chambers



Structure ID: 106 (28)

P2 MH072LD10-24X36RECT

MH FLAT TOP w/24"x36" Hole F/F



- P3) 24" x 36" - CASTING HEIGHT - 6"
P2) 72" - MH FLAT TOP w/24"x36" Hole F/F - 10"
P1) 72" - MH BASE Custom Ht F/n - 65"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 72" - Conseal CS-102 1.00"
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 38
1) Hole - 20
2) Hole - 30

0 lb
4149 lb
11640 lb
394 lb
0 lb
0 lb
0 lb
0 lb
0 lb
0 lb
Structure Total: 16184 lb

Structure Notes:

1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAST (HOE 470 SET LV (F/G/H)).

REINFORCING PER ASTM A615 (GRADE 60).
- TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W..
- RISER/WALLS (As .18)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.

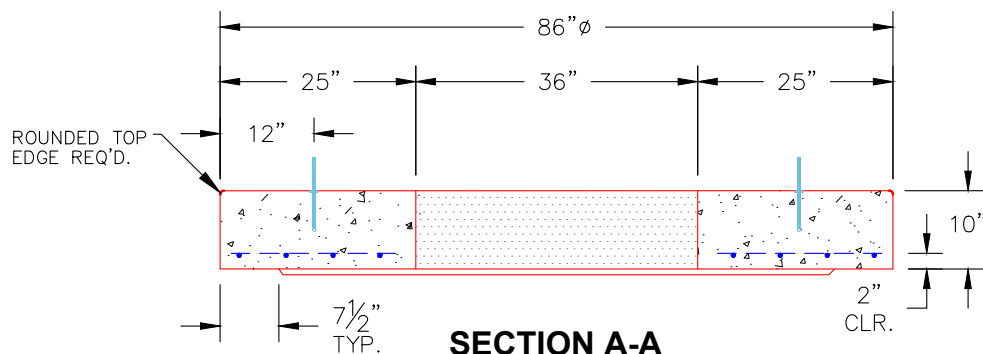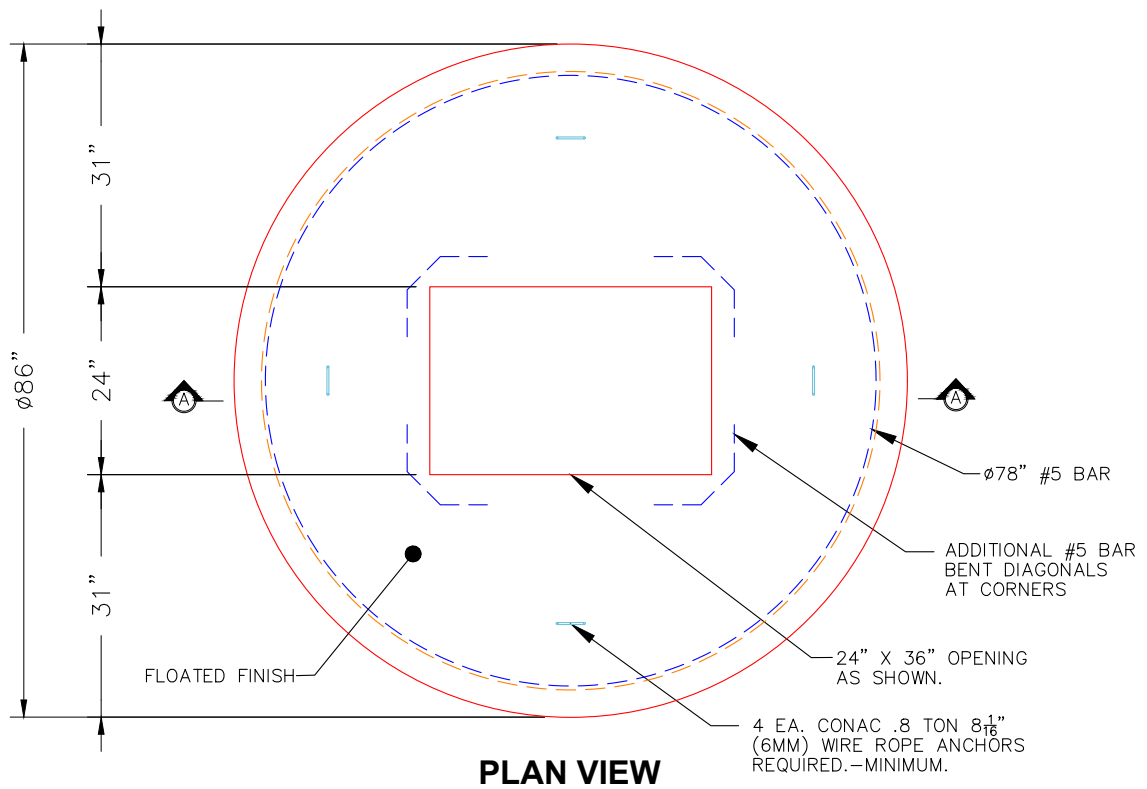

NOTES:

1. MANUFACTURED TO ASTM C-478 (LATEST REVISION).
2. CONCRETE: 4,000 PSI AT 28 DAYS.
3. REINFORCING: #5 BAR @ 6" O.C. E.W. (GRADE 60).

Coating (Int):
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 7"

Height (Ext): 10"

Weight (Net): 4149 lb
Volume (Net): 1.06cu.yd
