

Contractor: Winwater Hartford KY Co.

TECH: Jared - F

Plant: 100



Size: 36" x 36"

Rim to Invert: 2.68'

Floor Height: 8"

Slack: 0.41"


Structure Notes: 1. PER ASTM C913 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. NO STEPS AND NO INVERT CHANNEL.
4. CASTING BY ICAT (HOE 595 F/G).
REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:

P2) 36" x 36" - CASTING HEIGHT - 3"
P1) 36" x 36" - BOX BASE 8inW, 8inF - 30"
1) CASTING - HOE 595 F/G
1) 36" x 36" - Conseal CS-102 1.00"
1) Hole - 16

0 lb
5225 lb
376 lb
0 lb
0 lb



Structure Total: 5601 lb

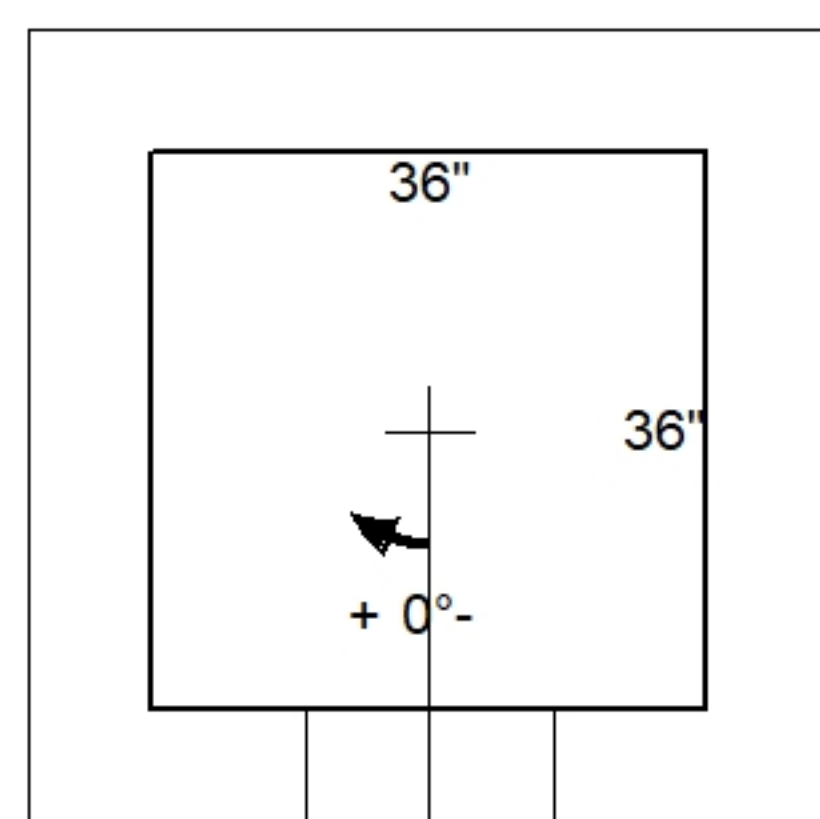

Invert: 1
Degree: 0°

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	870.93'							
Reducer								
Invert 1	868.25'	0°	12" HDPE	14.5"	16"	Hole 16	0"	P1
Invert 2								
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

Default - Interior Dimensions

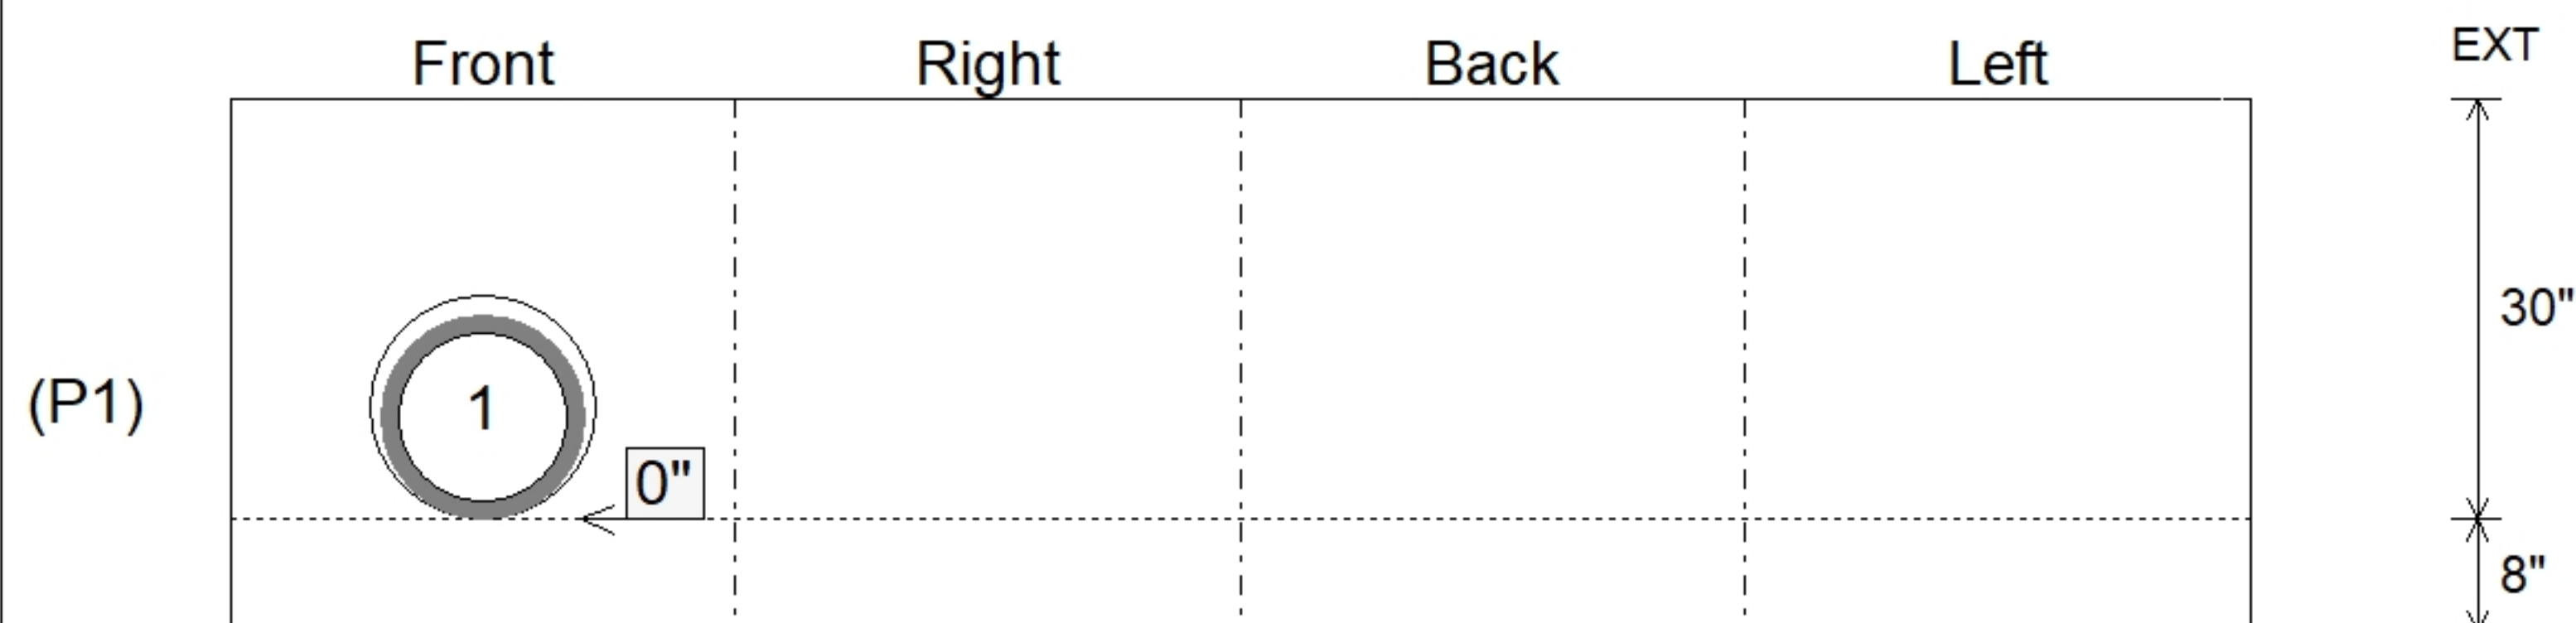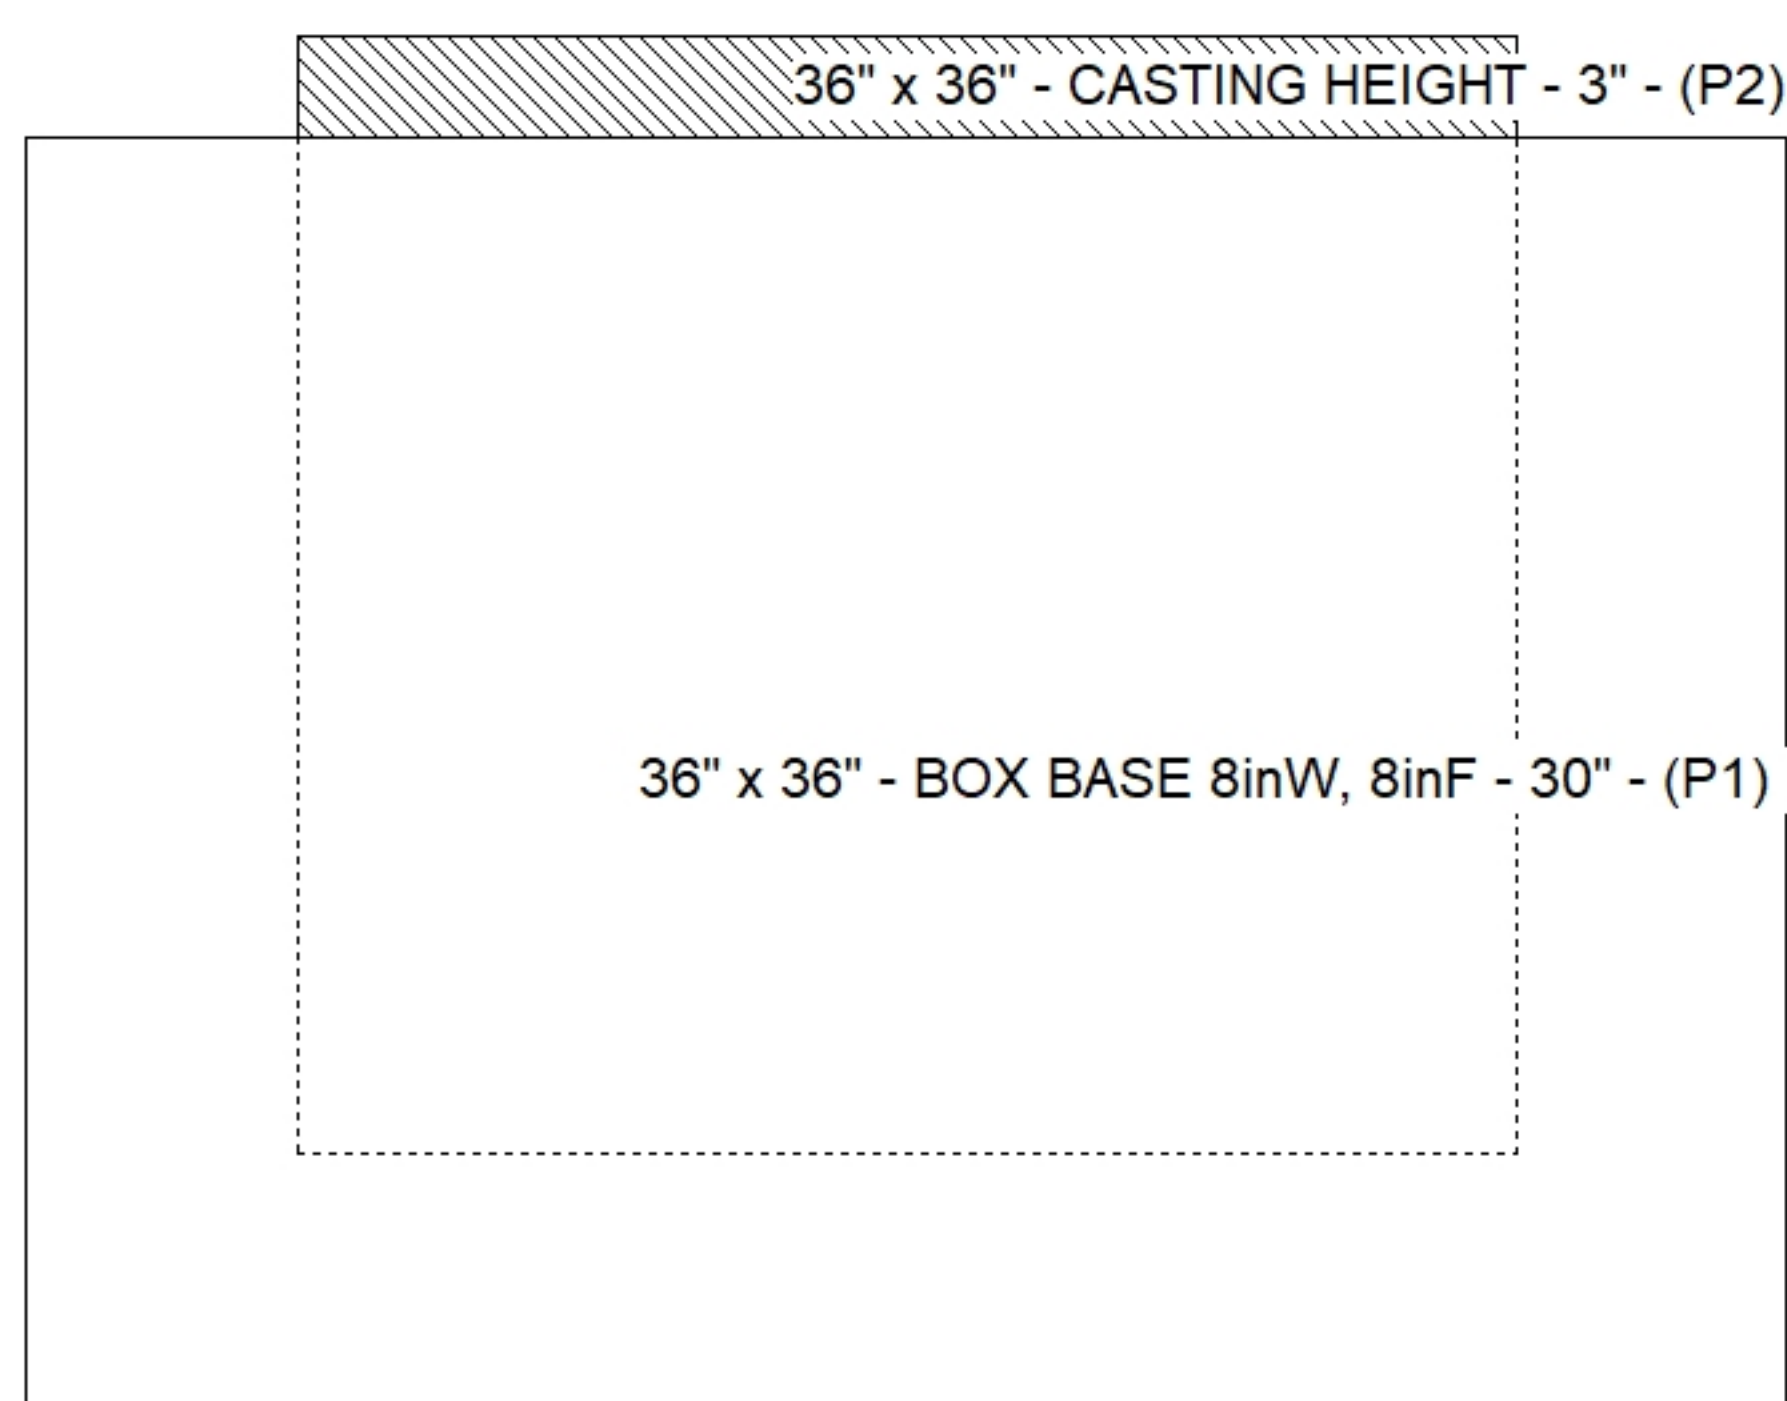

Submittal Drawing
6/1/2026 9:41:00 AM

SUBMITTAL
APPROVED BY:
