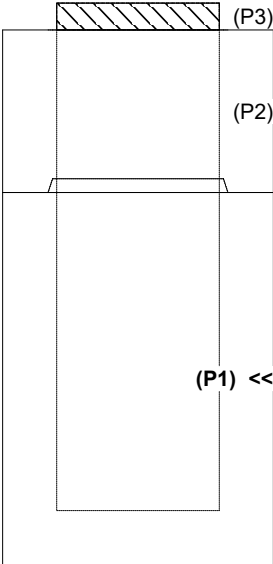


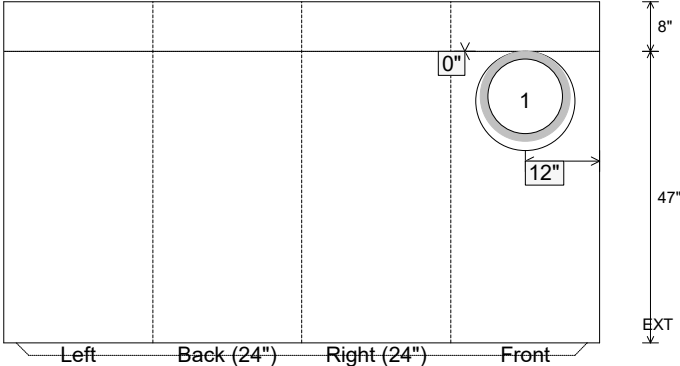


Job Name: 25-4508 - Georgetown Commons Target Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.				Plant: 100 5/28/2026 6:53:25 PM		Tech: Jared - F PC: A. Chambers					
Structure ID: 117 (34)											
P1 BX2424-08BAVF				BOX BASE 8inW, 8inF, Variable Ht T/n							
P3) 24" x 24" - CASTING HEIGHT - 4" P2) 24" x 24" - BOX RISER 8inW F/G - 24" P1) 24" x 24" - BOX BASE 8inW, 8inF, Variable Ht T/n - 47" 1) CASTING - HOE 280T F/G 2) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 16				0 lb 2062 lb 4978 lb 182 lb 0 lb 0 lb ----- Structure Total: 7222 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 280T F/G) REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.					
Rim: 874.6'				Rim to Invert: 6.2'		Slack: 0.65"		Sump: 1.25"		Step Position:	
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	868.4'	0°	20"	12" HDPE	14.5"	Hole 16	16"	16"	0"	0"	
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
				RIGHT-SIDE UP VIEW (int. dimensions)				UPSIDE-DOWN VIEW (int. dimensions)			
				 Invert: 1 Degree: 0° Horz: 12" Hole: 16" Up(): 0"				 Invert: 1 Degree: 0° Horz: 12" Hole: 16" Up(): 0"			
(P1) <<				INSIDE WALL DIMENSIONS							
				 Left Back (24") Right (24") Front EXT							
Coating (Int): Coating (Ext):				Seam Up: Tongue Seam Dn: n/a		Wall Thickness: 8" Floor Height: 8"		Height (Int): 47" Height (Ext): 55"		Weight (Net): 4978 lb Volume (Net): 1.27cu.yd	
