



Job Name: 25-4508 - Georgetown Commons Target Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.					Plant: 100 5/28/2026 11:25:33 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: 12 (15)											
P1 MH060BA66		MH BASE T/n									
P3) 24" x 36" - CASTING HEIGHT - 6" P2) 60" - MH FLAT TOP w/24"x36" Hole F/G - 13" P1) 60" - MH BASE T/n - 66" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 60" - Conseal CS-102 1.00" 1) 24" x 36" - Conseal CS-102 1.00" 2) Hole - 38						0 lb 3499 lb 8403 lb 394 lb 0 lb 0 lb 0 lb ----- Structure Total: 12296 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 470 SET LV (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 871'		Rim to Invert: 6.9'		Slack: 0.35"		Sump: 2.55"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	864.1'	0°	0"	30" HDPE	35.1"	Hole 38	38"	41.151"	0"	0"	
Invert 2	864.1'	180°	113.125"	30" HDPE	35.1"	Hole 38	38"	41.151"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

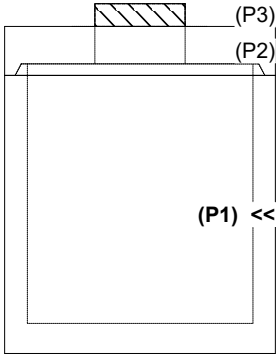


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

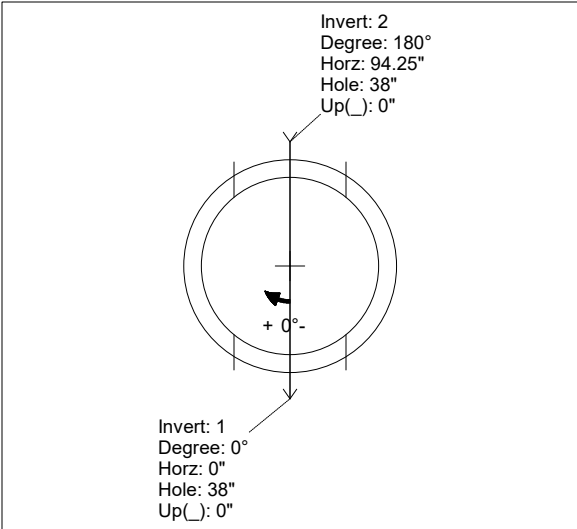

UPSIDE-DOWN VIEW (int. dimensions)

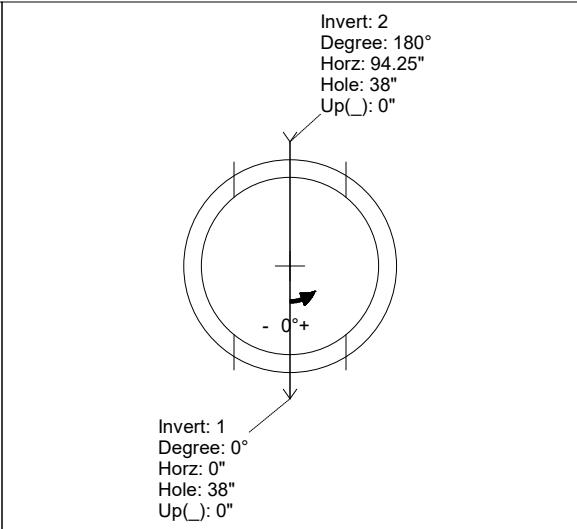

INSIDE WALL DIMENSIONS

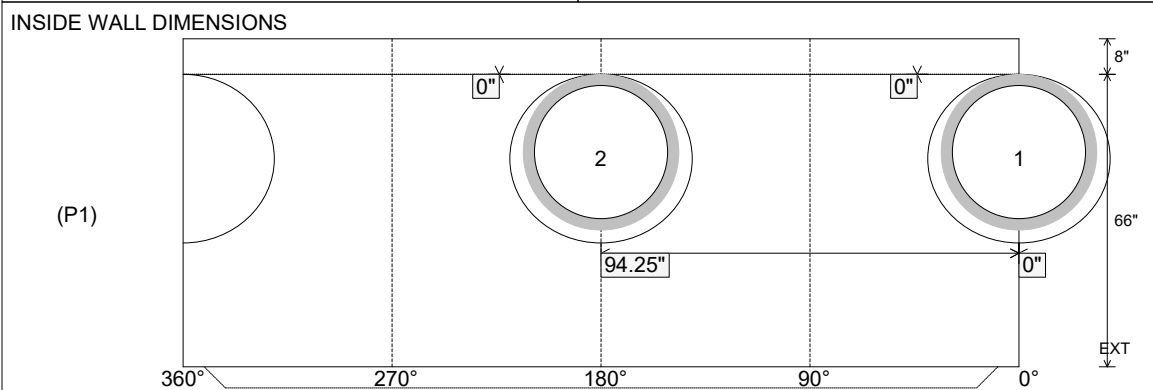

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 66" Height (Ext): 74"	Weight (Net): 8403 lb Volume (Net): 2.15cu.yd
----------------------------------	---------------------------------	--	--	--
