



Job Name: 25-4508 - Georgetown Commons Target Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.					Plant: 100 5/28/2026 11:25:34 AM		Tech: Jared - F PC: A. Chambers			
Structure ID: 14 (17)										
P1 MH060BA72		MH BASE T/n								
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING F/F - 4" P2) 60" - MH FLAT TOP w/ 24" ECC Hole F/G - 13" P1) 60" - MH BASE T/n - 72" 1) CASTING - HOE MC-375 F/C Storm 1) 60" - Conseal CS-102 1.00" 2) Hole - 38 1) Hole - 30 6) MH Step ML-10-TDS-NCR - 10"					0 lb 270 lb 2869 lb 8660 lb 271 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 12070 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE MC-375 F/C STORM). REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB (As .62) #5 BARS AT 6" C.C.E.W.. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.			
Rim: 871.55' Rim to Invert: 7.95' Slack: 1.95' Sump: 2.55' Step Position: 90°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	863.6'	0°	0"	30" HDPE	35.1"	Hole 38	38"	41.151"	0"	0"
Invert 2	863.6'	180°	113.125"	24" HDPE	27.8"	Hole 30	30"	31.416"	0.625"	0"
Invert 3	865.7'	245°	154"	30" HDPE	35.1"	Hole 38	38"	41.151"	25.25"	0"
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

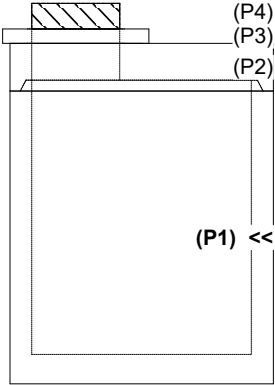

(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

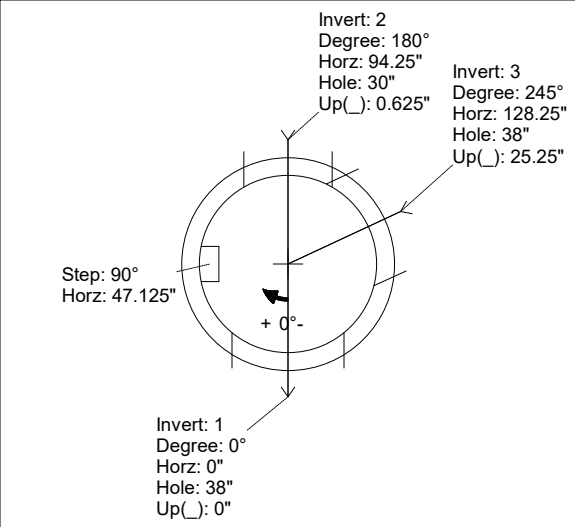

Invert: 2
Degree: 180°
Horz: 94.25"
Hole: 30"
Up(): 0.625"


Invert: 3
Degree: 245°
Horz: 128.25"
Hole: 38"
Up(): 25.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 38"
Up(): 0"

Step: 90°
Horz: 47.125"

+ 0°-

UPSIDE-DOWN VIEW (int. dimensions)

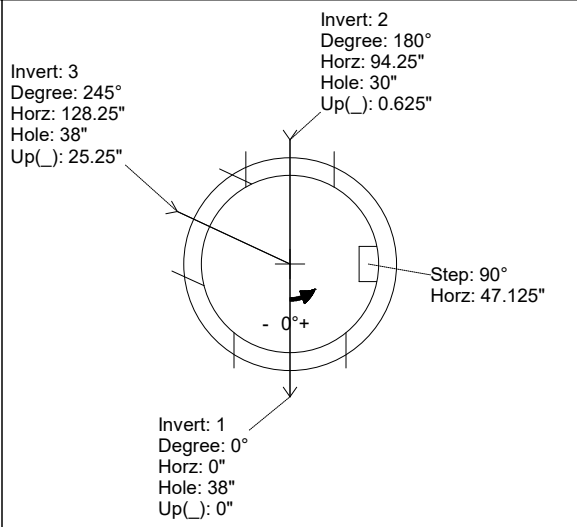

Invert: 2
Degree: 180°
Horz: 94.25"
Hole: 30"
Up(): 0.625"


Invert: 3
Degree: 245°
Horz: 128.25"
Hole: 38"
Up(): 25.25"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 38"
Up(): 0"

Step: 90°
Horz: 47.125"

- 0°+

INSIDE WALL DIMENSIONS

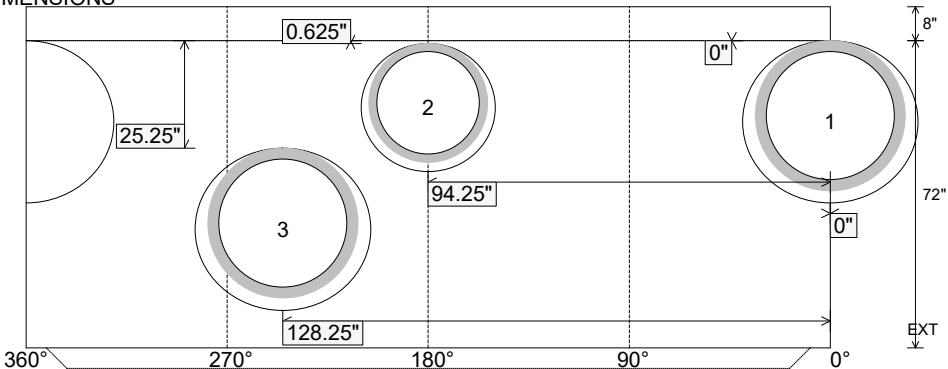

0.625"

25.25"

94.25"

128.25"

8"

72"

EXT

360° 270° 180° 90° 0°

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 6" Floor Height: 8"	Height (Int): 72" Height (Ext): 80"	Weight (Net): 8660 lb Volume (Net): 2.21cu.yd
----------------------------------	---------------------------------	--	--	--
