




Job Name: 25-4508 - Georgetown Commons Target Job Location: Georgetown, KY Contractor: Winwater Hartford KY Co.					Plant: 100 5/28/2026 11:25:35 AM		Tech: Jared - F PC: A. Chambers				
Structure ID: 17 (20)											
P1 BX2436-08BA30			BOX BASE 8inW, 8inF F/n								
P2) 24" x 36" - CASTING HEIGHT - 6" P1) 24" x 36" - BOX BASE 8inW, 8inF F/n - 30" 1) CASTING - HOE 470 SET LV (F/G/H) 1) 24" x 36" - Conseal CS-102 1.00" 1) Hole - 20 1) Hole - 16					0 lb 4112 lb 394 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 4506 lb		Structure Notes: 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. NO STEPS AND NO INVERT CHANNEL. 4. CASTING BY ICAST (HOE 470 SET LV (F/G/H)). REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .12) #5 BARS AT 12" C.C.E.W. - FLOOR (As .12) #5 BARS AT 12" C.C.E.W.				
Rim: 870.85' Rim to Invert: 2.95' Slack: 0.65' Sump: 1.25' Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	867.9'	0°	20"	15" HDPE	17.6"	Hole 20	20"	20"	0"	0"	
Invert 2	867.9'	270°	26"	12" HDPE	14.5"	Hole 16	16"	16"	0"	0"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

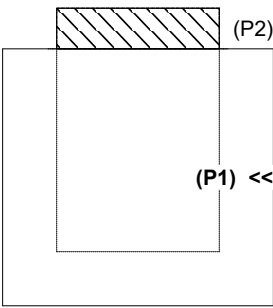

RIGHT-SIDE UP VIEW (int. dimensions)

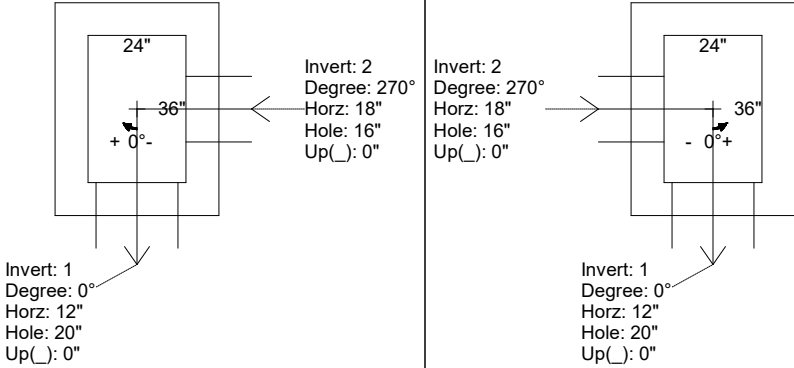

UPSIDE-DOWN VIEW (int. dimensions)

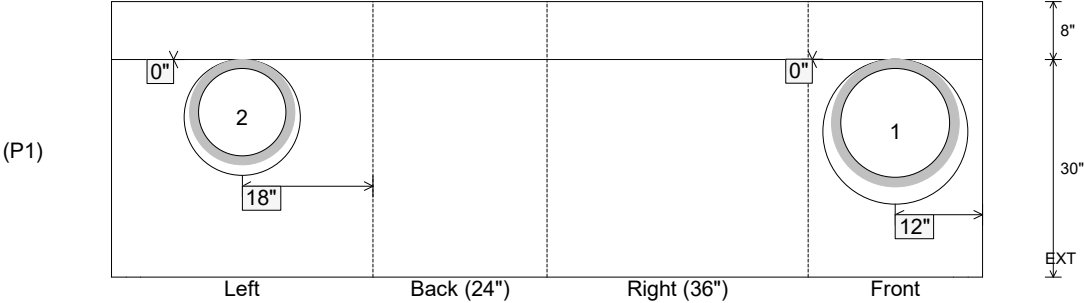

INSIDE WALL DIMENSIONS

Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 30" Height (Ext): 38"	Weight (Net): 4112 lb Volume (Net): 1.05cu.yd
----------------------------------	-------------------------------	--	--	--
