

**Contractor: Winwater Hartford KY Co.**

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 2.95'

Floor Height: 8"


Slack: 0.65"

STRUCTURE SUMMARY:


P2) 24" x 36" - CASTING HEIGHT - 6"  
P1) 24" x 36" - BOX BASE 8inW, 8inF - 30"  
1) CASTING - HOE 470 SET LV (F/G/H)  
1) 24" x 36" - Conseal CS-102 1.00"  
1) Hole - 20  
1) Hole - 16

0 lb  
4112 lb  
394 lb  
0 lb  
0 lb  
0 lb


Structure Total: 4506 lb

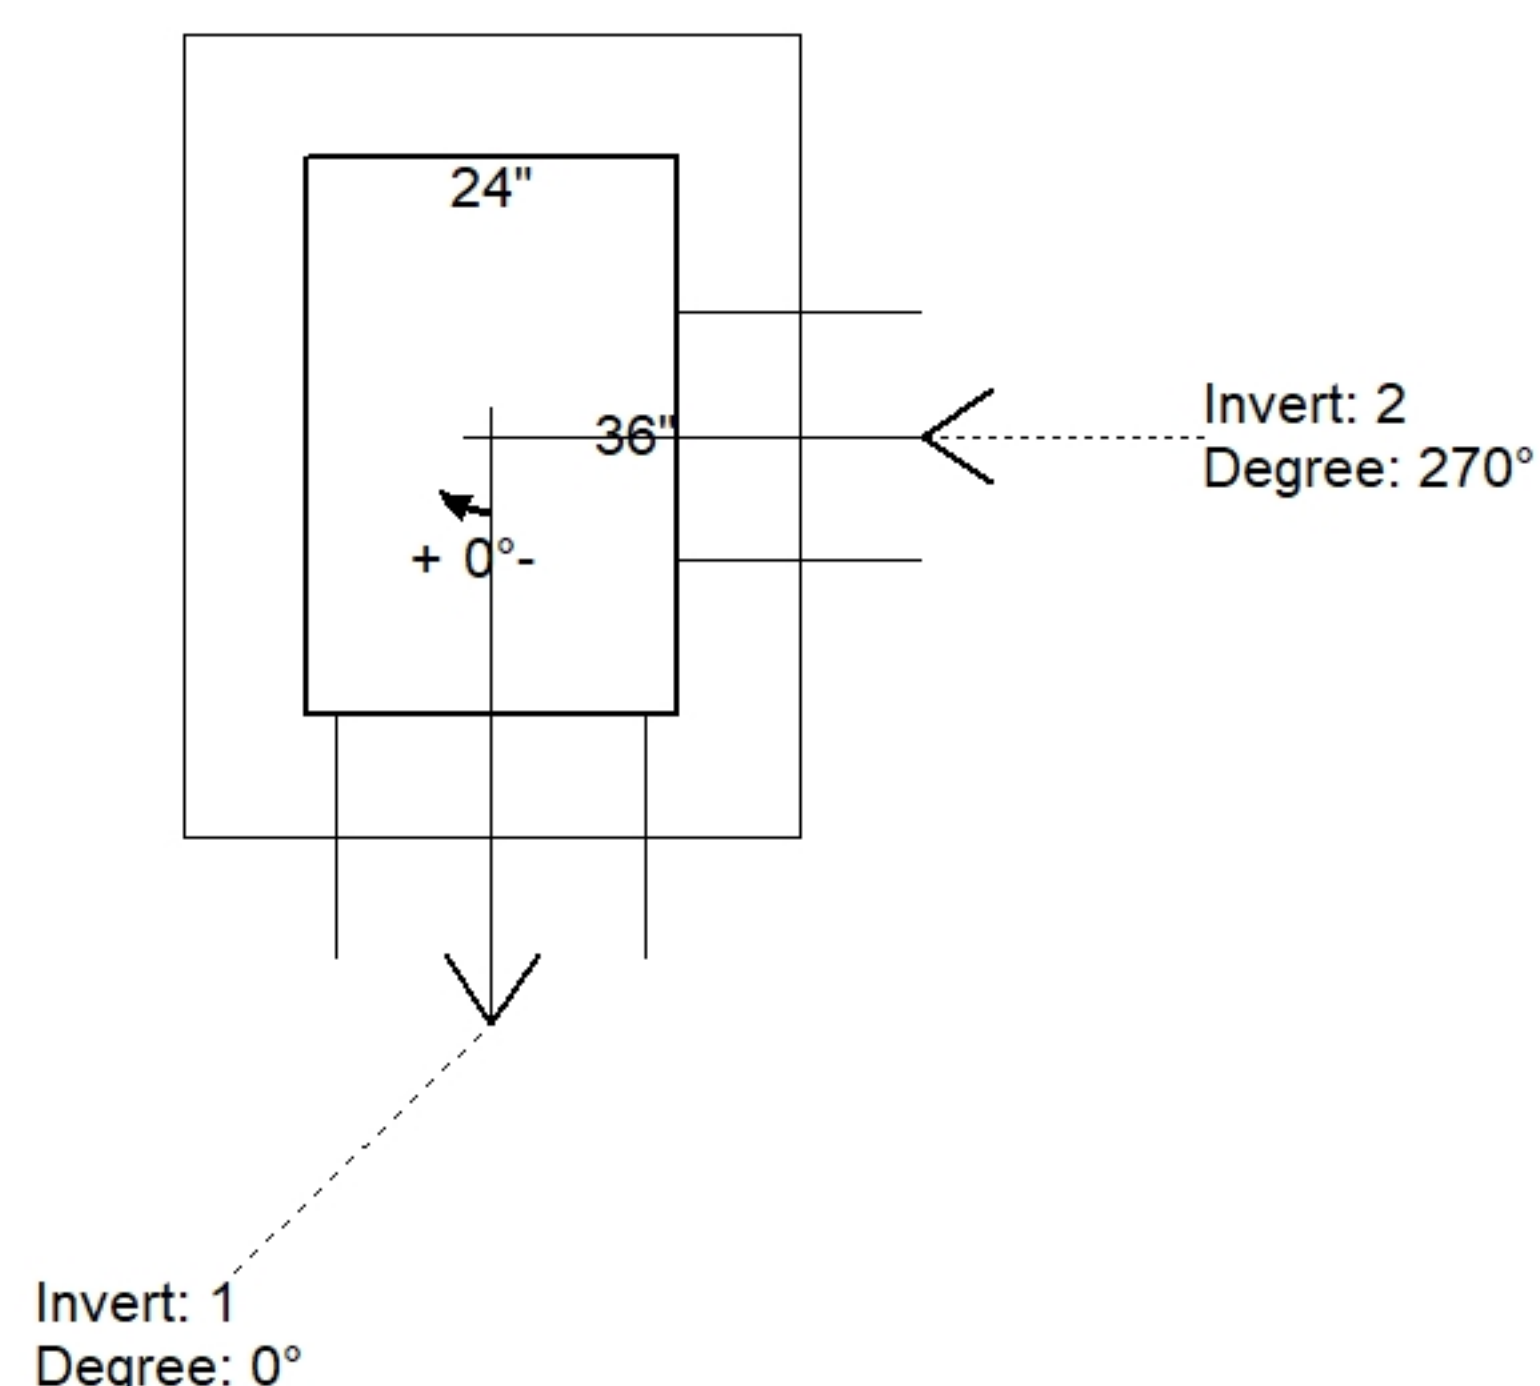

| Position | Elev    | Angle | Pipe     | Pipe OD | Hole | Connector | Up ( ) | Ref |
|----------|---------|-------|----------|---------|------|-----------|--------|-----|
| Rim      | 870.85' |       |          |         |      |           |        |     |
| Reducer  |         |       |          |         |      |           |        |     |
| Invert 1 | 867.9'  | 0°    | 15" HDPE | 17.6"   | 20"  | Hole 20   | -0.05" | P1  |
| Invert 2 | 867.9'  | 270°  | 12" HDPE | 14.5"   | 16"  | Hole 16   | 0"     | P1  |
| Invert 3 |         |       |          |         |      |           |        |     |
| Invert 4 |         |       |          |         |      |           |        |     |
| Invert 5 |         |       |          |         |      |           |        |     |
| Invert 6 |         |       |          |         |      |           |        |     |
| Invert 7 |         |       |          |         |      |           |        |     |
| Invert 8 |         |       |          |         |      |           |        |     |

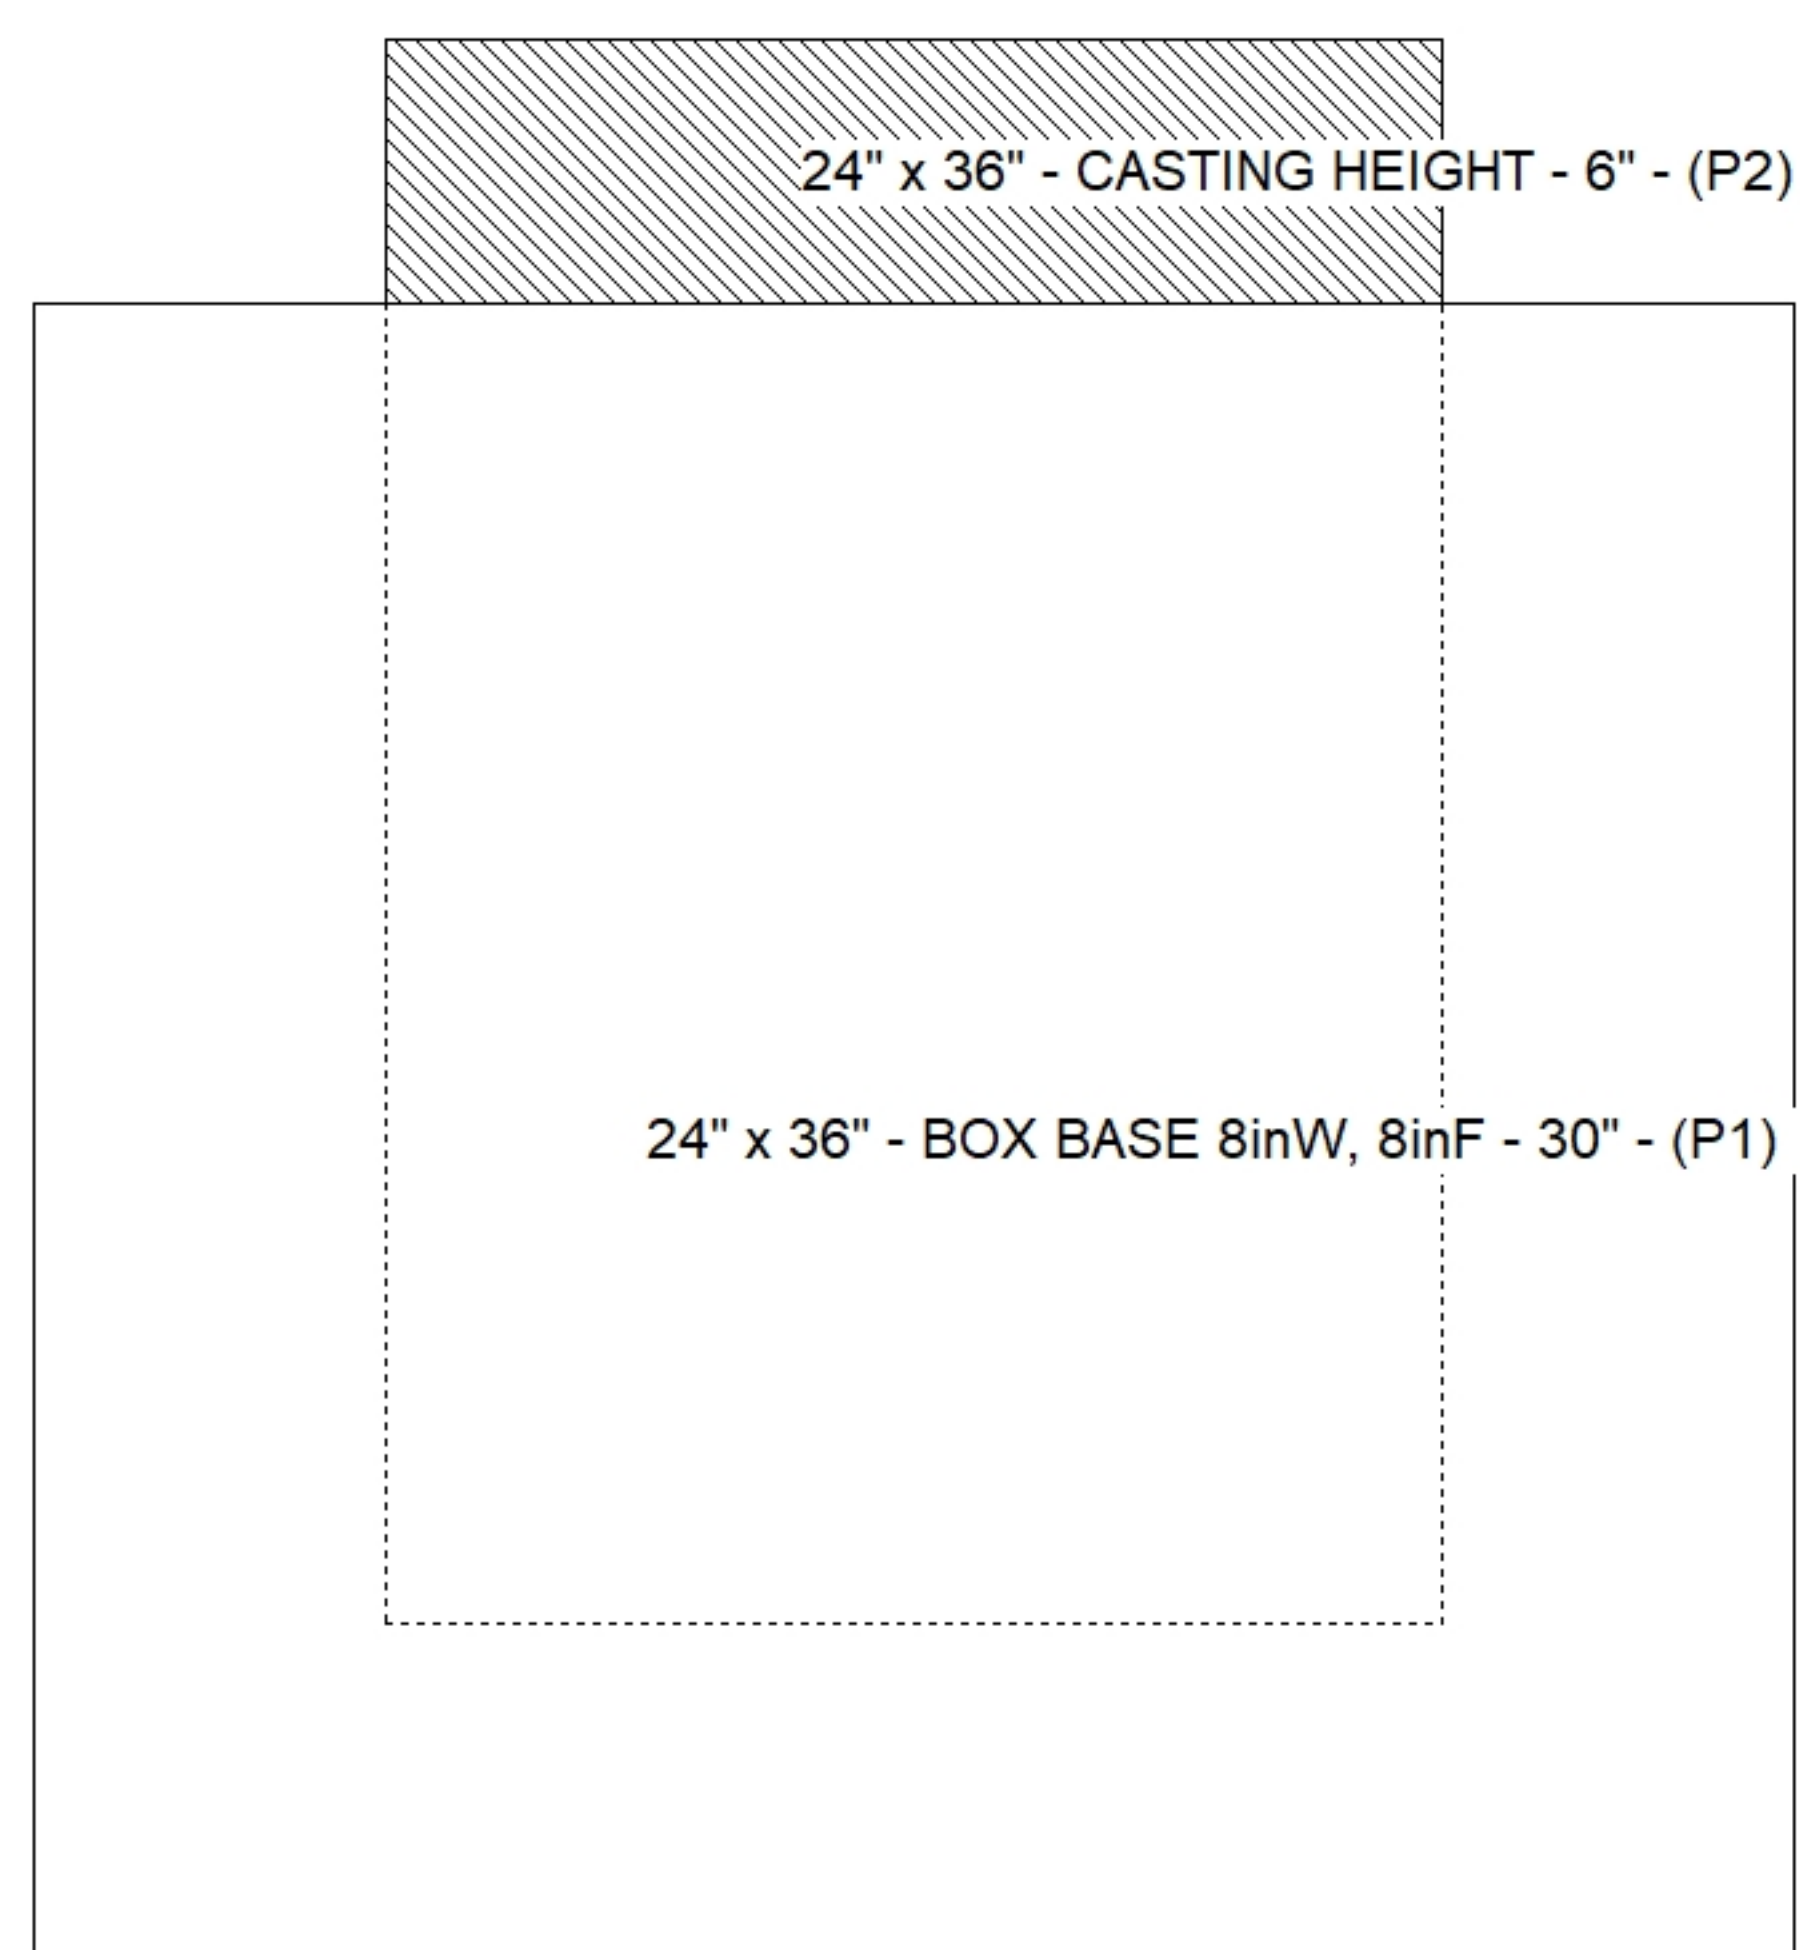

### Default - Interior Dimensions

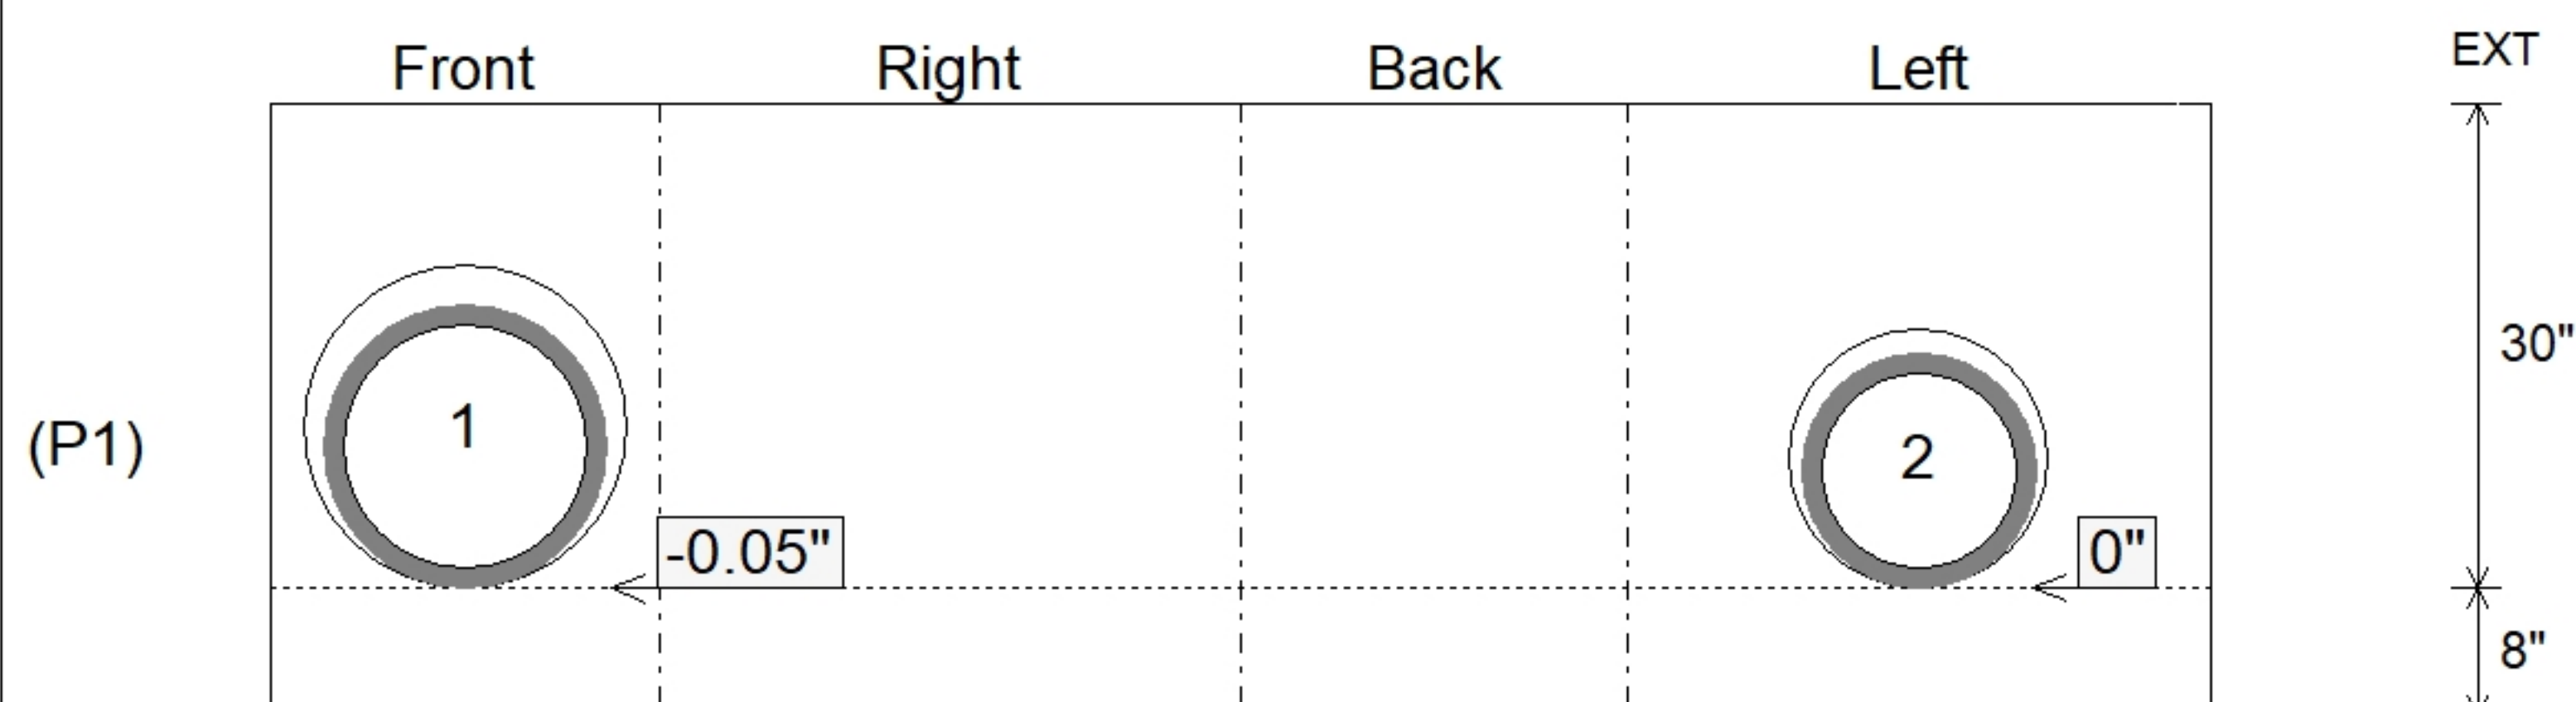

Submittal Drawing  
6/1/2026 9:40:57 AM

SUBMITTAL  
APPROVED BY:
