

Contractor: Winwater Hartford KY Co.

TECH: Jared - F

Plant: 100



Size: 24" x 36"

Rim to Invert: 3'

Floor Height: 8"


Slack: 0.25"

REINFORCING PER ASTM A615 (GRADE 60).
- WALLS (As .12) #5 BARS AT 12" C.C.E.W.
- FLOOR (As .12) #5 BARS AT 12" C.C.E.W.

P2) 24" x 36" - CASTING HEIGHT - 6"
P1) 24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31"
1) CASTING - HOE 470 SET LV (F/G/H)
1) 24" x 36" - Conseal CS-102 1.00"
1) Hole - 20
1) Hole - 16

0 lb
4158 lb
394 lb
0 lb
0 lb
0 lb

Structure Total: 4552 lb

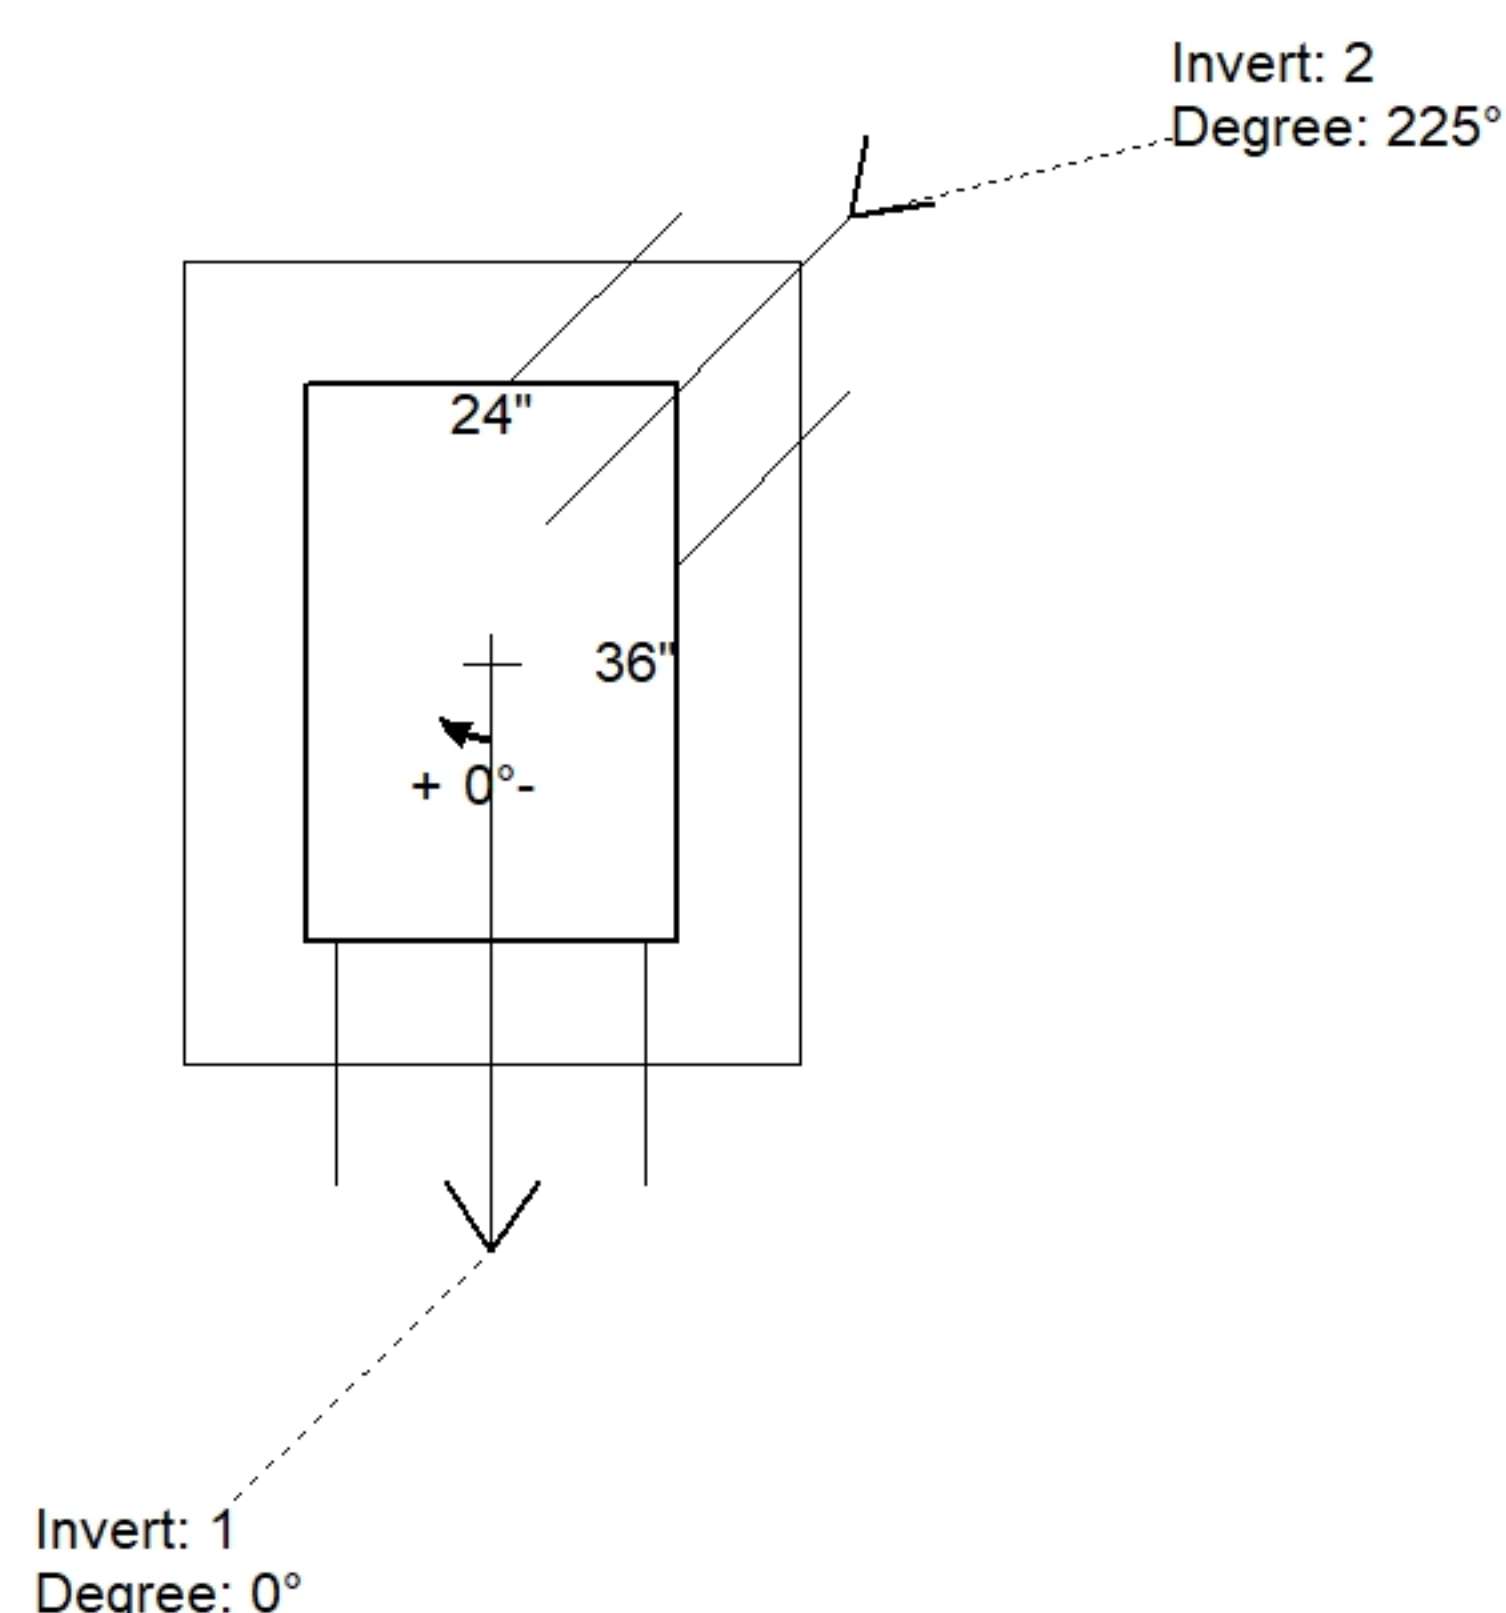


Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	870.75'							
Reducer								
Invert 1	867.75'	0°	15" HDPE	17.6"	20"	Hole 20	-0.05"	P1
Invert 2	867.75'	225°	12" HDPE	14.5"	16"	Hole 16	0"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

24" x 36" - CASTING HEIGHT - 6" - (P2)

24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31" - (P1)

The diagram illustrates a casting mold assembly. It features a rectangular casting area at the top, shaded with diagonal lines, labeled "24" x 36" - CASTING HEIGHT - 6" - (P2)". Below this is a larger rectangular area, outlined with a dashed border, labeled "24" x 36" - BOX BASE 8inW, 8inF, Variable Ht - 31" - (P1)". The entire assembly is contained within a larger rectangular frame.

Default - Interior Dimensions

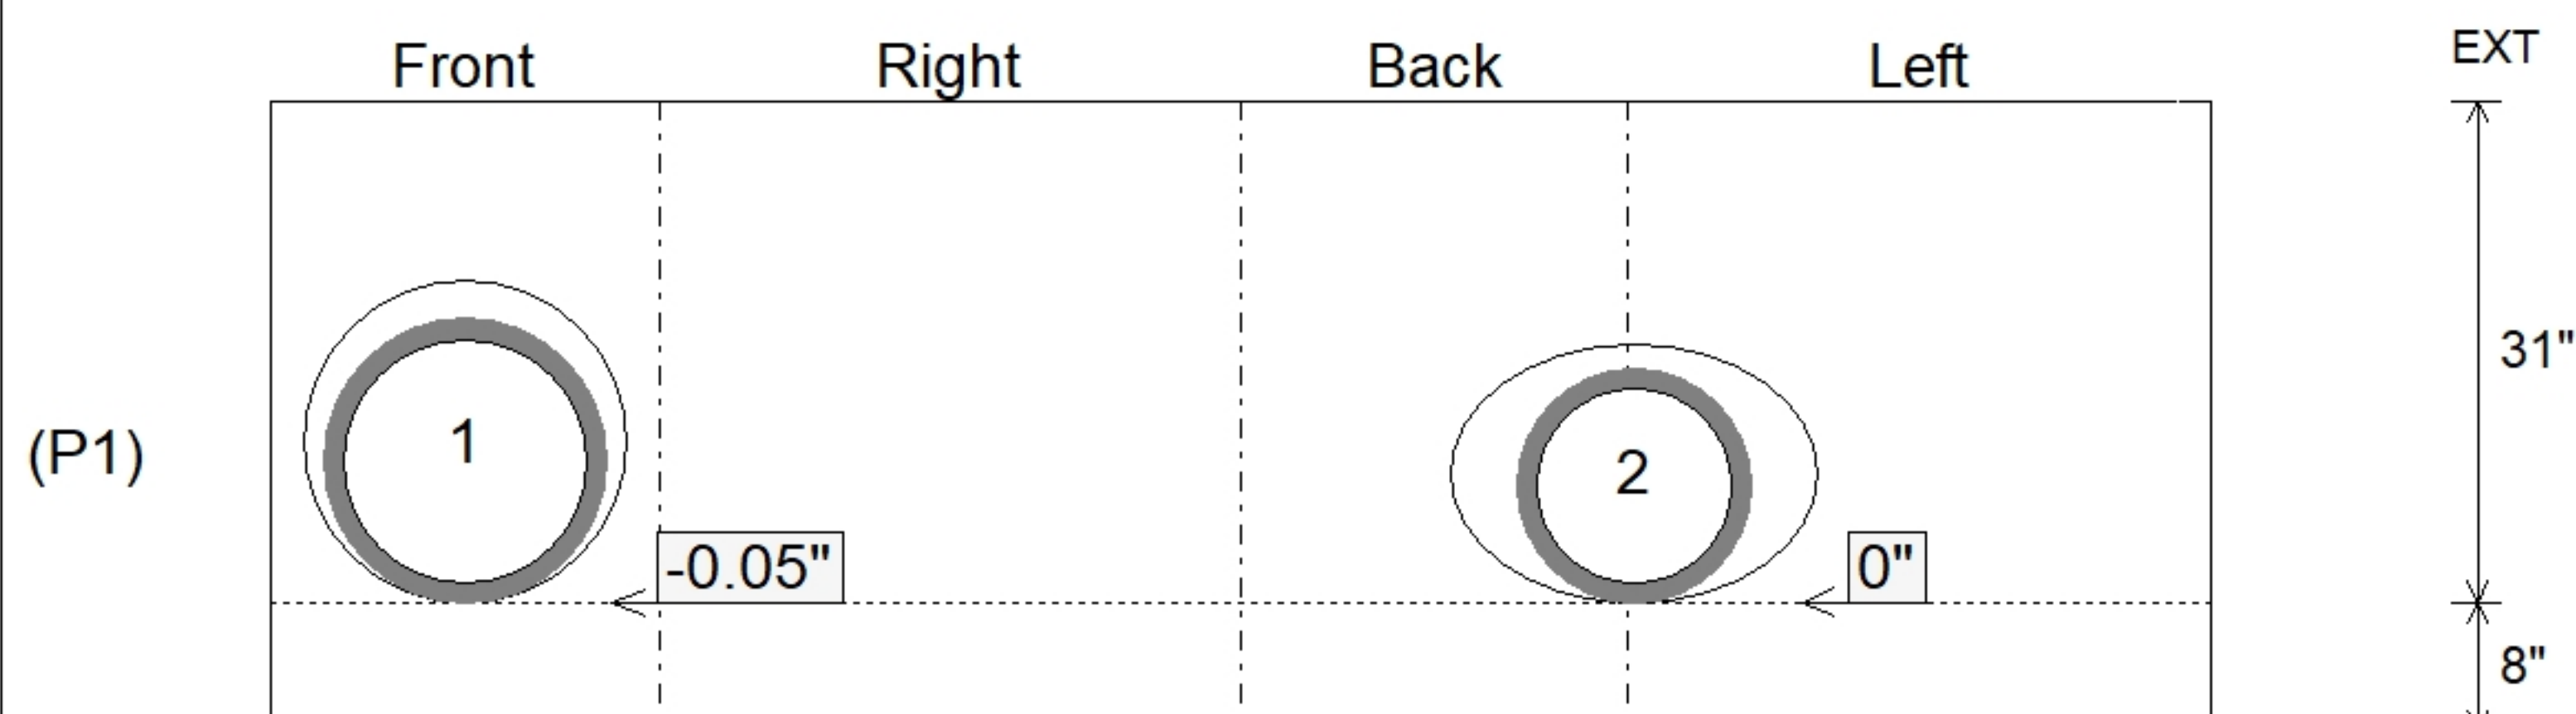

Submittal Drawing
6/1/2026 9:40:51 AM

SUBMITTAL
APPROVED BY:
