

Job Name: 25-4514 - 828940 Towneplace Suites
 Job Location: Shepherdsville, KY
 Contractor: Contech Engineering Solutions

Plant: Beaver Dam

12/1/2025 8:34:33 AM

Tech: J. Coppage

PC: T. Sekula



Structure ID: 10-CDS2015-4-C

P1 MH048BA24

MH BASE

- P5) 30" - CASTING HEIGHT - 4"
- P4) 48" - MH FLAT LID w/30in ECC Hole - 12"
- P3) 48" - MH RISER SPECIAL - 12"
- P2) 48" - MH RISER SPECIAL - 66"
- P1) 48" - MH BASE - 24"
- 1) PSASSEMBLY
- 1) CVSTENCILING
- 1) SEPARATION SLAB - *
- 3) 48" - Conseal CS-102 1.00"
- 2) Hole - 12

0 lb
 1413 lb
 838 lb
 4515 lb
 3007 lb
 0 lb
 0 lb
 1474 lb
 0 lb
 0 lb

 Structure Total: 11247 lb



Structure Notes:
 (4" Tall Casting By Others)
 Lifting Hooks To Be Installed
 On The Outside Of The Structure
 Contech's Logo As Well As
 The Inlets And Outlet Must Be
 Stenciled Onto The Structure
 ICAST To Install The Internals

Rim: 449' Rim to Invert: 4.55' Slack: 0.8" Sump: 64.2" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (L)	Offset
Invert 1										
Invert 2										
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

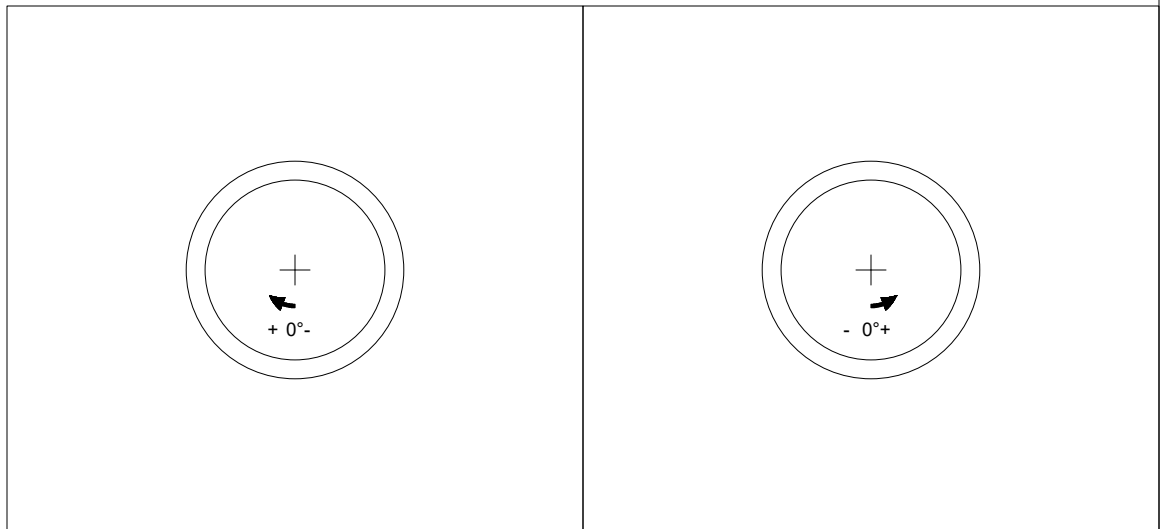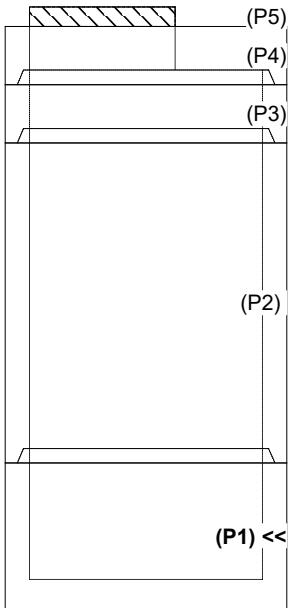

INSIDE WALL DIMENSIONS



Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 24" Height (Ext): 30"	Weight (Net): 3007 lb Volume (Net): 0.77cu.yd
----------------------------------	---------------------------------	----------------------------------------	----------------------------------------	--------------------------------------------------
