

Contractor: Pace Contracting, LLC

TECH: Jared - F

Plant: 100



Spec: Sanitary
Type: SAN.MH
Size: 84"

Rim: 442'
Invert: 431'
Rim to Invert: 11'

Sump: 3"
Floor (Top): 430.75'
Floor Height: 8"

Floor (Bot): 430.083'
Overall Height: 11.917'
Slack: 0"


REINFORCING PER ASTM A615 (GRADE 60).

- TOP SLAB (As .31) #5 BARS AT 6" C.C.E.W.
- RISER/WALLS (As .12)
- FLOOR (As .37) #5 BARS AT 10" C.C.E.W.


- P4) 24" - CASTING HEIGHT - 7"
- P3) 84" - MH FLAT TOP w/24" ECC Hole - 17"
- P2) 84" - MH RISER Custom Ht - 15"
- P1) 84" - MH BASE - 96"
- 1) Chimney Seal - Cretek Chimney Seal
- 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
- 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
- 1) 84" - MH INVERT CHANNEL - FULL HEIGHT
- 1) CASTING - HOE MC-375-WT F/C Sanitary
- 2) 84" - Conseal CS-102 1.00" (Double)
- 1) 24" - Conseal CS-102 1.00" (Double)
- 2) Kor-N-Seal2 - S206-42
- 8) MH Step ML-10-TDS-NCR - 10"

0 lb
7959 lb
2910 lb
21965 lb
10 lb
0 lb
0 lb
5422 lb
271 lb
0 lb
0 lb
13 lb
0 lb


Structure Total: 38550 lb

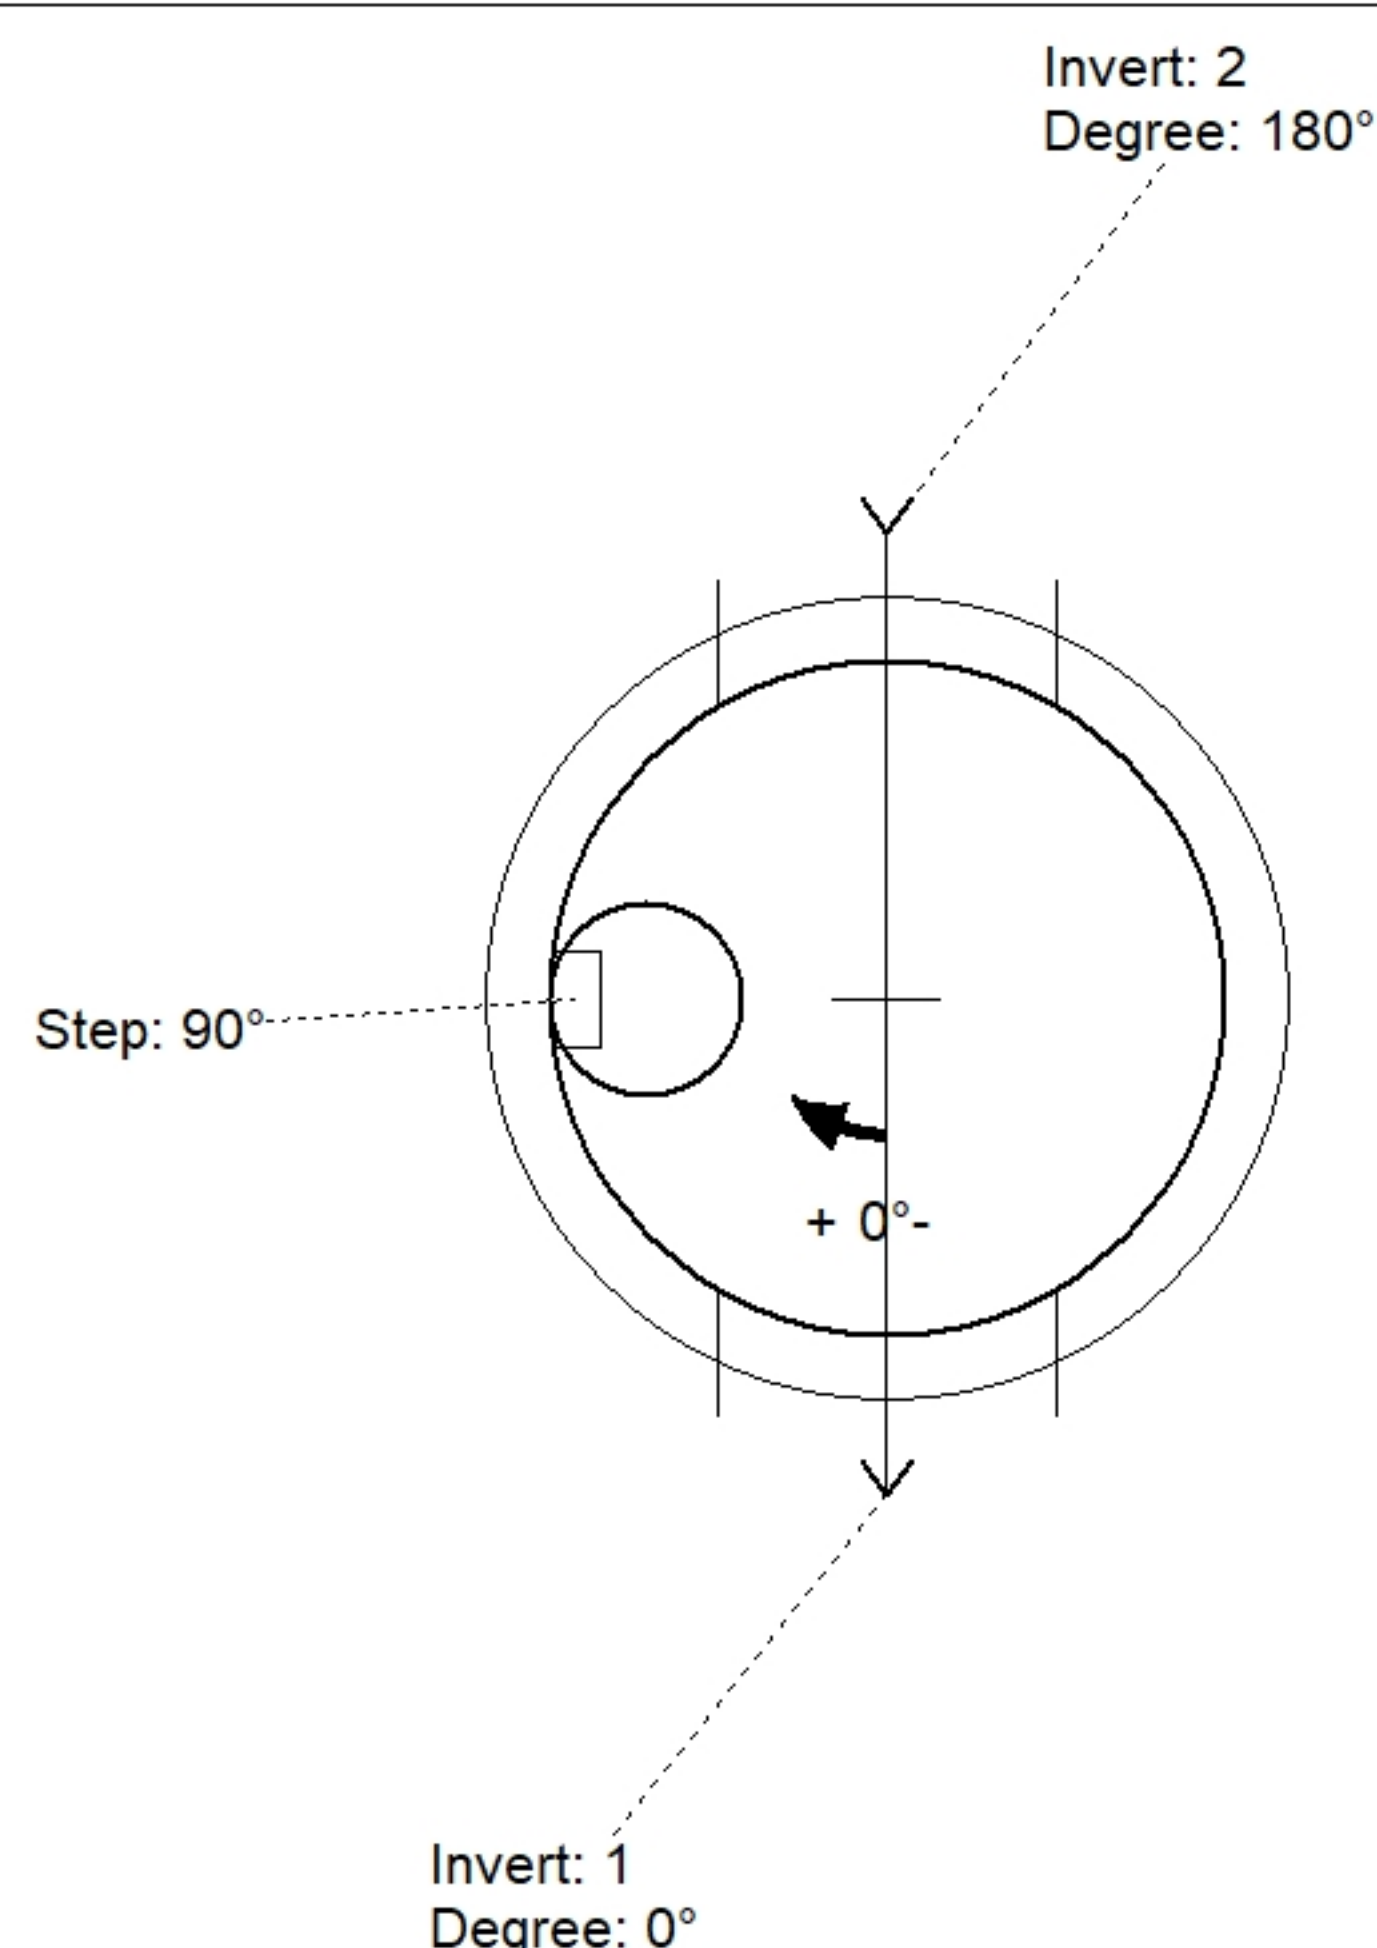

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	442'							
Reducer								
Invert 1	431'	0°	36" DI	38.5"	42"	Kor-N-Seal2 S206-42	0"	P1
Invert 2	435.08'	180°	36" DI	38.5"	42"	Kor-N-Seal2 S206-42	48.96"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

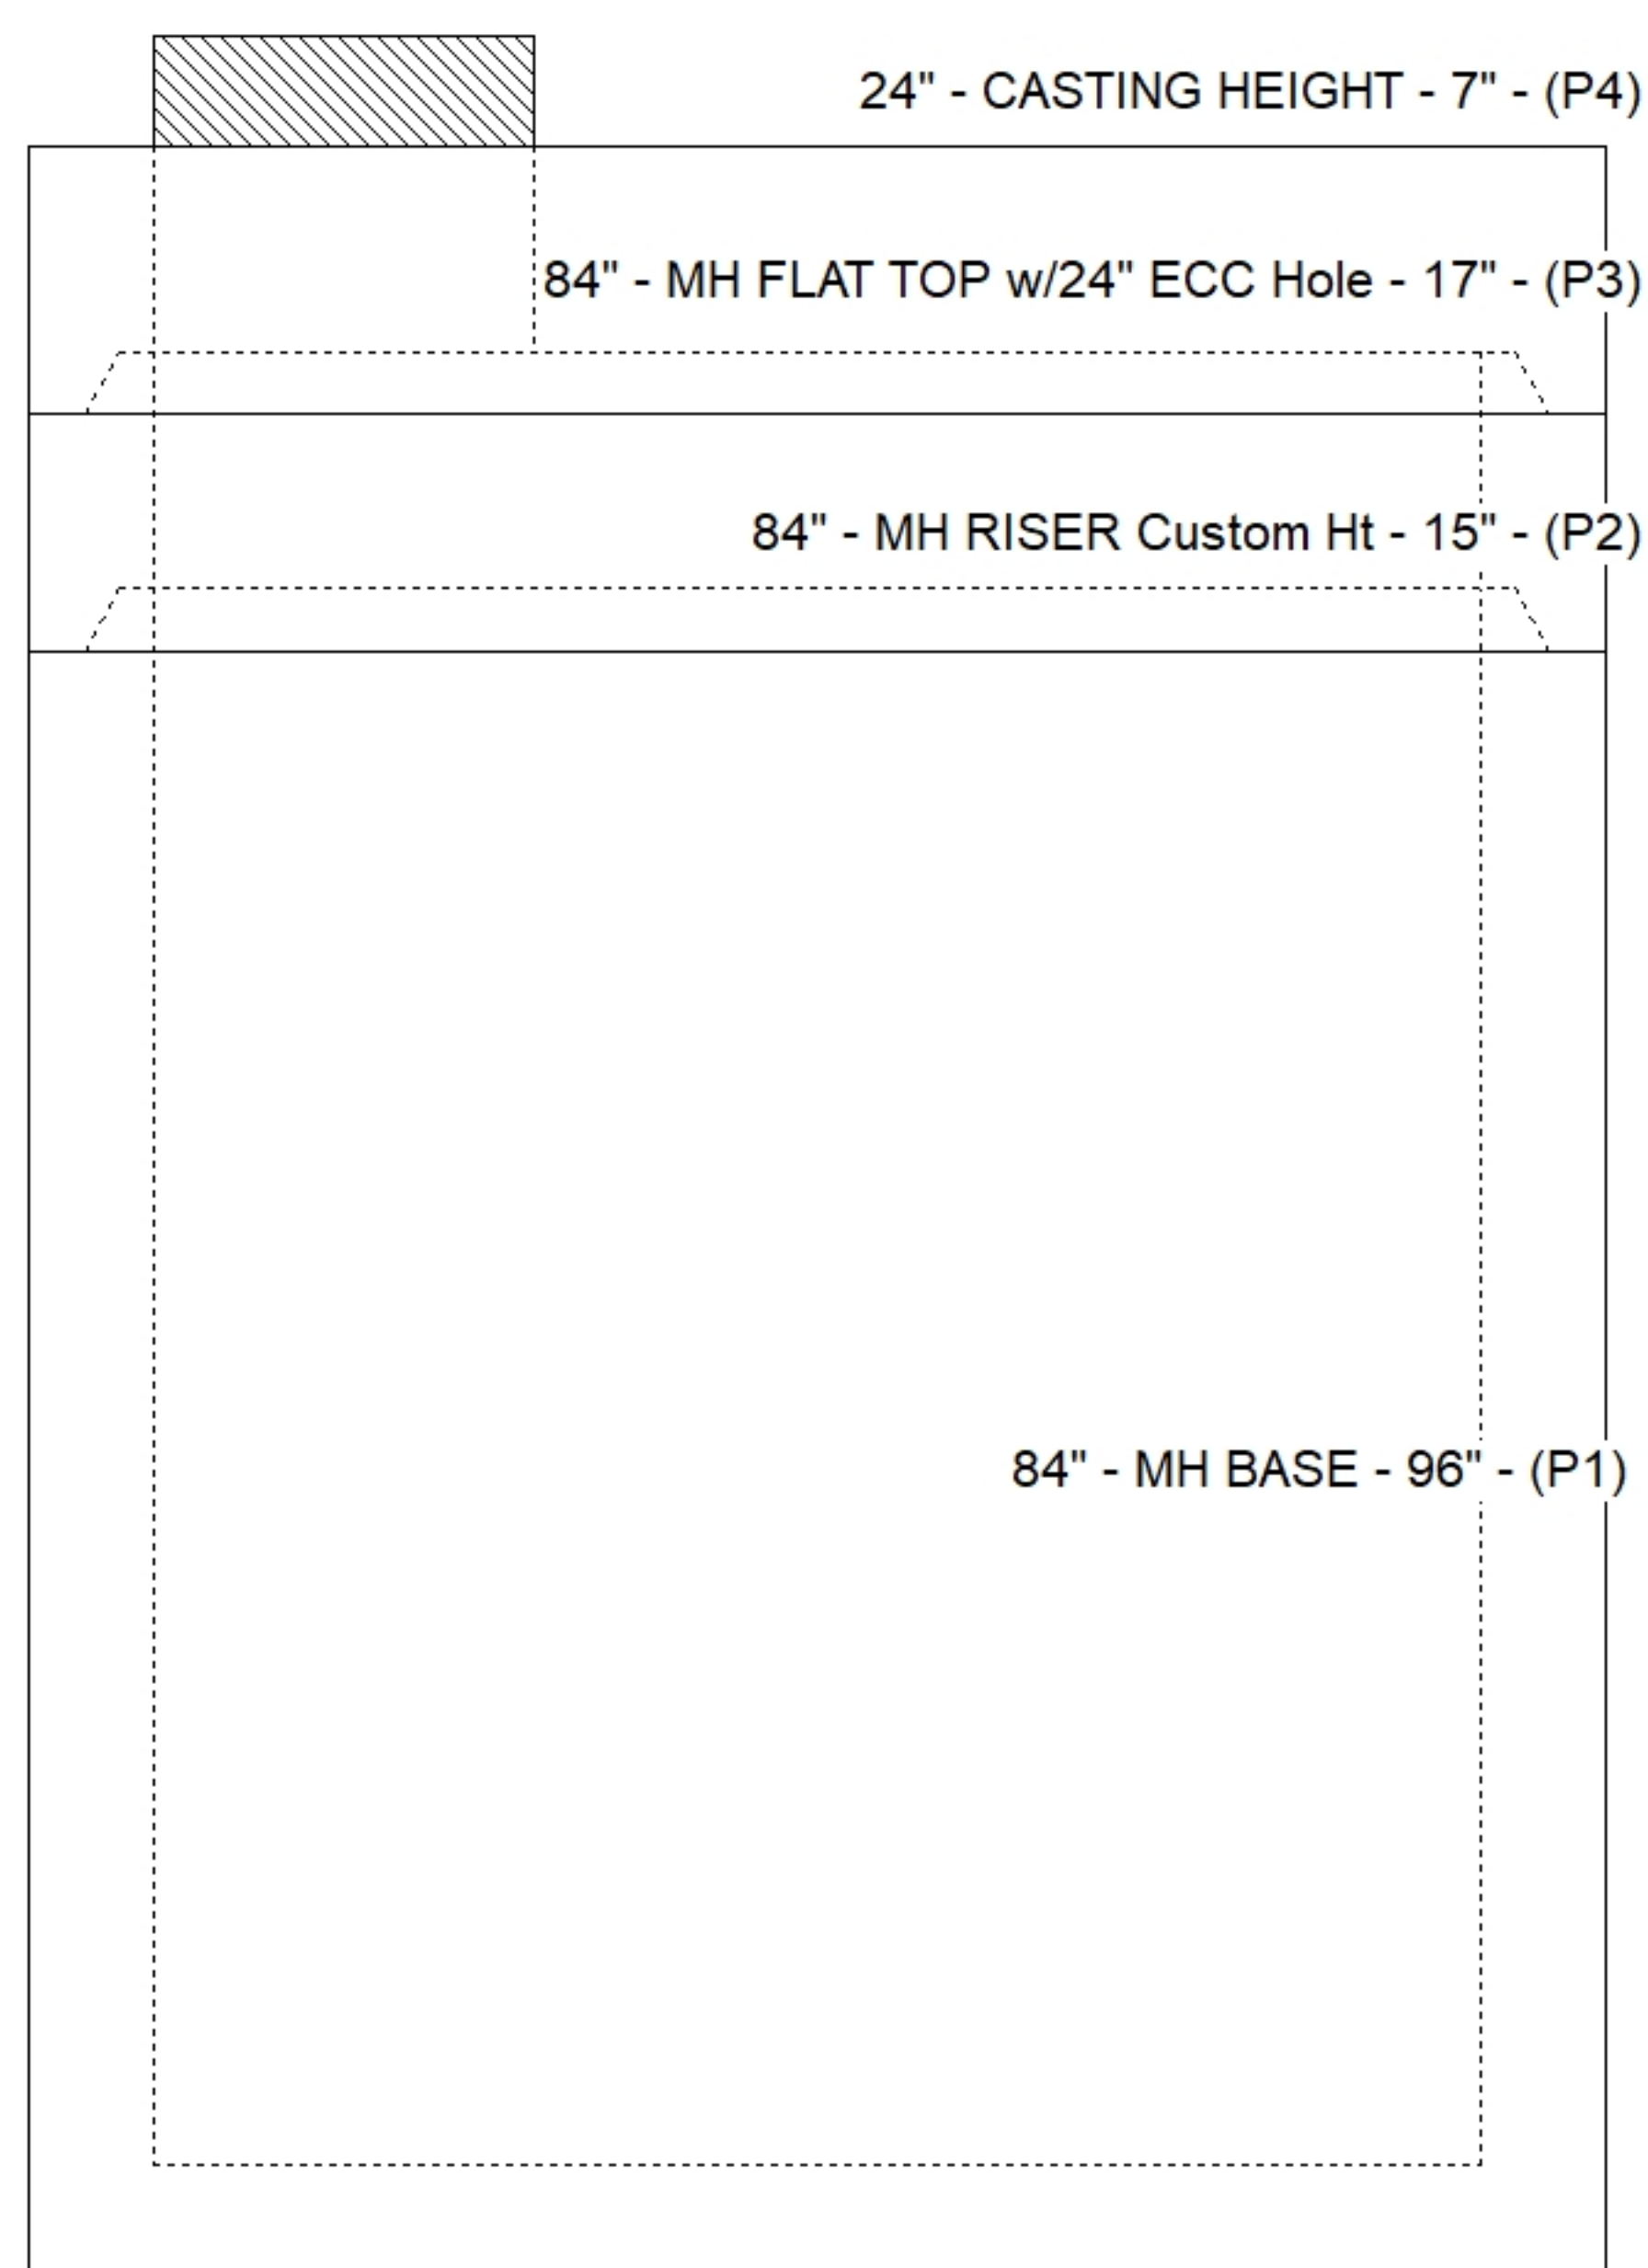

Default - Interior Dimensions

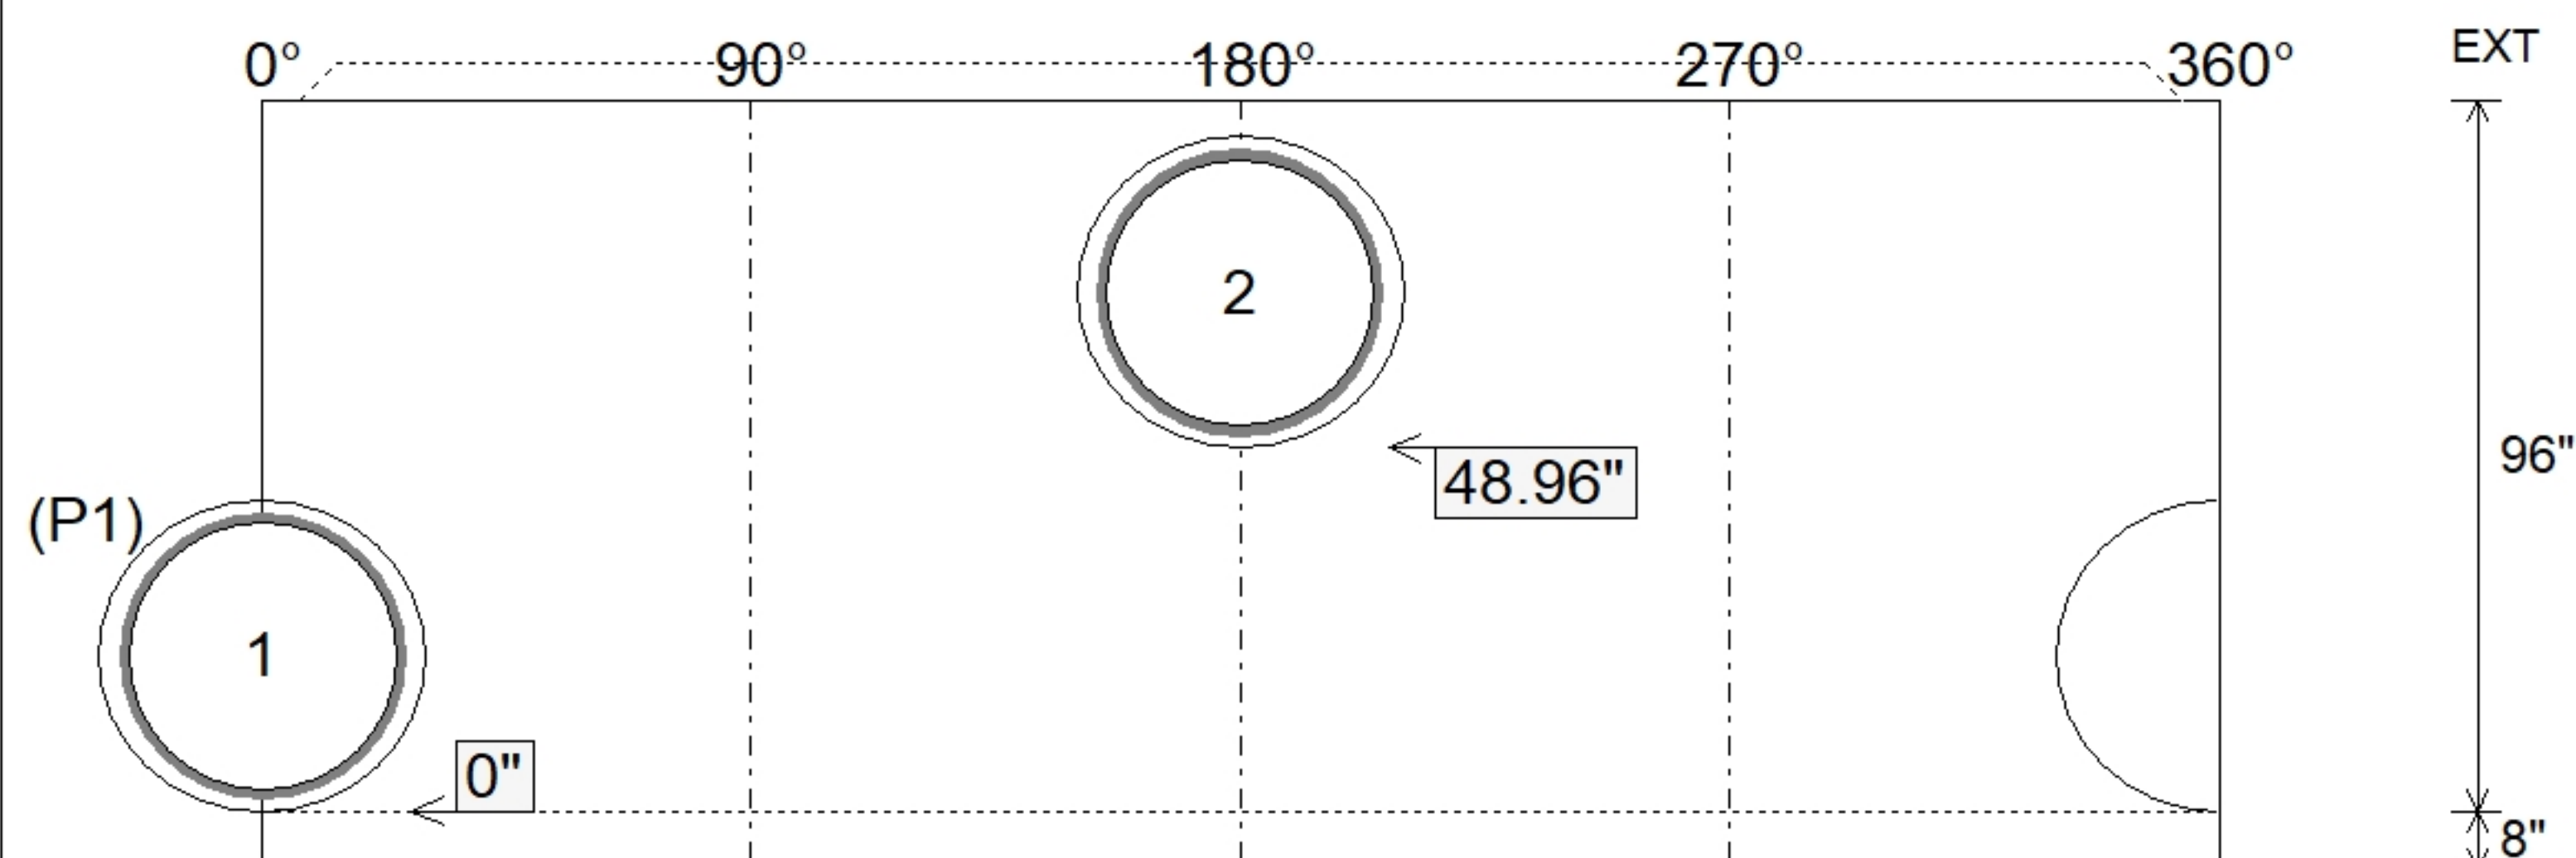

Submittal Drawing
6/8/2026 10:33:43 AM

SUBMITTAL
APPROVED BY:
