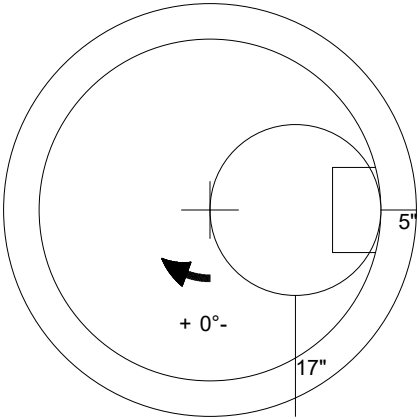



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion		Plant: 100	Tech: Jared - F	
Job Location: Shepherdsville, KY		6/4/2026 1:36:59 PM	PC: J Jarvis	
Contractor: Pace Contracting, LLC				
Structure ID: MH-2				
P4 MH048CN42		ECC CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 42" P3) 60" - MH Transition Slab 48" Hole T/G - 13" P2) 60" - MH RISER Custom Ht T/G - 55" P1) 60" - MH BASE T/h - 24" 1) Chimney Seal - Cretex Chimney Seal 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 2) 60" - Conseal CS-102 1.00" (Double) 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 3) PSX - 12M NYLO 6) MH Step ML-10-TDS-NCR - 10" 0 lb 3200 lb 1928 lb 5742 lb 5067 lb 10 lb 0 lb 0 lb 2692 lb 271 lb 0 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 18933 lb Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375 F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - TRANS. SLAB (As .31) #5 BARS AT 6" C.C.E.W. - RISER/WALLS (As .18) - FLOOR (As .37) #5 BARS AT 10" C.C.E.W.				
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 42"	Weight (Net): 3200 lb Volume (Net): 0.5cu.yd
