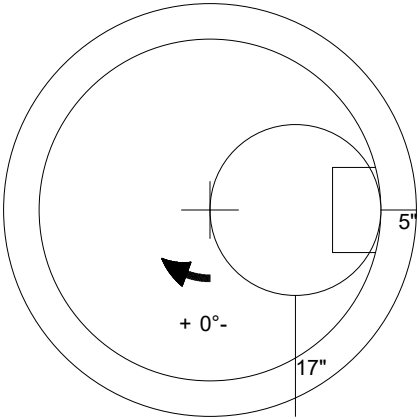



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC		Plant: 100 5/29/2026 3:22:00 PM	Tech: Jared - F PC: J Jarvis		
Structure ID: MH-3					
P3 MH048CN30		ECC CONE w/ 24" HOLE F/G			
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE Custom Ht T/n - 28" 1) Chimney Seal - Cretex Chimney Seal 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375-WT F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 1) PSX - 16Y NYLO 1) PSX - 12M NYLO 8) MH Step ML-10-TDS-NCR - 10"		0 lb 2050 lb 3353 lb 3153 lb 10 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 8 lb 8 lb 0 lb ----- Structure Total: 10293 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375-WT F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
					
 48" - ECC CONE w/ 24" HOLE F/G - 30" - (P3)					
Coating (Int): Coating (Ext):		Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
