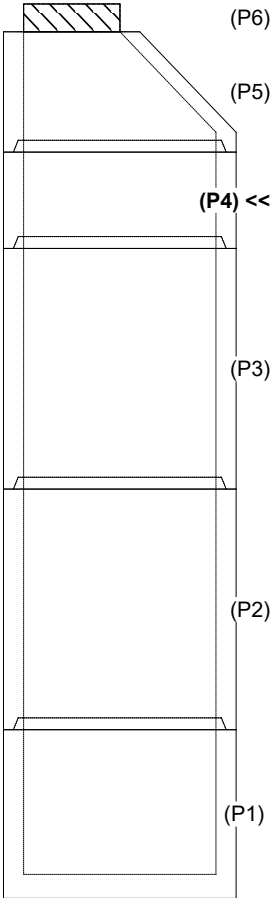
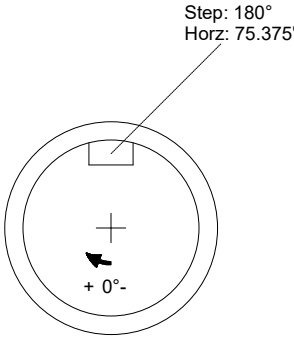



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion Job Location: Shepherdsville, KY Contractor: Pace Contracting, LLC					Plant: 100 5/29/2026 3:22:44 PM		Tech: Jared - F PC: J Jarvis				
Structure ID: MH-39-052											
P4		MH048RS24		MH RISER T/G							
P6) 24" - CASTING HEIGHT - 7" P5) 48" - ECC CONE w/ 24" HOLE F/G - 30" P4) 48" - MH RISER T/G - 24" P3) 48" - MH RISER T/G - 60" P2) 48" - MH RISER T/G - 60" P1) 48" - MH BASE T/n - 36" 1) Chimney Seal - Cretex Chimney Seal 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-375 F/C Sanitary 4) 48" - Conseal CS-102 1.00" (Double) 2) Kor-N-Seal2 - S206-22 16) MH Step ML-10-TDS-NCR - 10"					0 lb 2050 lb 1677 lb 4192 lb 4192 lb 3516 lb 10 lb 0 lb 0 lb 1440 lb 271 lb 0 lb 13 lb 0 lb ----- Structure Total: 17359 lb		Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375 F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 433.28'		Rim to Invert: 18.15'		Slack: 2.8"		Sump: 2"		Step Position: 180°			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1											
Invert 2											
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions)											
											
INSIDE WALL DIMENSIONS											
											
Coating (Int): Coating (Ext):			Seam Up: Tongue Seam Dn: Groove		Wall Thickness: 5" Floor Height: 0"		Height (Int): 24" Height (Ext): 24"		Weight (Net): 1677 lb Volume (Net): 0.43cu.yd		
