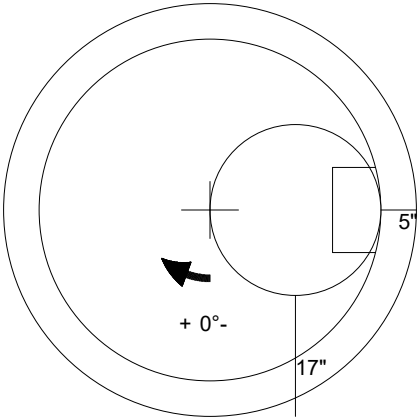



Job Name: 25-4547 - WWTP Improvements & Hydraulic Expansion		Plant: 100	Tech: Jared - F	
Job Location: Shepherdsville, KY		5/29/2026 3:22:01 PM	PC: J Jarvis	
Contractor: Pace Contracting, LLC				
Structure ID: MH-6				
P2 MH048CN24		ECC CONE w/ 24" HOLE F/G		
P3) 24" - CASTING HEIGHT - 7" P2) 48" - ECC CONE w/ 24" HOLE F/G - 24" P1) 48" - MH BASE T/n - 24" 1) Chimney Seal - Cretex Chimney Seal 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) CASTING - HOE MC-375-WT F/C Sanitary 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12M NYLO 2) PSX - 12-06 NYLO 1) PSX - 8QRS-S NYLO 3) MH Step ML-10-TDS-NCR - 10"		0 lb 1550 lb 2842 lb 10 lb 1440 lb 0 lb 0 lb 271 lb 0 lb 0 lb 8 lb 16 lb 6 lb 0 lb ----- Structure Total: 6144 lb	Structure Notes: . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING SUPPLIED BY I-CAST (HOE MC-375-WT F/C SANITARY). 4. 8.5" EXTERNAL CHIMNEY SEAL BY I-CAST. . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As.12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1550 lb Volume (Net): 0.33cu.yd
