

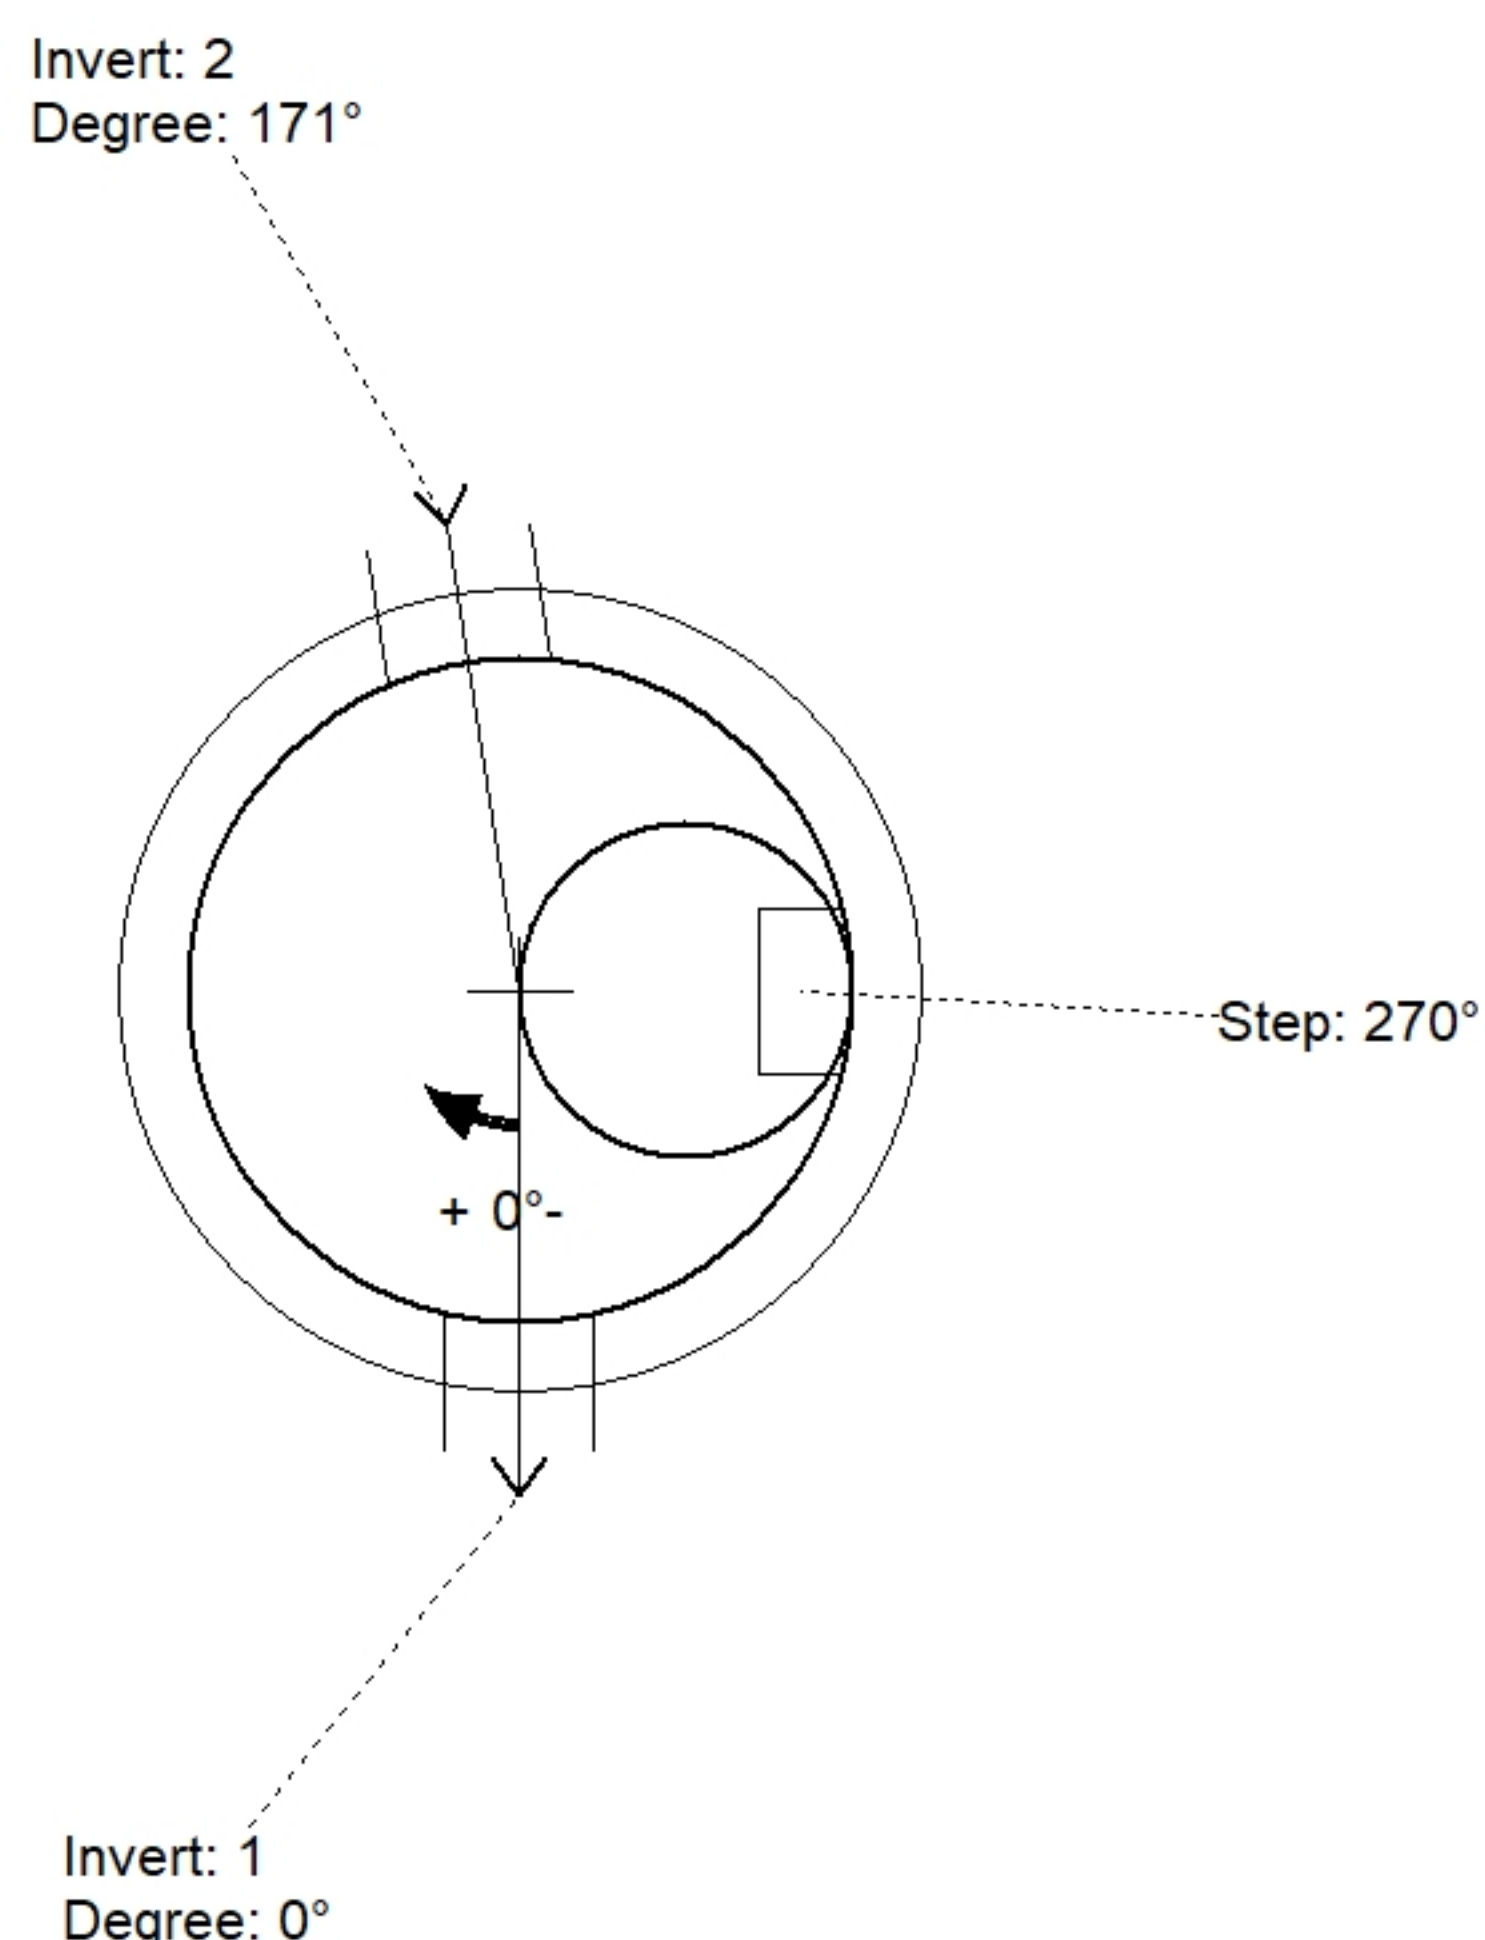


Floor (Bot): 867.723'
Overall Height: 4.583'
Slack: 2.2"

P3) 24" - CASTING HEIGHT - 7"	0 lb
P2) 48" - ECC CONE w/ 24" HOLE - 24"	1550 lb
P1) 48" - MH BASE - 18"	2501 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-315 F/C Sanitary	258 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
1) Quik-Lok - QL-08-C	1 lb
1) PSX - 12M NYLO	8 lb
3) MH Step ML-10-TDS-NCR - 10"	0 lb
Structure Total:	5758 lb

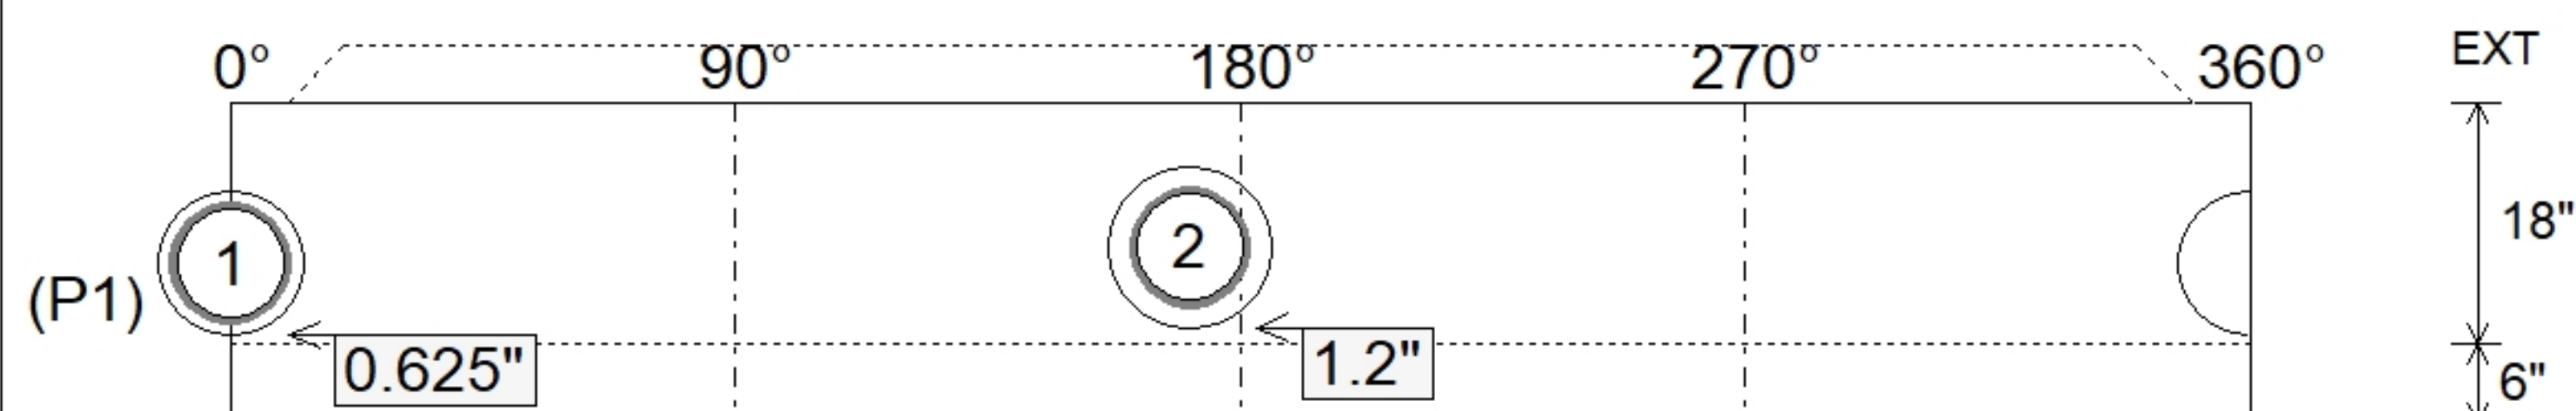

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (')	Ref
Rim	872.49'							
Reducer								
Invert 1	868.39'	0°	8" PVC C900	9.05"	10.75"	Quik-Lok QL-08-C	0.625"	P1
Invert 2	868.49'	171°	8" PVC C900	9.05"	12"	PSX 12M NYLO	1.2"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

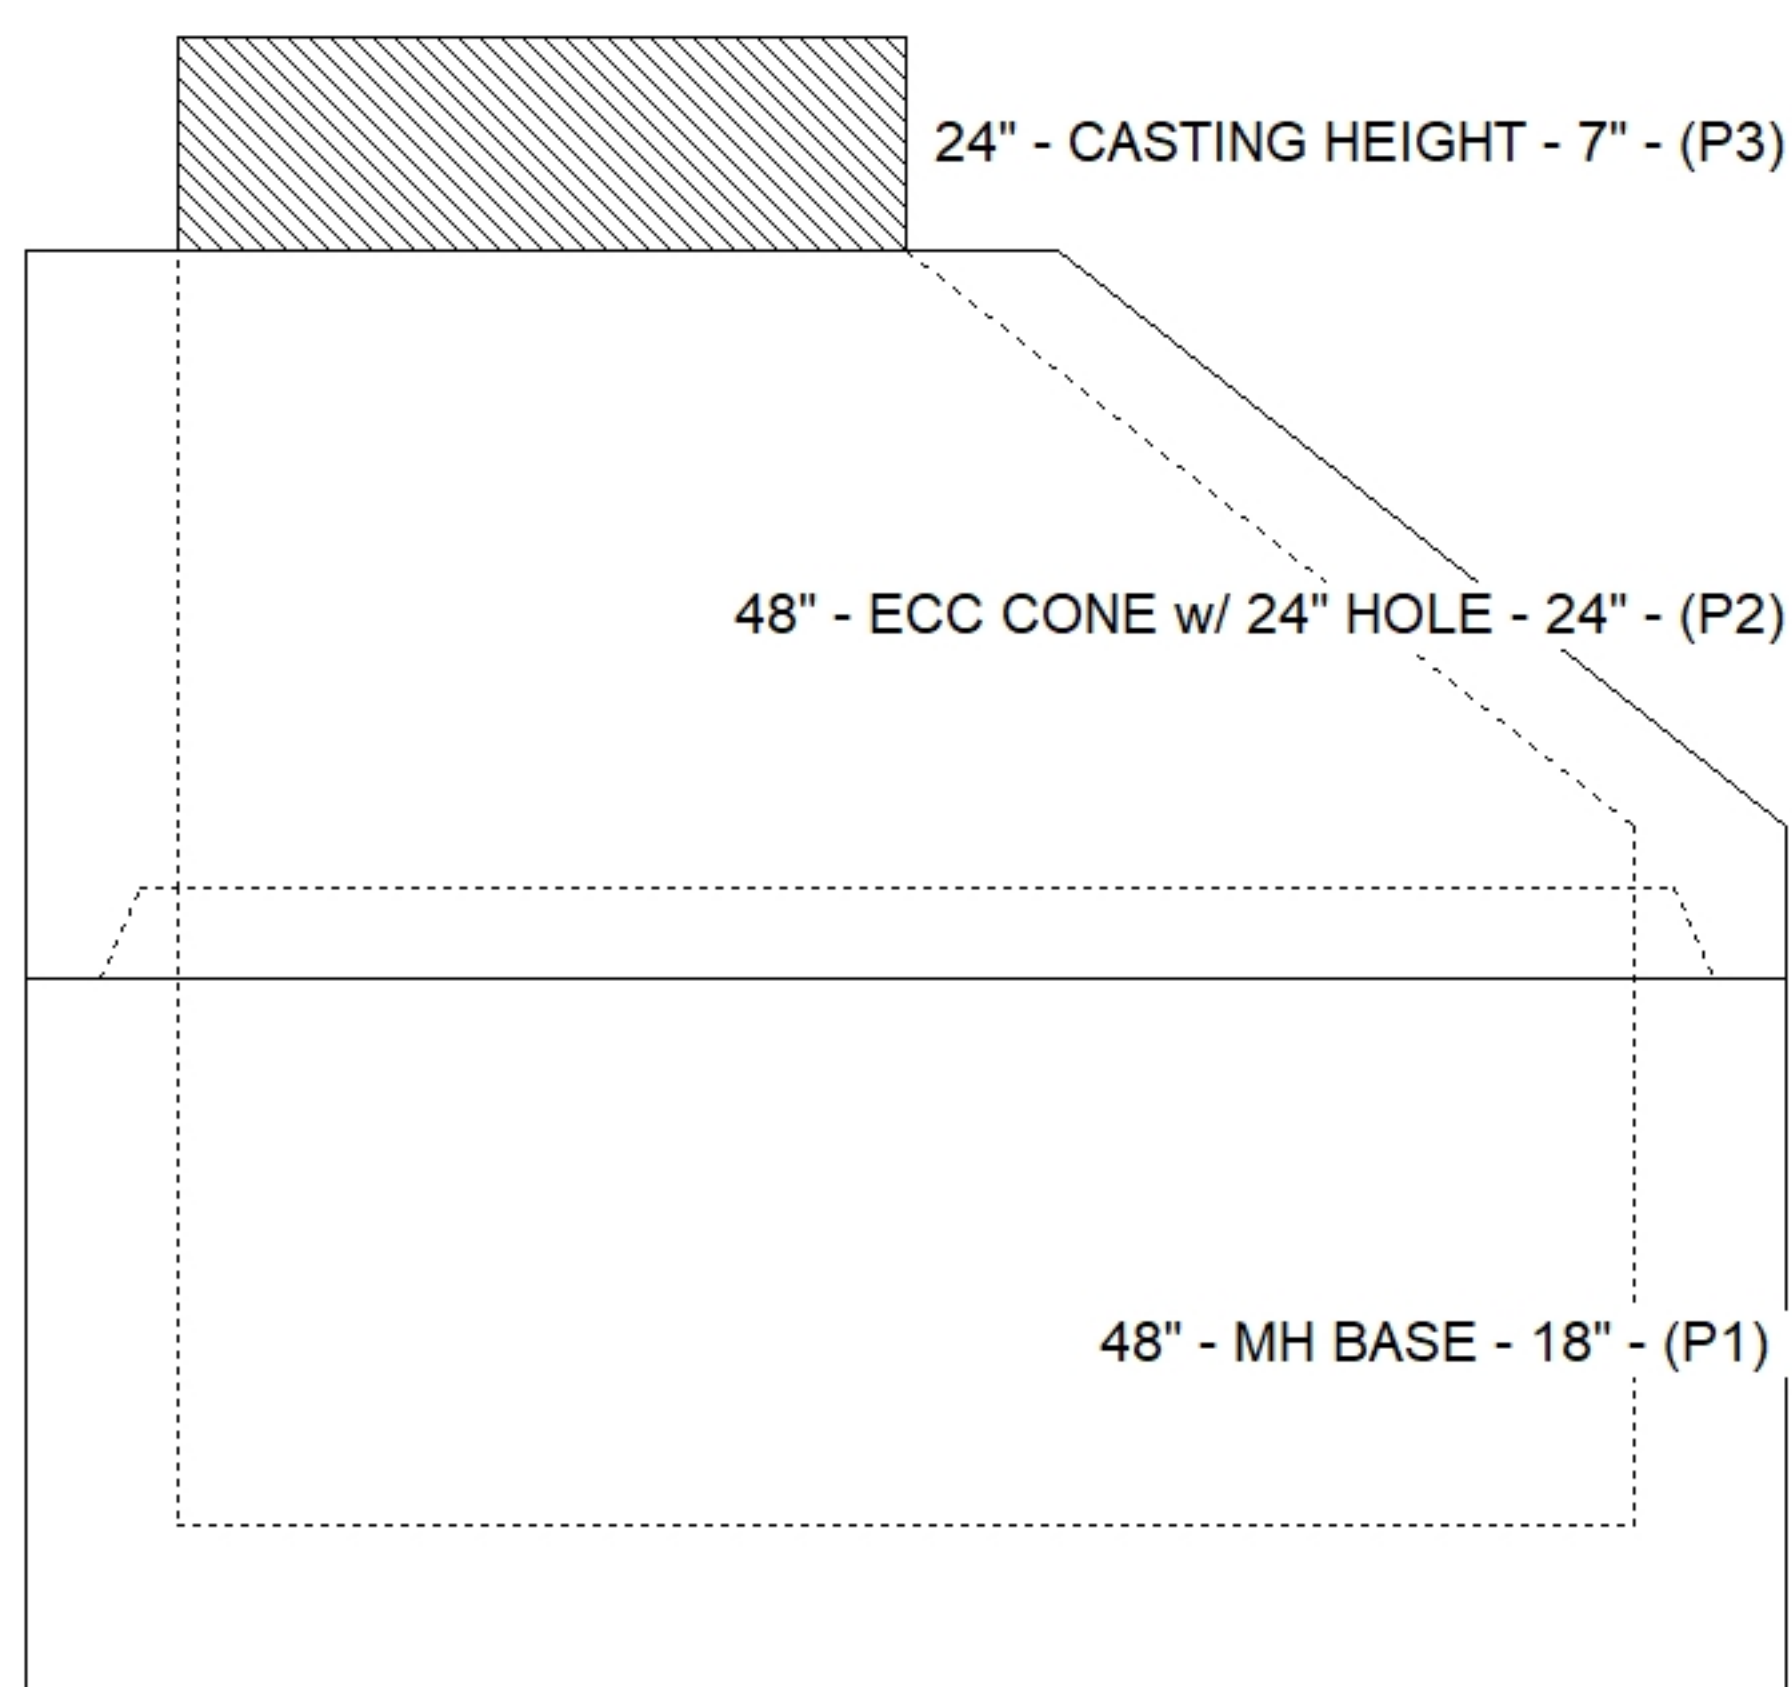

SUBMITTAL
APPROVED BY:
