



Floor (Bot): 879.453'
Overall Height: 8.583'
Slack: 0.52"

P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 48" - ECC CONE w/ 24" HOLE - 30"	2050 lb
P2) 48" - MH RISER - 36"	2515 lb
P1) 48" - MH BASE - 24"	2863 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-315 F/C Sanitary	258 lb
2) 48" - Conseal CS-102 1.00" (Double)	0 lb
2) PSX - 12M NYLO	16 lb
1) PSX - 12-06 NYLO	8 lb
7) MH Step ML-10-TDS-NCR - 10"	0 lb

Structure Total:	9150 lb

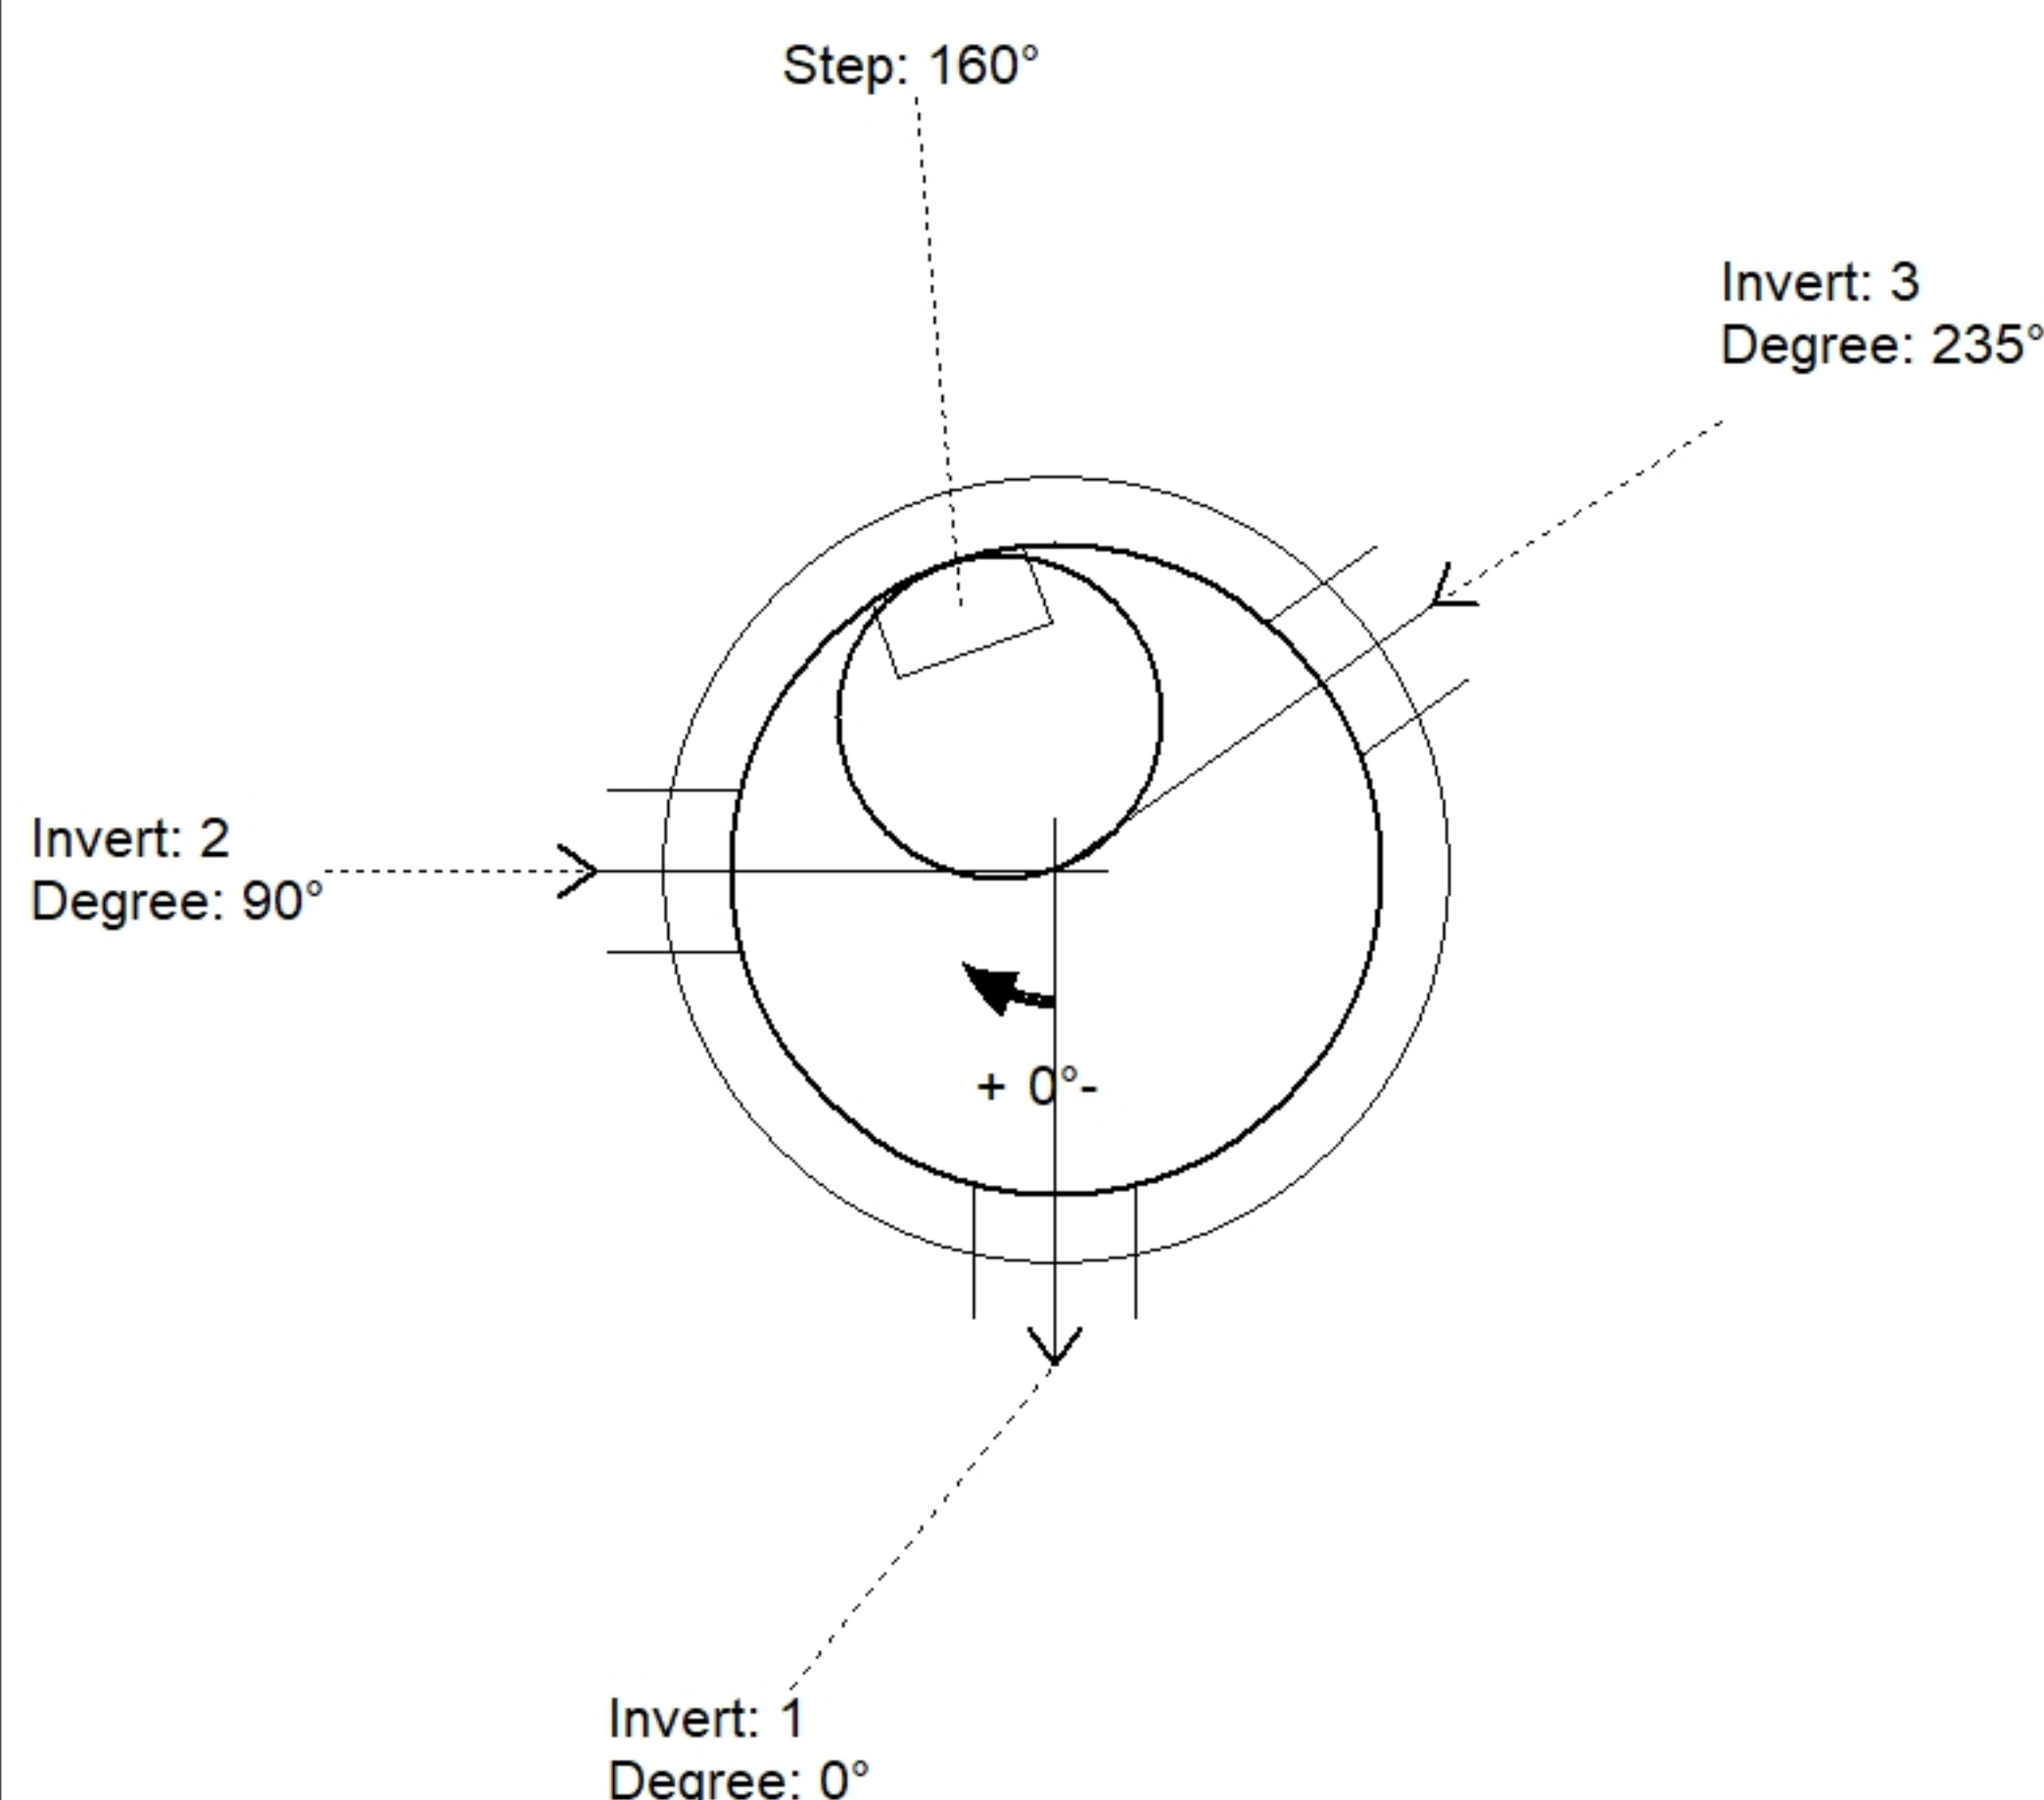

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (")	Ref
Rim	888.08'							
Reducer								
Invert 1	880.12'	0°	8" PVC C900	9.05"	12"	PSX 12M NYLO	0"	P1
Invert 2	880.22'	90°	8" PVC C900	9.05"	12"	PSX 12M NYLO	1.2"	P1
Invert 3	880.22'	235°	6" PVC C900	6.9"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

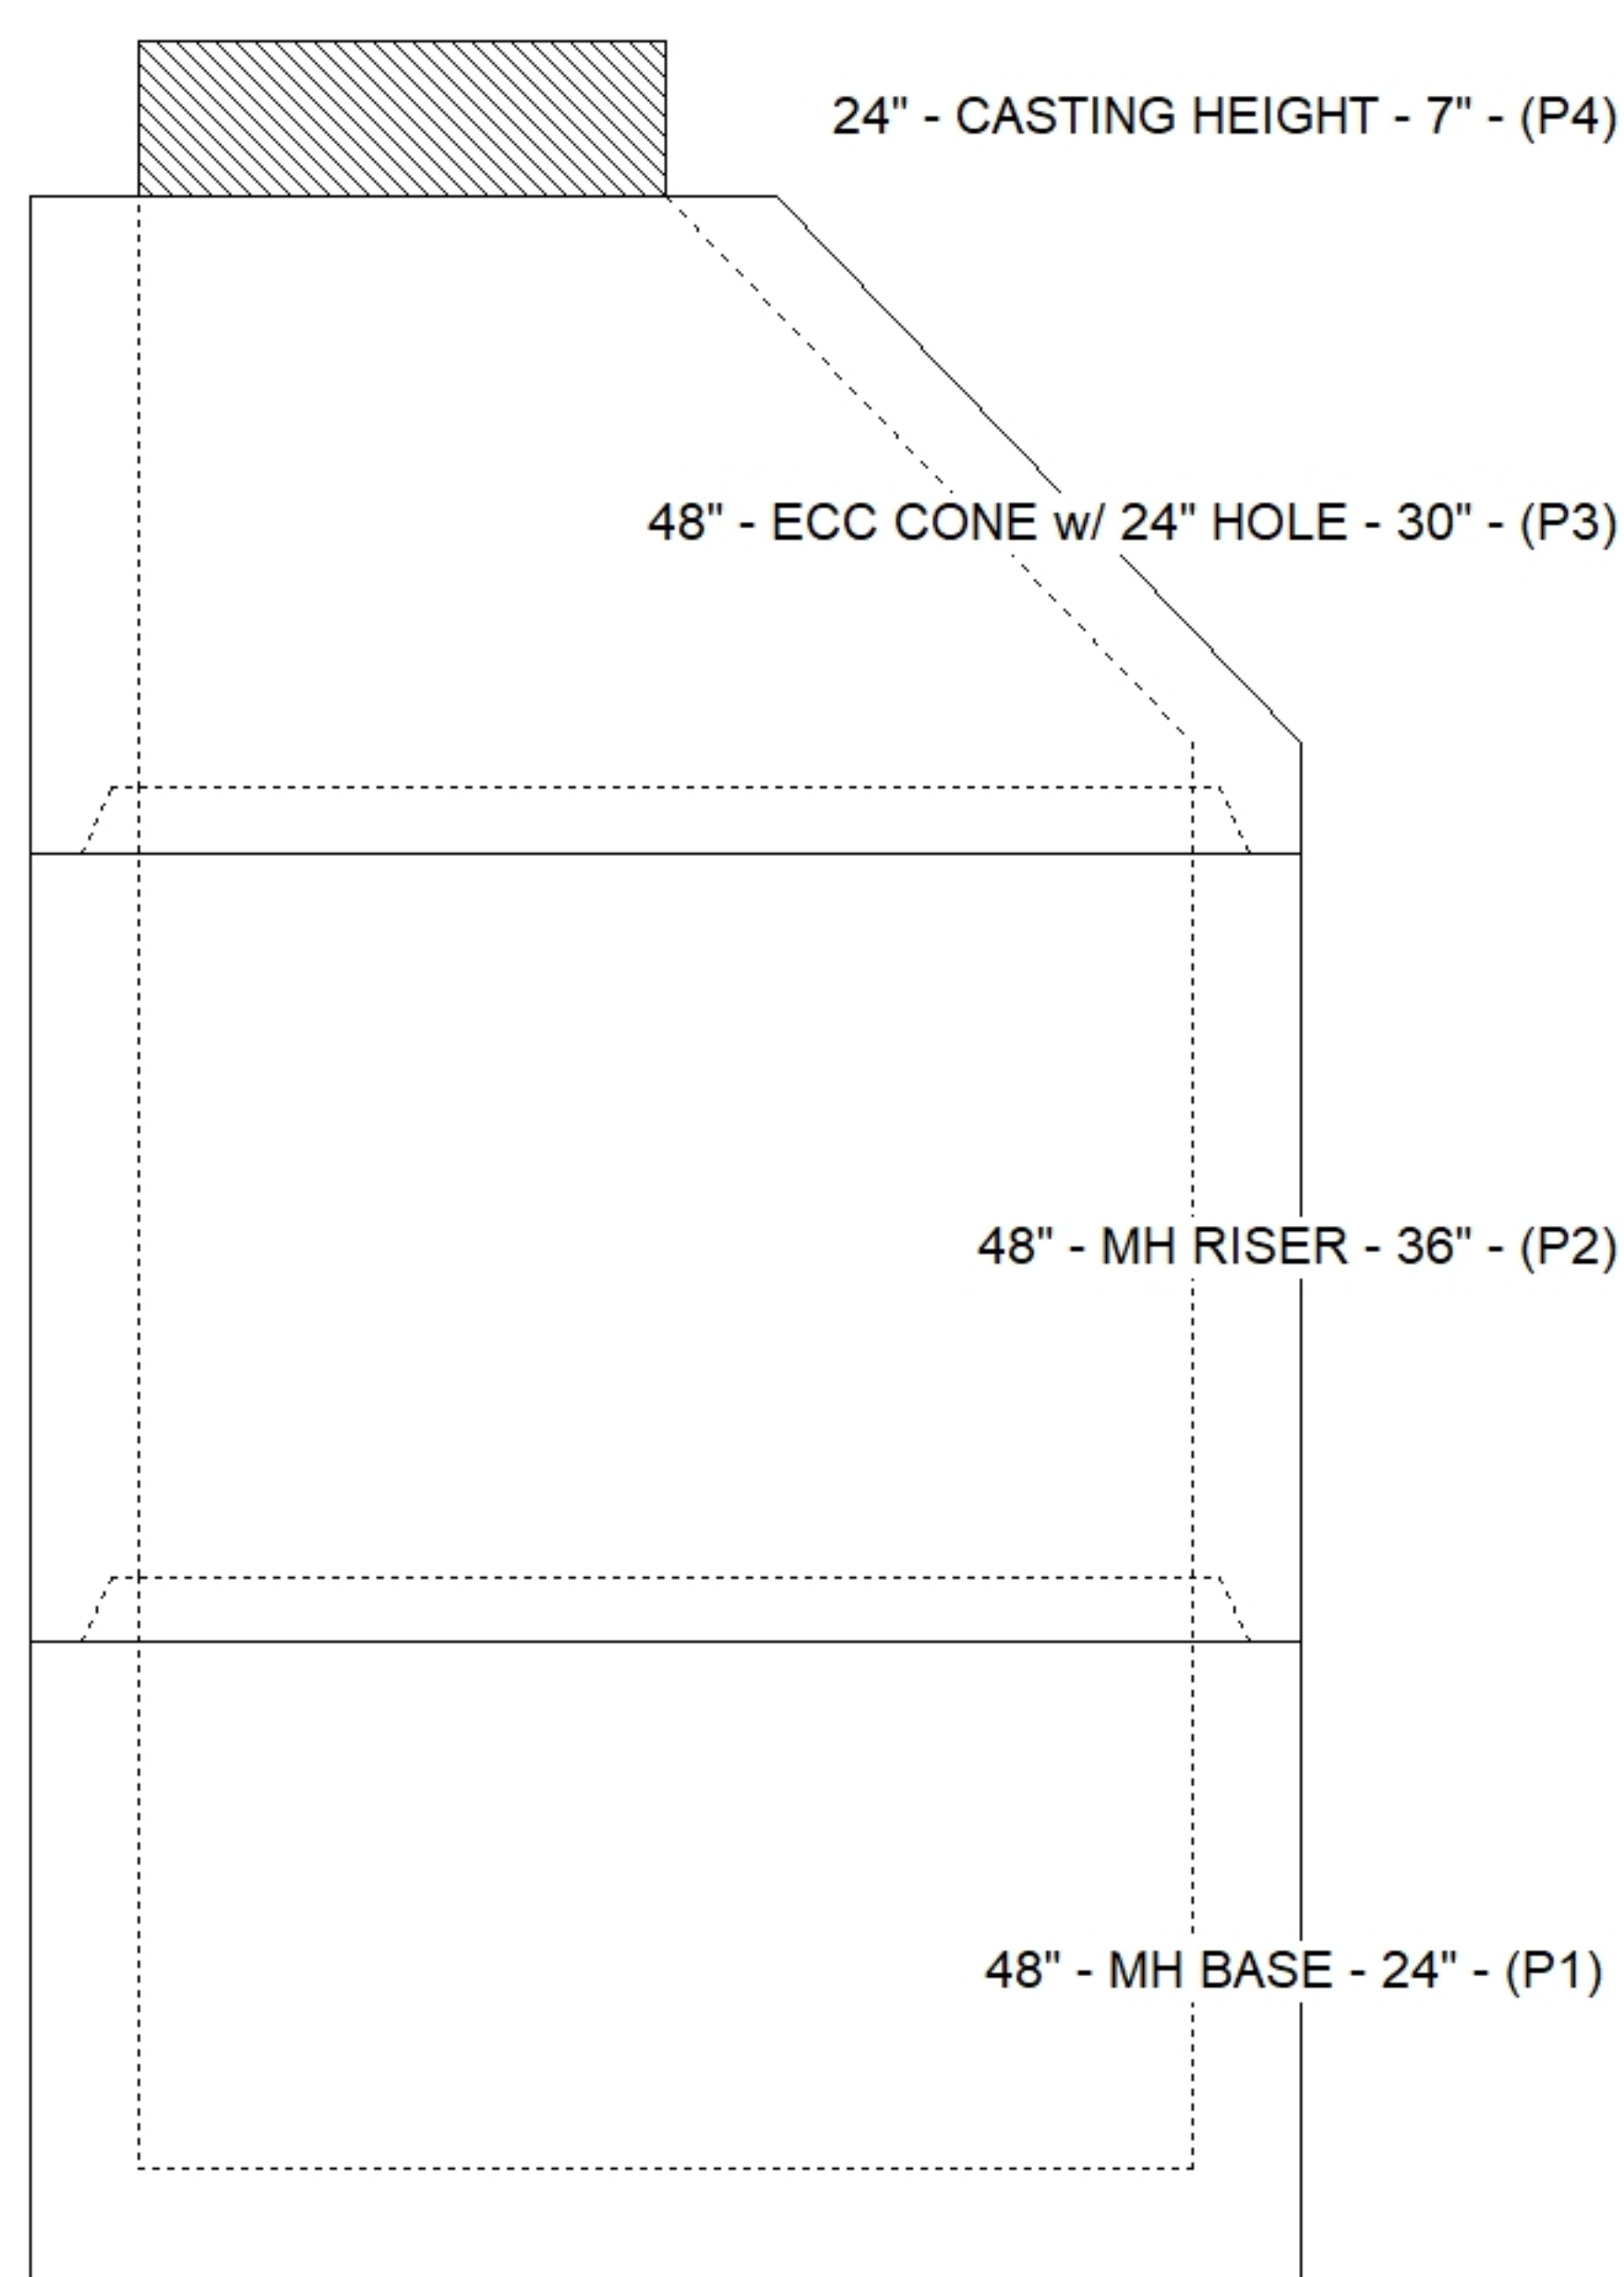

SUBMITTAL
APPROVED BY:
