



Job Name: 25-4733 - The Paddock Job Location: Springfield, KY Contractor: Core & Main LP (Lou)					Plant: 100 5/4/2026 6:49:16 PM		Tech: Jared - F PC: T. Lewis						
Structure ID: SSWR-4													
P1 MH048BA18			MH BASE T/n										
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12M NYLO 8) MH Step ML-10-TDS-NCR - 10"						0 lb 2050 lb 3353 lb 2492 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 16 lb 0 lb ----- Structure Total: 9609 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.					
Rim: 888.1' Rim to Invert: 8.44' Slack: 0.28" Sump: 2" Step Position: 90°													
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset			
Invert 1	879.66'	0°	0"	8" PVC C900	9.05"	PSX 12M NYLO	12"	12.129"	0"	0"			
Invert 2	879.76'	180°	91.125"	8" PVC C900	9.05"	PSX 12M NYLO	12"	12.129"	1.25"	0"			
Invert 3													
Invert 4													
Invert 5													
Invert 6													
Invert 7													
Invert 8													

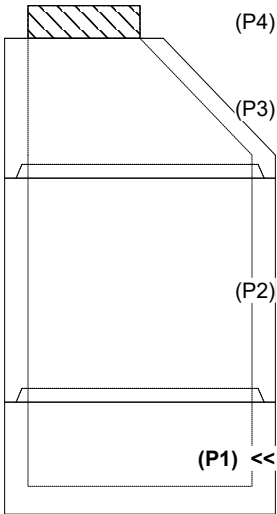

(P4)
(P3)
(P2)
(P1) <<

RIGHT-SIDE UP VIEW (int. dimensions)

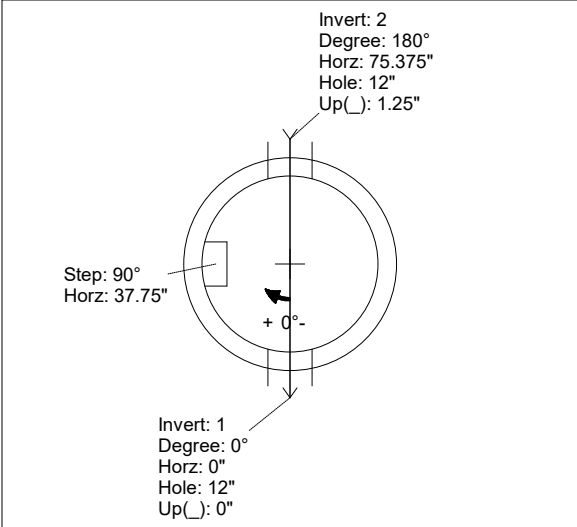


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 12"
Up(_): 1.25"

Step: 90°
Horz: 37.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(_): 0"

UPSIDE-DOWN VIEW (int. dimensions)

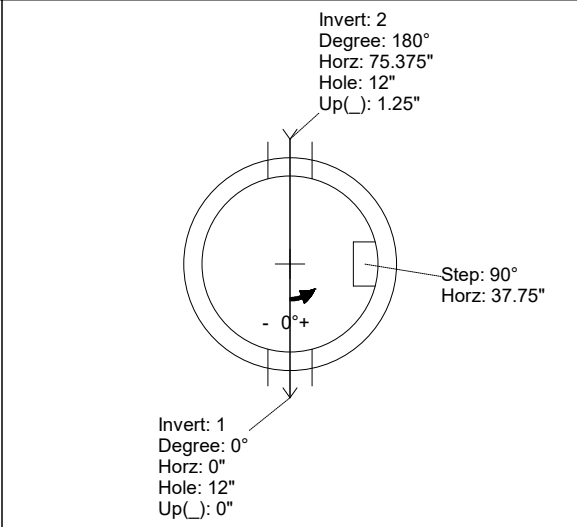


Invert: 2
Degree: 180°
Horz: 75.375"
Hole: 12"
Up(_): 1.25"

Step: 90°
Horz: 37.75"

Invert: 1
Degree: 0°
Horz: 0"
Hole: 12"
Up(_): 0"

INSIDE WALL DIMENSIONS



(P1)


1.25"
75.375"
0"


360° 270° 180° 90° 0°


6"
18"
EXT


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2492 lb Volume (Net): 0.64cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 25-4733 - The Paddock Job Location: Springfield, KY Contractor: Core & Main LP (Lou)					Plant: 100 5/4/2026 6:49:16 PM		Tech: Jared - F PC: T. Lewis					
Structure ID: SSWR-4												
P1 MH048BA18			MH BASE T/n									
P4) 24" - CASTING HEIGHT - 7" P3) 48" - ECC CONE w/ 24" HOLE F/G - 30" P2) 48" - MH RISER T/G - 48" P1) 48" - MH BASE T/n - 18" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 48" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 2) 48" - Conseal CS-102 1.00" (Double) 2) PSX - 12M NYLO 8) MH Step ML-10-TDS-NCR - 10"						0 lb 2050 lb 3353 lb 2492 lb 0 lb 0 lb 1440 lb 258 lb 0 lb 16 lb 0 lb ----- Structure Total: 9609 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. CASTING BY ICAST (HOE MC-315 F/C SANITARY). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 888.1' Rim to Invert: 8.44' Slack: 0.28" Sump: 2" Step Position: 90°												
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset		
Invert 1	879.66'	0°	0"	8" PVC C900	9.05"	PSX 12M NYLO	12"	12.129"	0"	0"		
Invert 2	879.76'	180°	91.125"	8" PVC C900	9.05"	PSX 12M NYLO	12"	12.129"	1.25"	0"		
Invert 3												
Invert 4												
Invert 5												
Invert 6												
Invert 7												
Invert 8												

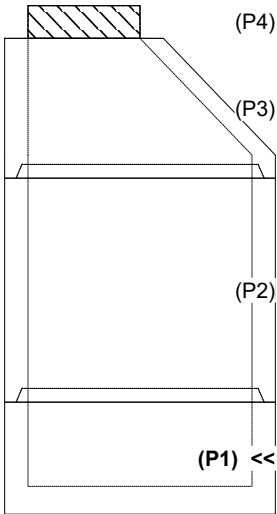

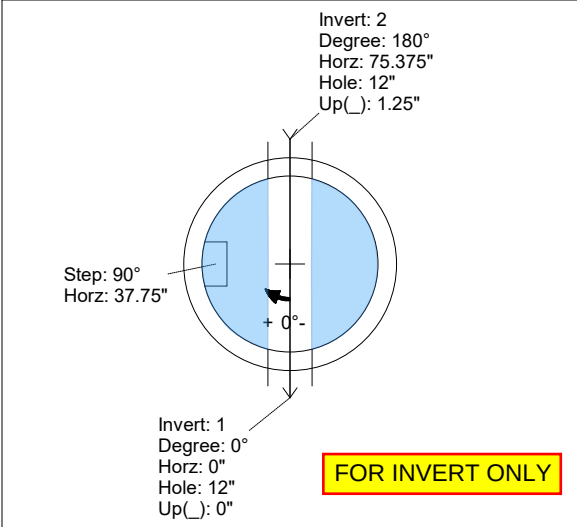RIGHT-SIDE UP VIEW (int. dimensions)

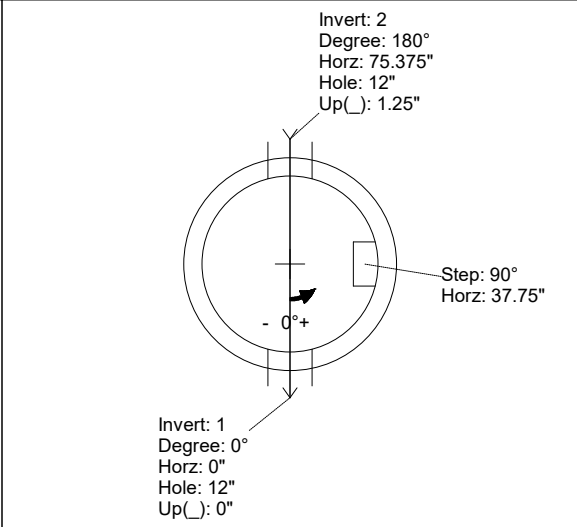
UPSIDE-DOWN VIEW (int. dimensions)


INSIDE WALL DIMENSIONS


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 18" Height (Ext): 24"	Weight (Net): 2492 lb Volume (Net): 0.64cu.yd
----------------------------------	---------------------------------	--	--	--
