


Structure ID: SSWR-6			
Spec: Sanitary	Rim: 892.81'	Sump: 2"	Floor (Bot): 885.963'
Type: SAN.MH	Invert: 886.63'	Floor (Top): 886.463'	Overall Height: 6.833'
Size: 48"	Rim to Invert: 6.18'	Floor Height: 6"	Slack: 0.16"


Structure Notes: 1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. CASTING BY ICAST (HOE MC-315 F/C SANITARY).
REINFORCING PER ASTM A615 (GRADE 60).
- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

STRUCTURE SUMMARY:	
P4) 24" - CASTING HEIGHT - 7"	0 lb
P3) 24" - GRADE RING - 3"	202 lb
P2) 48" - ECC CONE w/ 24" HOLE - 36"	3000 lb
P1) 48" - MH BASE - 30"	3282 lb
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212	0 lb
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)	0 lb
1) 48" - MH INVERT CHANNEL - FULL HEIGHT	1440 lb
1) CASTING - HOE MC-315 F/C Sanitary	258 lb
1) 48" - Conseal CS-102 1.00" (Double)	0 lb
2) PSX - 12M NYLO	16 lb
1) PSX - 12-06 NYLO	8 lb
5) MH Step ML-10-TDS-NCR - 10"	0 lb


Structure Total:	8207 lb

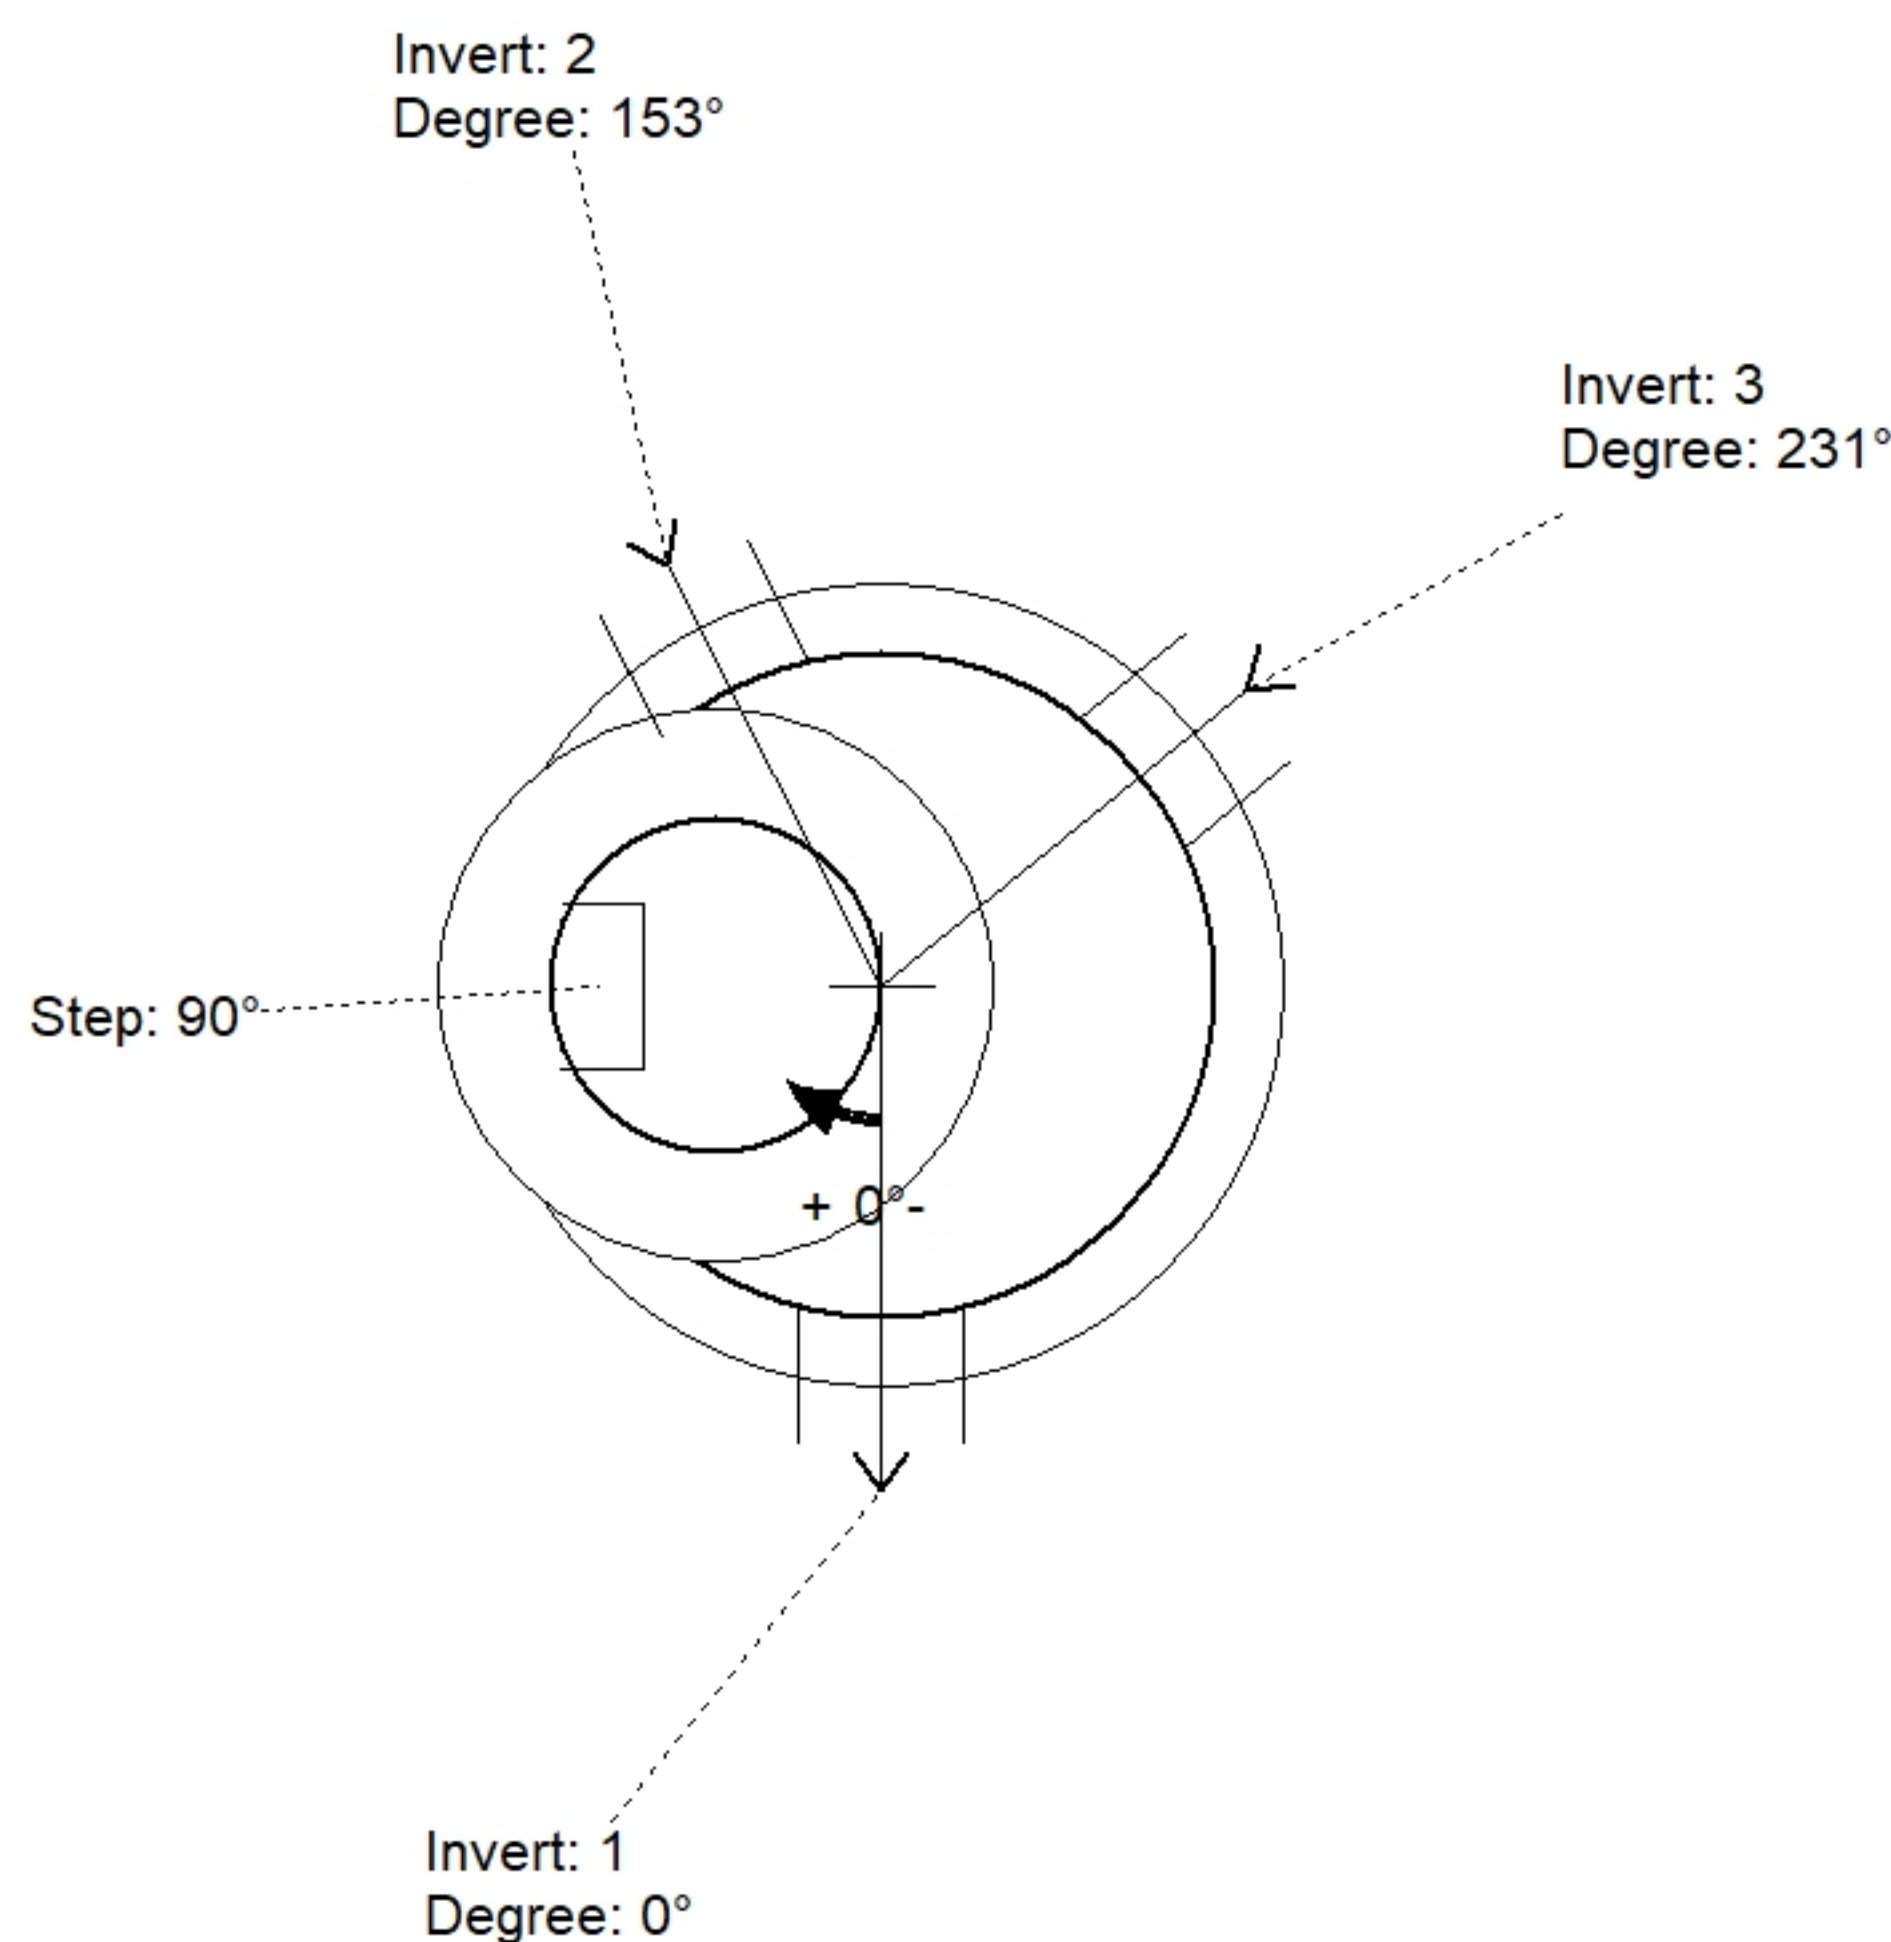

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up ()	Ref
Rim	892.81'							
Reducer								
Invert 1	886.63'	0°	8" PVC C900	9.05"	12"	PSX 12M NYLO	0"	P1
Invert 2	886.73'	153°	8" PVC C900	9.05"	12"	PSX 12M NYLO	1.2"	P1
Invert 3	886.73'	231°	6" PVC C900	6.9"	12"	PSX 12-06 NYLO	0.2"	P1
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

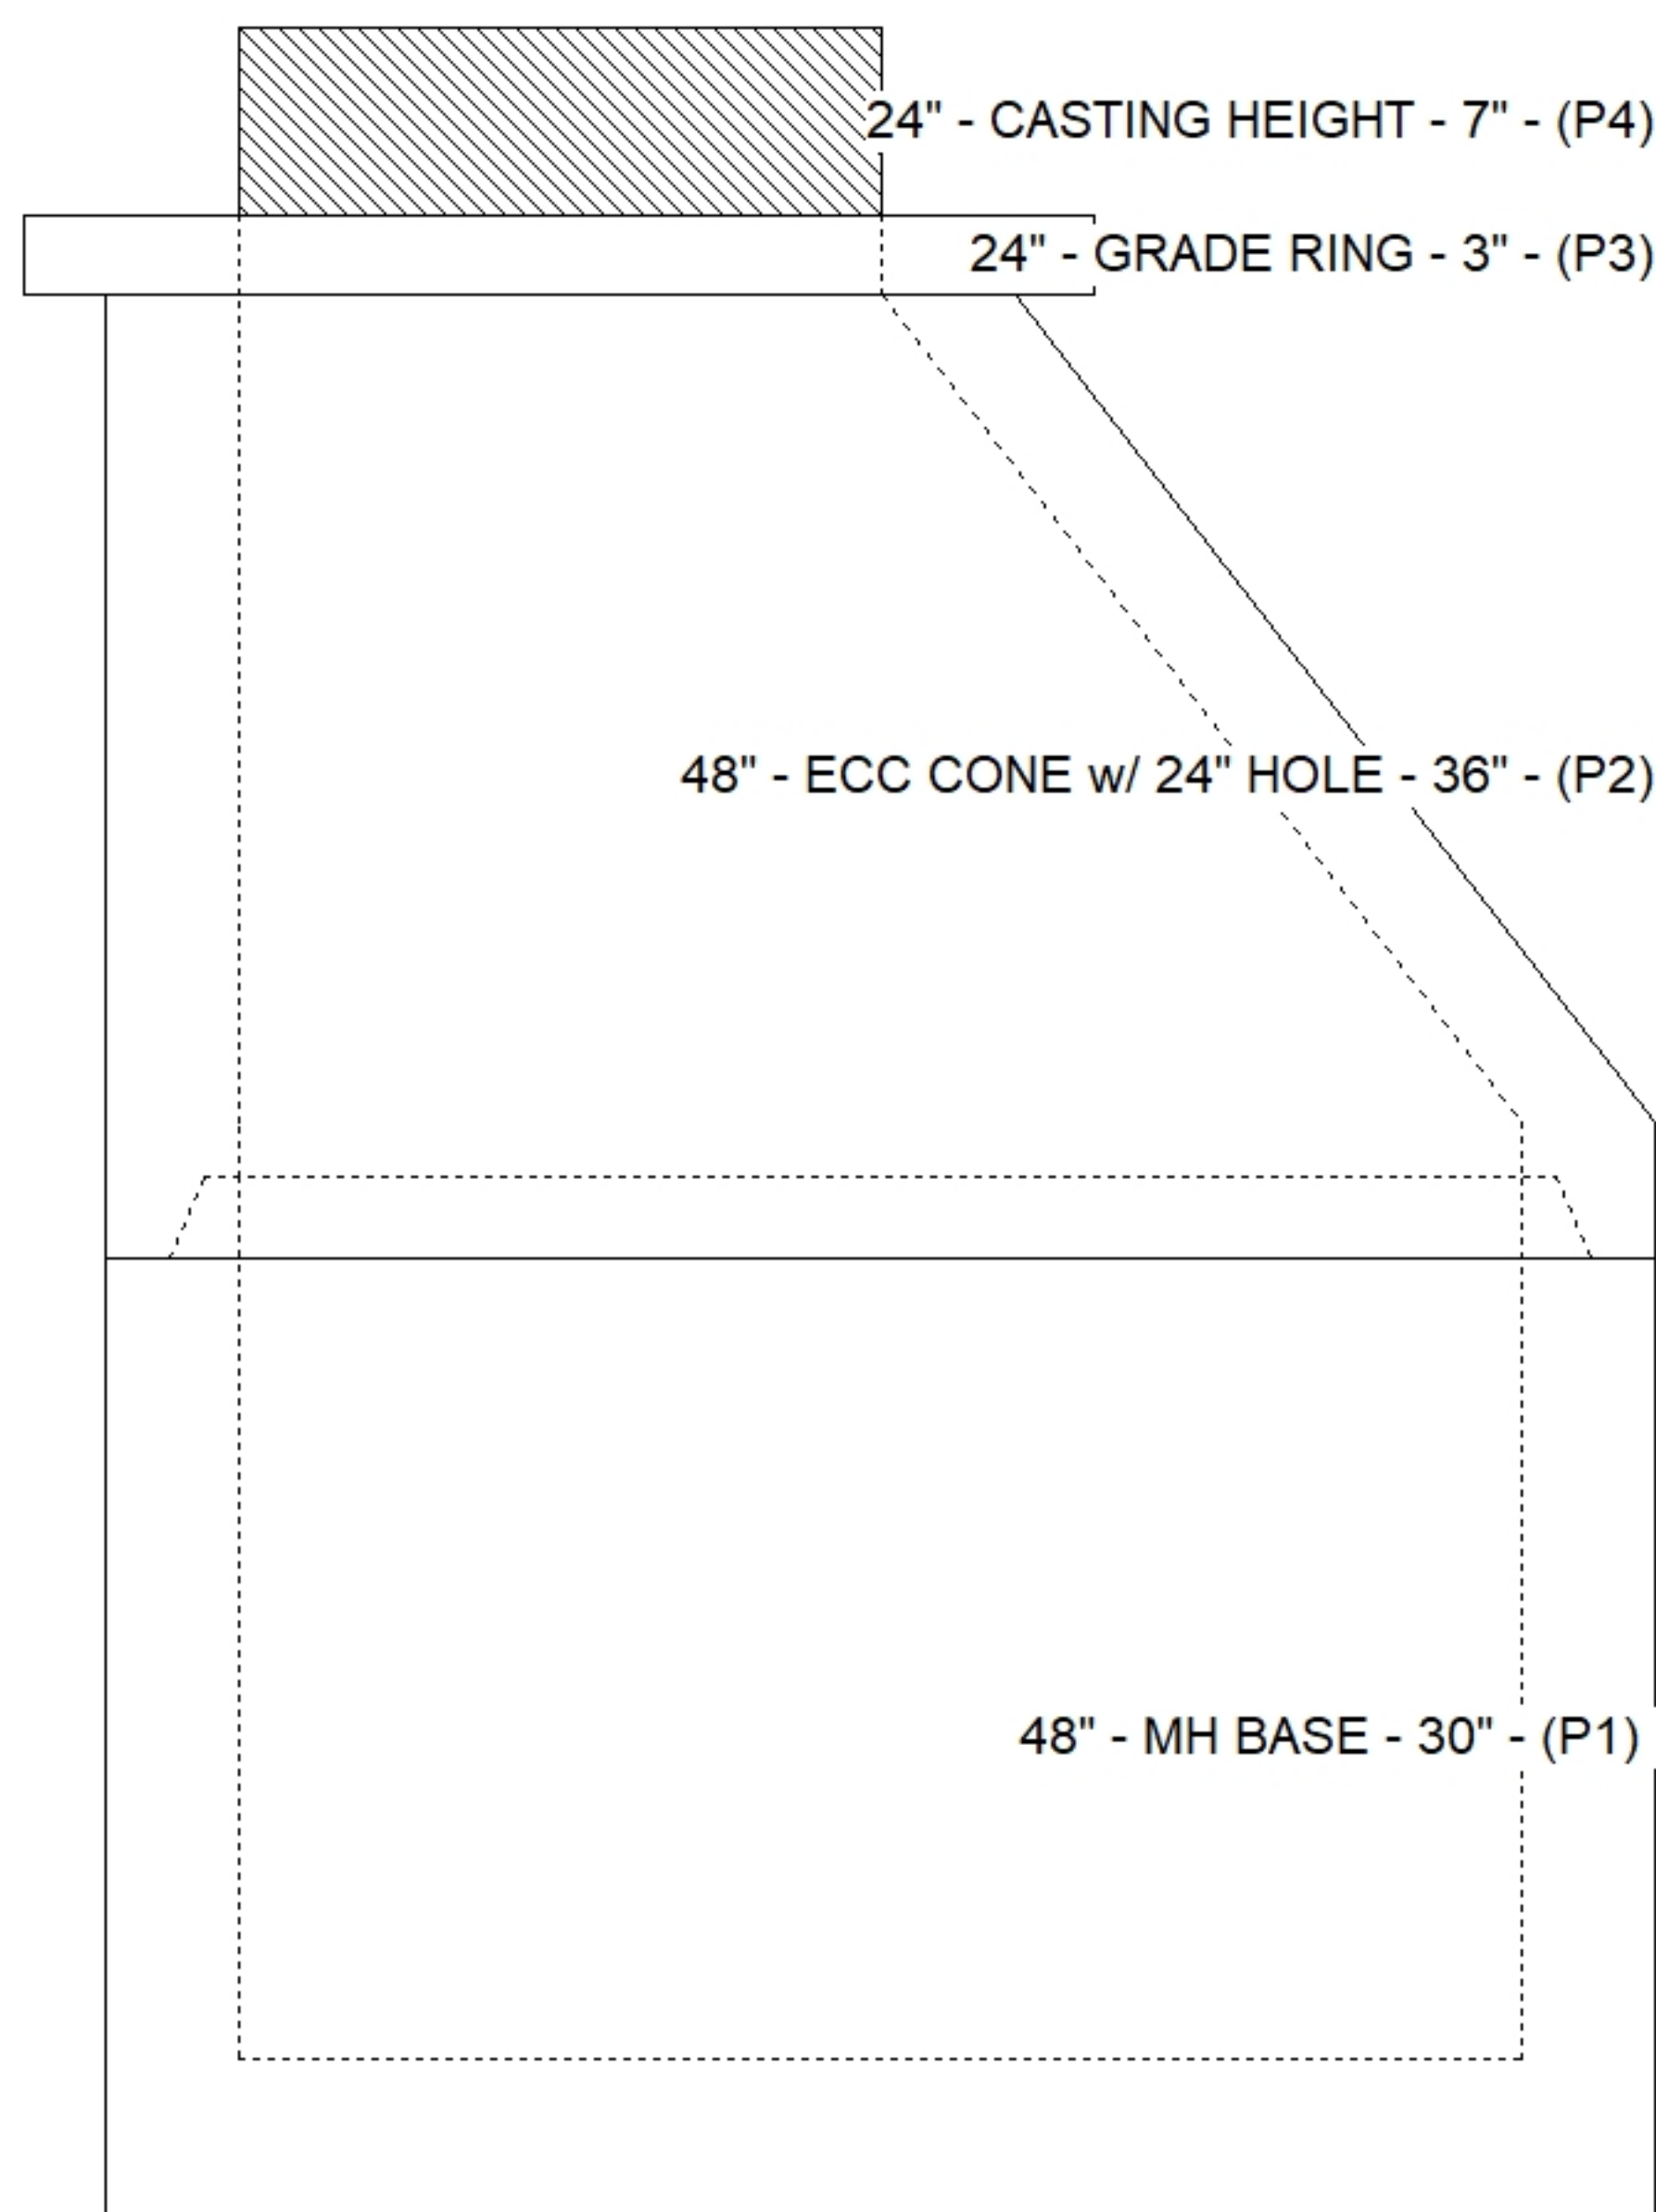

Default - Interior Dimensions

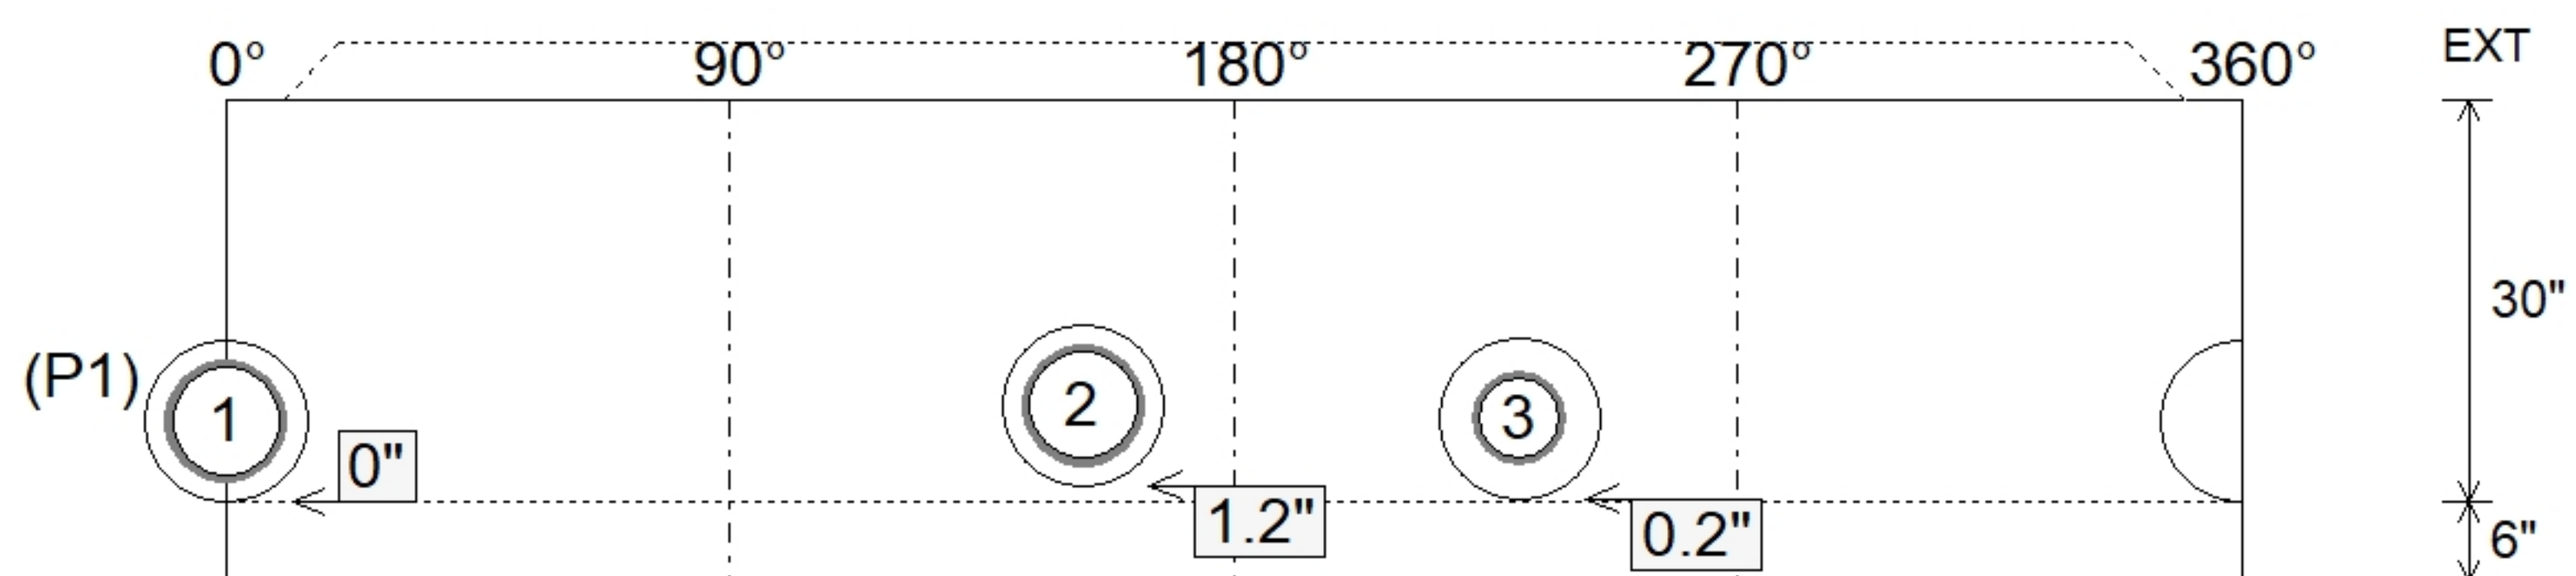

Submittal Drawing 5/18/2026 10:36:28 AM	SUBMITTAL APPROVED BY:
--	---------------------------
