

**Contractor: Covenant Constructors, LLC**

TECH: Jared - F

Plant: 100



Size: 28" x 64"

Rim to Invert: 2.72'

Floor Height: 6"


Slack: 0.64"

REINFORCING PER ASTM A615 (GRADE 60).  
- WALLS (As .31) #5 BARS AT 12" C.C.E.W.  
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.


P2) 28" x 64" - CASTING HEIGHT - 7.50"  
P1) 28" x 64" - BOX BASE 6inW, 6inF, Variable Ht - 27"  
1) CASTING - JBS 3300 F/G/H - Double Curb Inlet  
1) 28" x 64" - Conseal CS-102 1.00"  
1) DOGHOUSE INVRTD - 26"x27"  
1) DOGHOUSE INVRTD - 26"x25"

0 lb  
3740 lb  
500 lb  
0 lb  
0 lb  
0 lb


Structure Total: 4240 lb

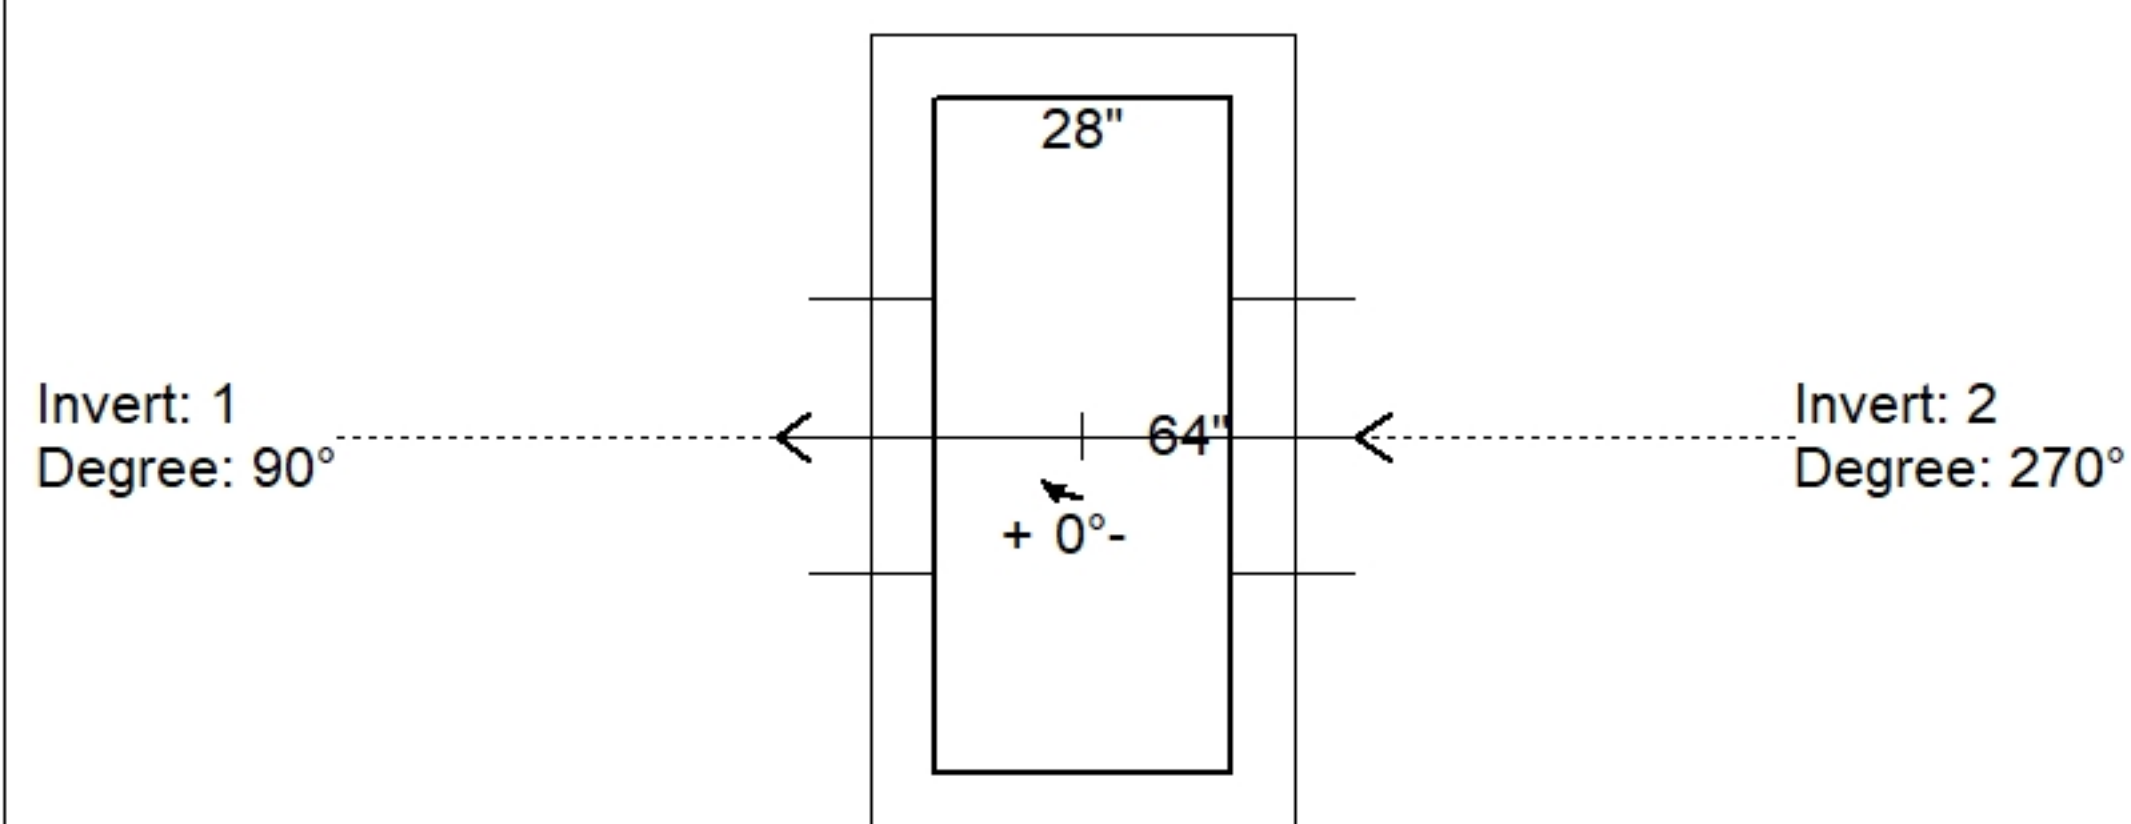

| Position | Elev    | Angle | Pipe           | Pipe OD | Hole      | Connector               | Up ( ) | Ref |
|----------|---------|-------|----------------|---------|-----------|-------------------------|--------|-----|
| Rim      | 481.34' |       |                |         |           |                         |        |     |
| Reducer  |         |       |                |         |           |                         |        |     |
| Invert 1 | 478.62' | 90°   | 18" RCP B WALL | 23"     | 26" x 27" | DOGHOUSE INVRTD 26"x27" | 0"     | P1  |
| Invert 2 | 478.72' | 270°  | 18" RCP B WALL | 23"     | 26" x 25" | DOGHOUSE INVRTD 26"x25" | 1.2"   | P1  |
| Invert 3 |         |       |                |         |           |                         |        |     |
| Invert 4 |         |       |                |         |           |                         |        |     |
| Invert 5 |         |       |                |         |           |                         |        |     |
| Invert 6 |         |       |                |         |           |                         |        |     |
| Invert 7 |         |       |                |         |           |                         |        |     |
| Invert 8 |         |       |                |         |           |                         |        |     |

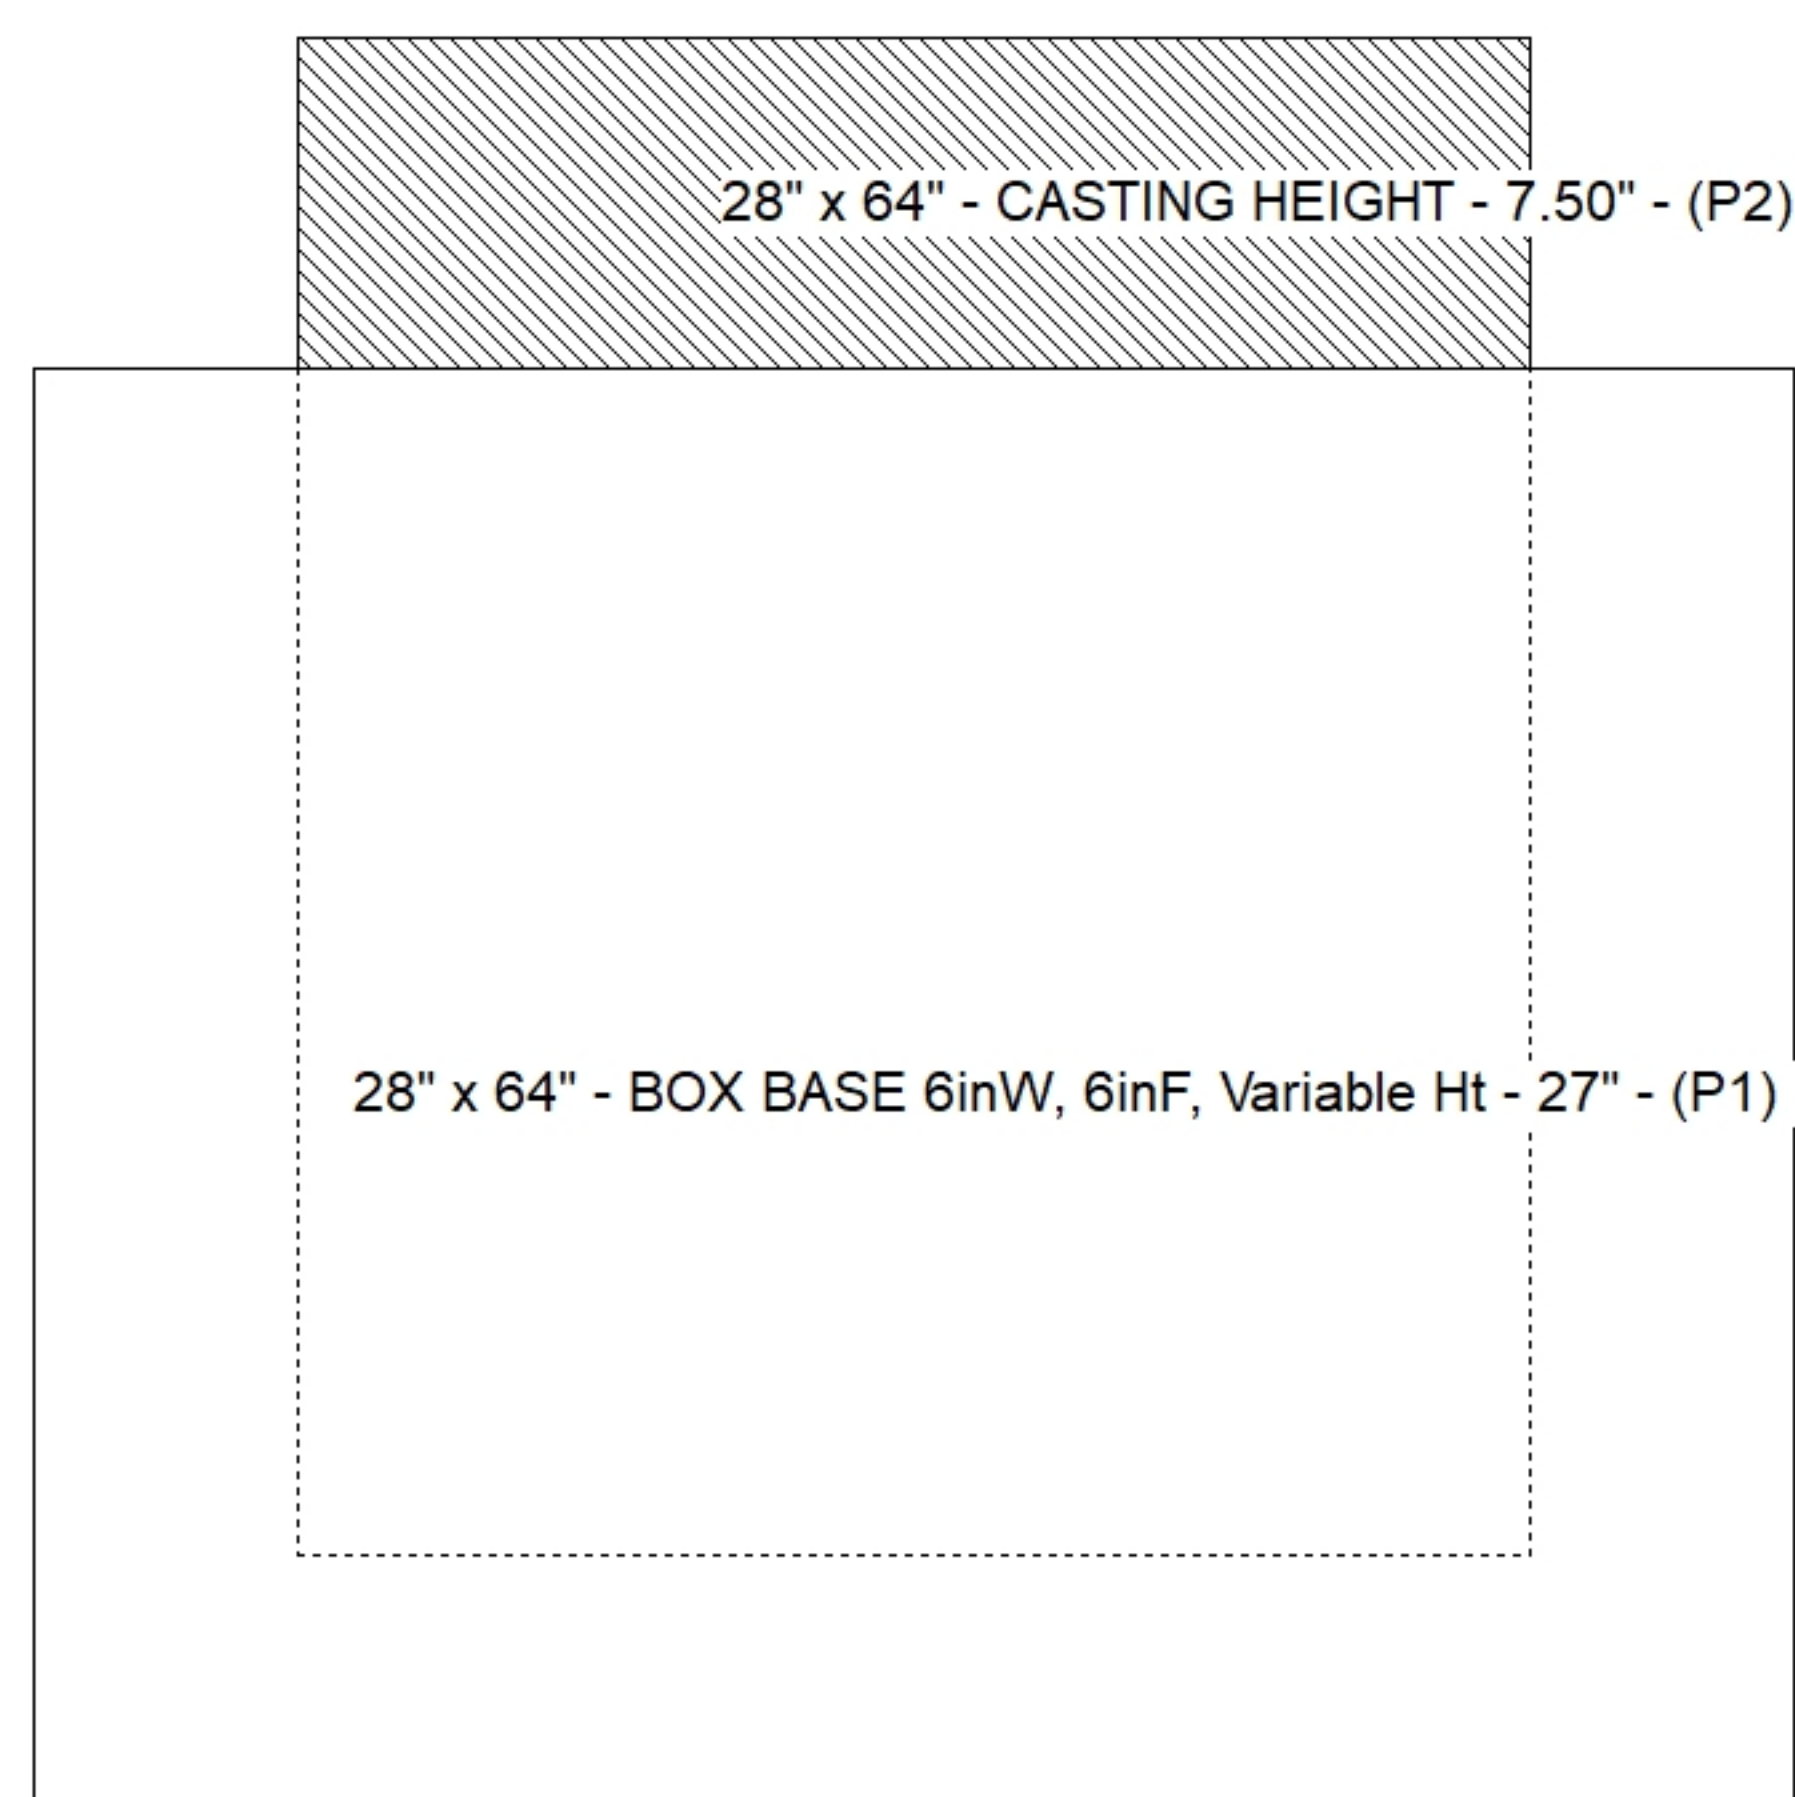

### Default - Interior Dimensions

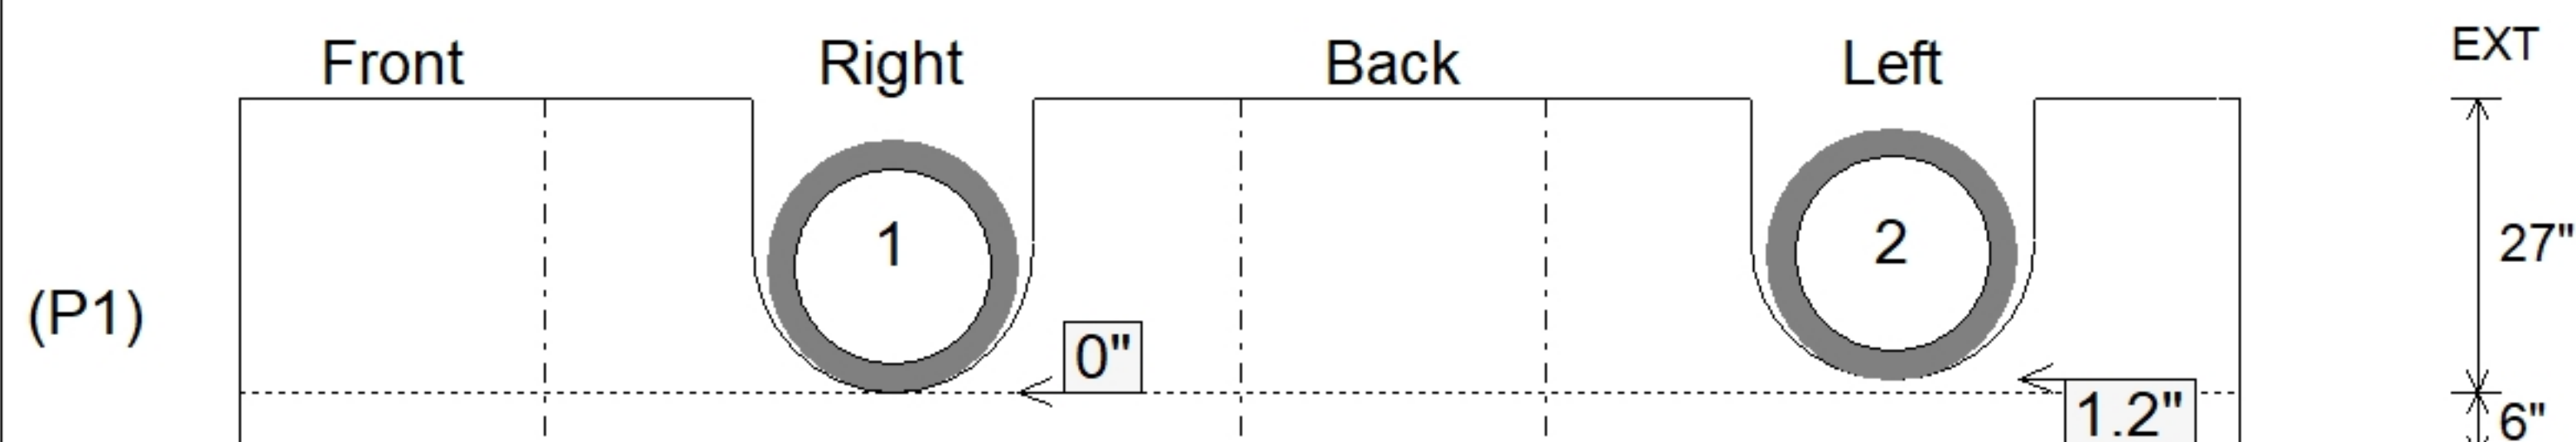

Submittal Drawing  
9/29/2026 10:09:02 AM

SUBMITTAL  
APPROVED BY:
