

Job Name: 26-1029 - 873697 BJ's Wholesale Club
 Job Location: Frankfort, KY
 Contractor: Contech Engineering Solutions

Plant: Beaver Dam
 1/9/2026 8:56:34 AM

Tech: J. Coppage
 PC: T. Sekula



Structure ID: 15-CS-6

P1 MH072BA84

MH BASE

- P4) 30" - CASTING HEIGHT - 4"
- P3) 72" - MH FLAT TOP SPEC. (30" ECC HOLE) - 15"
- P2) 72" - MH RISER - 36"
- P1) 72" - MH BASE - 84"
- 1) ASSEMBLY REQUIRED
- 1) CVSTENCILING
- 2) 72" - Conseal CS-102 1.00"
- 2) Hole - 16"

Structure Notes:
 (4" TALL CASTING PROVIDED BY OTHERS)
 LIFTING ANCHORS TO BE INSTALLED ON THE OUTSIDE OF THE STRUCTURE
 ICAST TO INSTALL THE INTERNALS
 CONTECH'S LOGO AS WELL AS THE INLET AND THE OUTLET MUST BE STENCILED ONTO THE STRUCTURE



Structure Total: 25816 lb

Rim: 734.71' Rim to Invert: 7.48' Slack: 10.76" Sump: 60" Step Position:


Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	727.23'	270°	202.633"	12" ADS N-12	14.5"	Hole 16	16"	16.135"	58"	0"
Invert 2	727.23'	344°	258.169"	12" ADS N-12	14.5"	Hole 16	16"	16.135"	58"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

RIGHT-SIDE UP VIEW (int. dimensions)

UPSIDE-DOWN VIEW (int. dimensions)

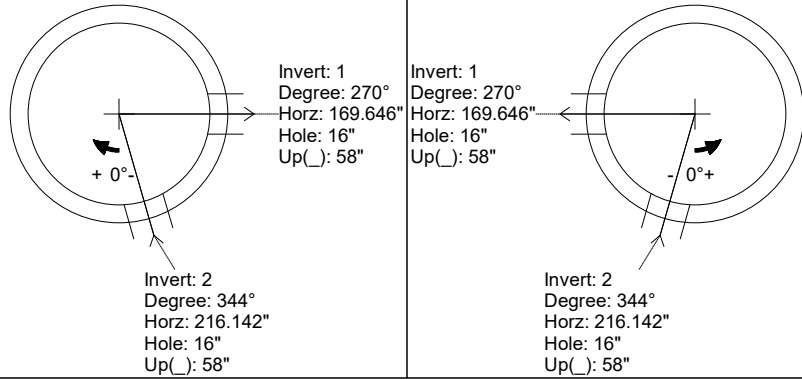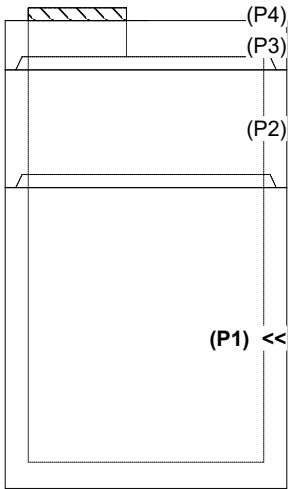

INSIDE WALL DIMENSIONS

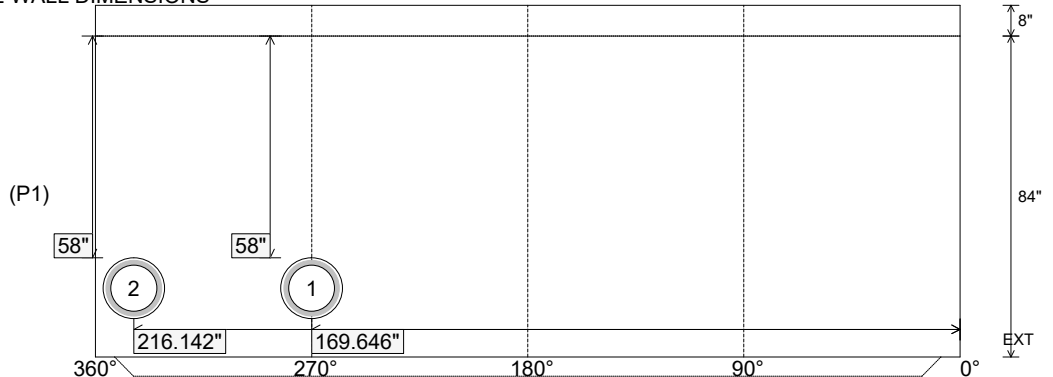

Coating (Int):
 Coating (Ext):

Seam Up: Tongue
 Seam Dn: n/a

Wall Thickness: 7"
 Floor Height: 8"

Height (Int): 84"
 Height (Ext): 92"

Weight (Net): 15907 lb
 Volume (Net): 4.06cu.yd
