



Job Name: 26-1038 - Perryville & Junction City WW Improvements Job Location: Danville, KY Contractor: Connhurst, LLC					Plant: 100 5/6/2026 4:06:53 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: 61038 (4)											
P4 MH096RSVF MH RISER Custom Ht T/G											
P6) 42" x 55" - HATCH (CAST FLUSH) - 3" P5) 96" - MH FLAT TOP w/42"x55" Hatch F/G - 17" P4) 96" - MH RISER Custom Ht T/G - 67" P3) 96" - MH RISER T/G - 72" P2) 96" - MH RISER T/G - 54" P1) 96" - MH SEPARATE BASE-T EXT. 14" (142" OD) T/n - 12" 1) This Structure Includes a Cast-in Item - 42" x 55" Hatch (Supplied by Others) 4) JOINT WRAP - 12" WD x 096" MAC WRAP 4) 96" - Conseal CS-231 1.00" (Double) 3) PSX - 8QRS-S NYLO 1) PSX - 12-08 NYLO						0 lb 8820 lb 16574 lb 17851 lb 13452 lb 19580 lb 0 lb 0 lb 0 lb 20 lb 8 lb Structure Total: 76305 lb		Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,500 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. NO STEPS 5. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AT 45°, 135°, 225°, & 315°, 16" FROM TOP OF WALLS 6. INVERTS 1 & 2 OFFSET 13.125" FROM CENTER (26.25" CENTER-TO-CENTER)			
Rim: 963.5' Rim to Invert: 10.85' Slack: 0" Sump: 74.8" Step Position:											
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	960.25'	0°	-13.25"	4" DI	4.75"	PSX 8QRS-S NYLO	8"	8.33"	38"	-13.125"	
Invert 2	960.25'	0°	13.25"	4" DI	4.75"	PSX 8QRS-S NYLO	8"	8.33"	38"	13.125"	
Invert 3	958.5'	0°	0"	4" DI	4.75"	PSX 8QRS-S NYLO	8"	8.009"	17"	0"	
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											

RIGHT-SIDE UP VIEW (int. dimensions)

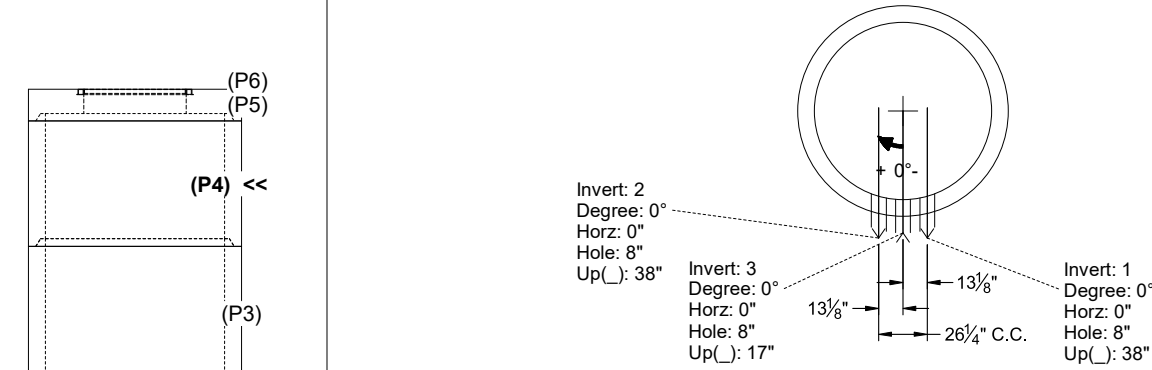

(P6)
(P5)
(P4) <<
(P3)
(P2)
(P1)

INSIDE WALL DIMENSIONS

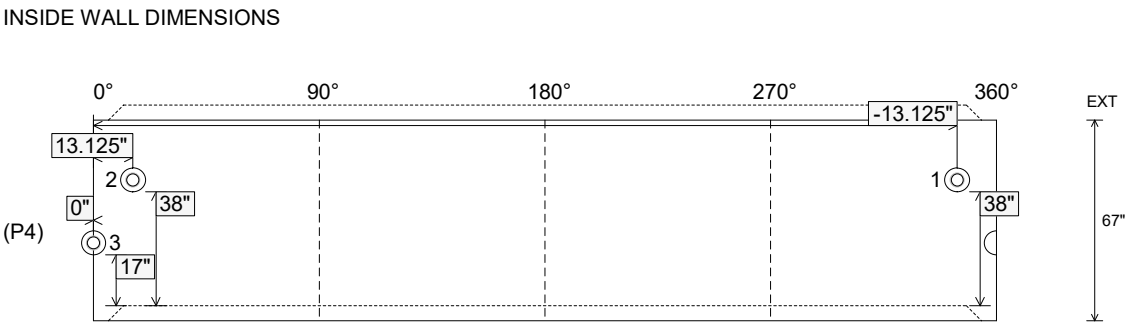

(P4)

Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: Groove	Wall Thickness: 9" Floor Height: 0"	Height (Int): 67" Height (Ext): 67"	Weight (Net): 16574 lb Volume (Net): 4.23cu.yd
----------------------------------	------------------------------------	--	--	---
