

Job Name: 26-1038 - Perryville & Junction City WW Improvements
Job Location: Danville, KY
Contractor: Connhurst, LLC

Plant: 100

5/6/2026 4:07:12 PM

Tech: Jared - A

PC: E. Bradley



Structure ID: 61038 (5)

P2 BX084096-08LD08SP

BX FLAT LID 8"W w/36"x36" HATCH F/F




- P3) 36" x 36" - HATCH (CAST FLUSH) - 0"
P2) 84" x 96" - BX FLAT LID 8"W w/36"x36" HATCH F/F - 8"
P1) 84" x 96" - BX BASE w/FLANGE 08W/08F/06EF F/n - 52"
1) This Structure Includes a Cast-in Item - 36" x 36" Hatch (Supplied by Others)
1) SPECIAL Internal Coating - Carboline 300M
1) SECONDARY POUR
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) LADDER (Alum.) - HALLIDAY L1B 48in Wall Mount Ladder
1) LADDER (Alum.) - HALLIDAY L1EAA Ladder Extension Safety Post
1) 84" x 96" - Con seal CS-102 1.00" (Double)
4) Hole - 8
250.01 SqFt) Carboline Bitumastic 300M [INT]

Structure Total:

0 lb
6695 lb
22872 lb
0 lb
0 lb
0 lb
0 lb
0 lb
50 lb
65 lb
0 lb
0 lb
0 lb
29682 lb

Structure Notes:

1. PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. 36" X 36" (35" X 35" CLEAR OPENING) HATCH SUPPLIED BY OTHERS - TO BE CAST INTO FLAT LID
5. 4" VENT PIPE SUPPLIED BY OTHERS
6. SPECIAL INTERNAL COATING REQUIRED - CARBOLINE 300M
7. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED AS SHOWN
8. TOP SURFACE TO RECEIVE LIGHT BRUSH FINISH

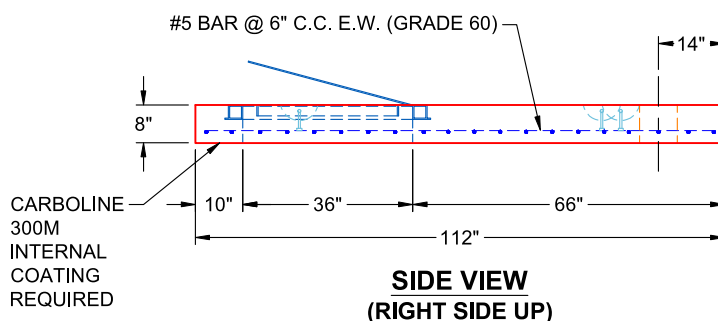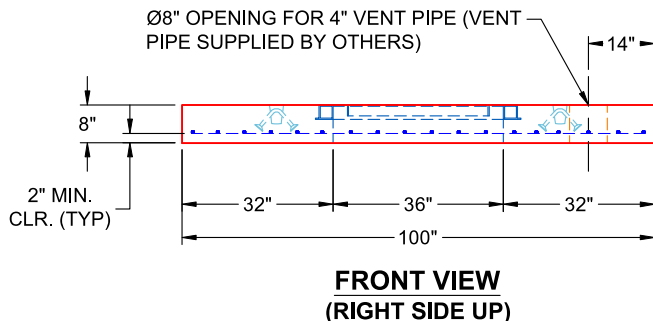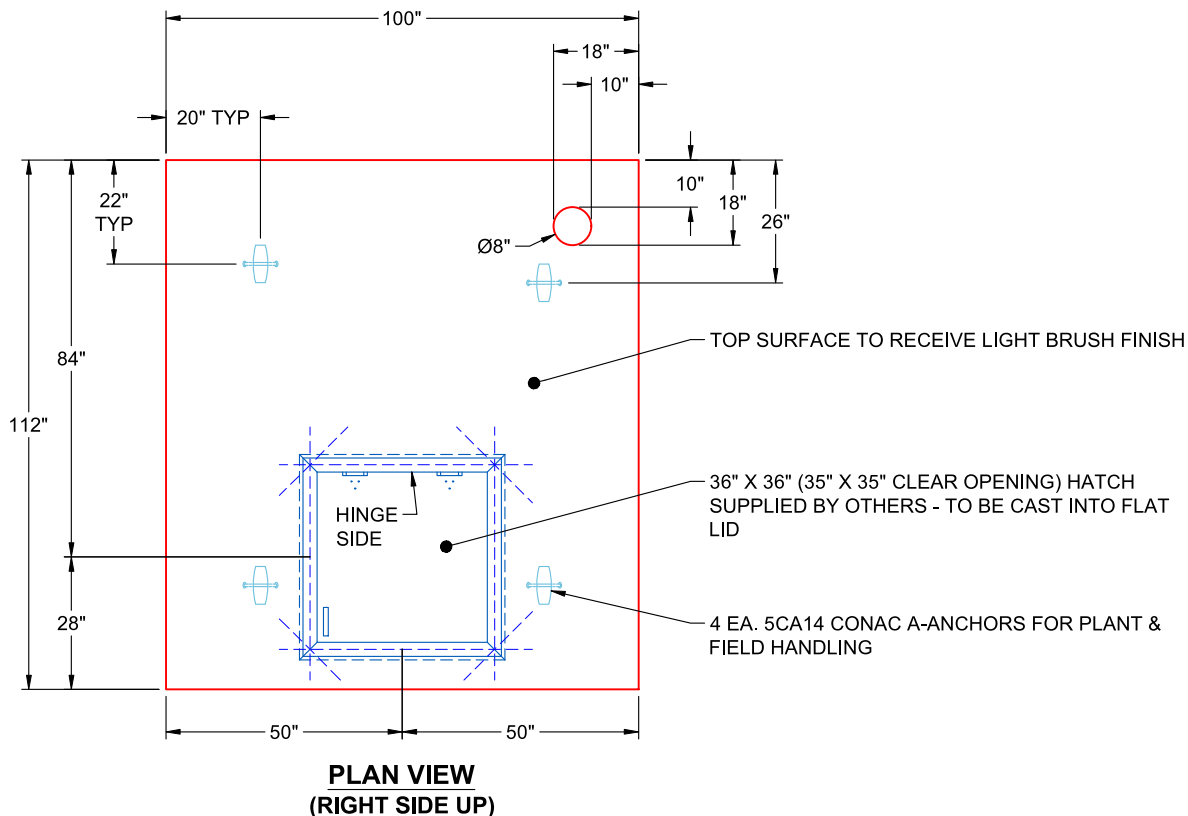

Coating (Int): Carboline Bitumastic 300M
Coating (Ext):

Seam Up: Flat
Seam Dn: Flat

Wall Thickness: 8"

Height (Ext): 8"

Weight (Net): 6695 lb
Volume (Net): 1.71cu.yd

Job Number:

26-1038

Job Name:

Perryville & Junction City WW
Improvements

Structure:

61038 (5)

Note:

36" x 36" (35" x 35" Clear Opening)
Hatch Supplied By Others To Be Cast
Into Flat Lid

Job Number:

26-1038

Job Name:

Perryville & Junction City WW
Improvements

Structure:

61038 (5)

Note:

This Structure Is To Receive An
Internal Coating of Carboline 300M
(Supplied By iCast)
