
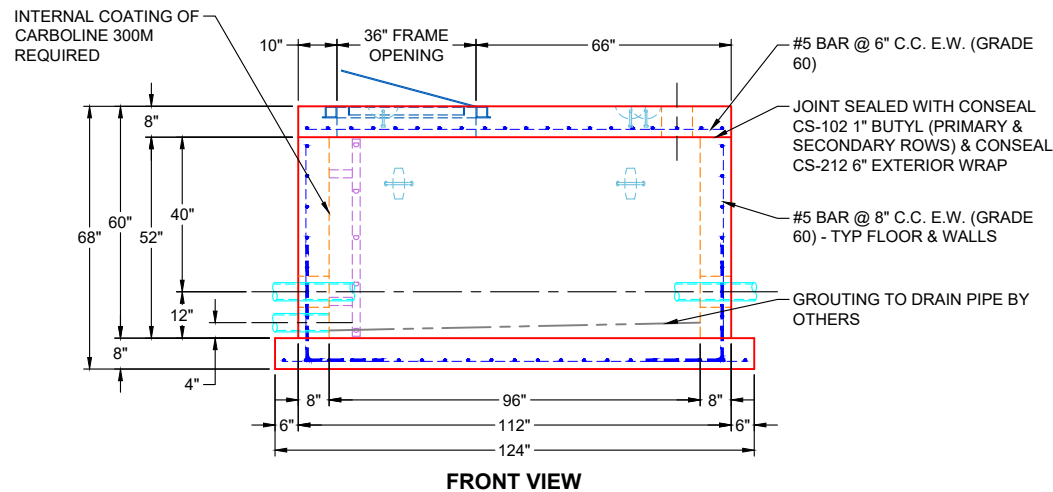


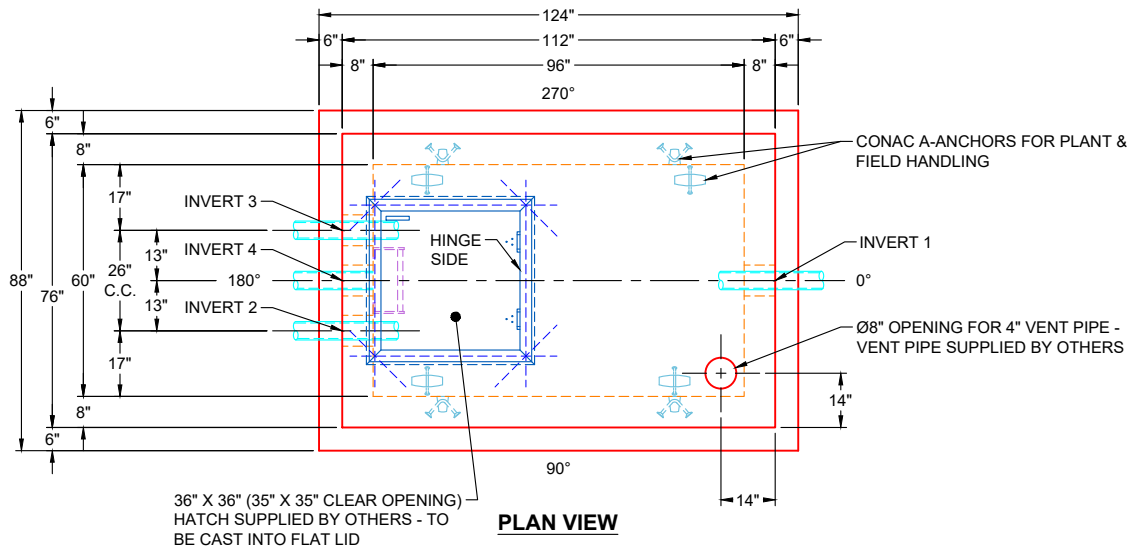


GENERAL NOTES:

1. MANUFACTURED PER ASTM C-913 SPECIFICATIONS
2. CONCRETE: 5,000 PSI AT 28 DAYS
3. REINFORCEMENT:
 - FLAT LID: #5 BAR @ 6" C.C. E.W. (GRADE 60)
 - BASE: #5 BAR @ 8" C.C. E.W. (GRADE 60)
4. WEIGHTS:

8" FLAT LID	4,890 LBS
52" BASE W/ 6" EXT. FLANGE	19,198 LBS
TOTAL WEIGHT	24,088 LBS
5. 36" X 36" (35" X 35" CLEAR OPENING) HATCH SUPPLIED BY OTHERS - TO BE CAST INTO FLAT LID
6. HALLIDAY L1B 4' LADDER & L1EAA SAFETY POST SUPPLIED BY ICAST
7. JOINT SEALANT: CONSEAL CS-102 - 1" (PRIMARY & SECONDARY ROWS) EXTERIOR WRAP: CONSEAL CS-212 - 6"
8. CARBONLINE 300M INTERNAL COATING REQUIRED
9. 4" VENT PIPE SUPPLIED BY OTHERS
10. OPENINGS TO BE GROUTED (BY OTHERS)

OPENINGS

PIPE ID	ELEV	ANGLE	PIPE	PIPE OD	HOLE	CONNECTOR	UP FROM BOTTOM
INVERT 1	840.83'	0°	4" DI	4.75"	8"	HOLE 8	8"
INVERT 2	840.83'	180°	4" DI	4.75"	8"	HOLE 8	8"
INVERT 3	840.83'	180°	4" DI	4.75"	8"	HOLE 8	8"
INVERT 4	840.17'	180°	4" DI	4.75"	8"	HOLE 8	0"

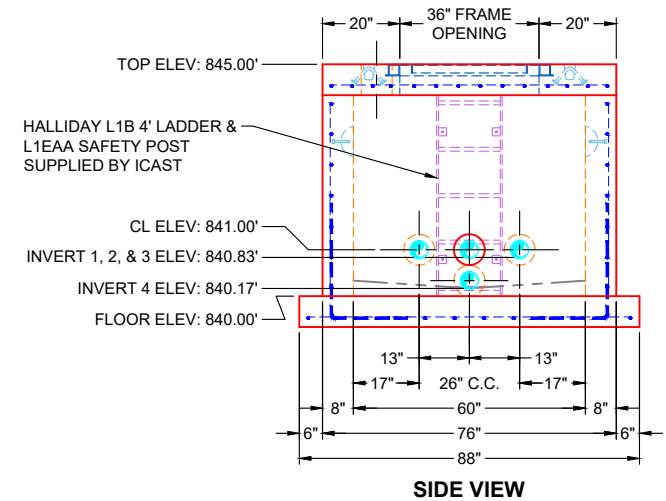

REVISION INFORMATION

REV. DATE: NO REVISIONS TO DATE



SUBMITTAL DRAWING: 60" X 96" VAULT (PERRYVILLE CITY HALL)

CUSTOMER: CONNHURST, LLC

PROJECT: PERRYVILLE & JUNCTION CITY WW IMPROVEMENTS

STRUCTURE: 61038 (6)

QUOTE/SALES ORDER NO: 26-1038

CHECKED BY: B. SMITH

DRAWN BY: K. CARDWELL

DATE: 05/04/26

SCALE: NTS

PG. 1 OF 1
