




Weight (Net): 18363 lb
Volume (Net): 4.69cu.yd


Job Name: 26-1038 - Perryville & Junction City WW Improvements Job Location: Danville, KY Contractor: Connhurst, LLC					Plant: 100 5/6/2026 4:05:53 PM		Tech: Jared - A PC: E. Bradley				
Structure ID: 61038 (7)											
P1 BX6072-08BAVF-EB					BX BASE w/FLANGE 08W/08F/06EF F/n						
P3) 36" x 36" - HATCH (CAST FLUSH) - 0" P2) 60" x 72" - BX FLAT LID 8"W w/36"x36" HATCH F/F - 8" P1) 60" x 72" - BX BASE w/FLANGE 08W/08F/06EF F/n - 64" 1) This Structure Includes a Cast-in Item - 36" x 36" Hatch (Supplied by Others) 1) SECONDARY POUR 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) SPECIAL Internal Coating - Carboline 300M 1) LADDER (Alum.) - HALLIDAY L1B 60in Wall Mount Ladder 1) LADDER (Alum.) - HALLIDAY L1EAA Ladder Extension Safety Post 1) 60" x 72" - Conseal CS-102 1.00" (Double) 3) Hole - 12 1) Hole - 8 185.34 SqFt) Carboline Bitumastic 300M [INT]					0 lb 3665 lb 18363 lb 0 lb 0 lb 0 lb 0 lb 0 lb 50 lb 65 lb 0 lb 0 lb 0 lb 0 lb Structure Total: 22143 lb		Structure Notes: 1. PER ASTM C-913 SPECIFICATIONS 2. CONCRETE: 5,000 PSI AT 28 DAYS 3. REINFORCEMENT: #5 BAR @ 8" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP) 4. FLOOR GROUTING TO DRAIN PIPE BY OTHERS 5. HALLIDAY L1B 5' WALL MOUNT LADDER & L1EAA SAFETY POST SUPPLIED BY ICAST 6. SPECIAL INTERNAL COATING REQUIRED - CARBOLINE 300M 7. LIFTERS: 4 EA. 5CA14 CONAC A-ANCHORS FOR PLANT & FIELD HANDLING - INSTALLED IN 90° & 270° WALLS, 16" FROM TOP OF WALLS				
Rim: 844'		Rim to Invert: 5.83'		Slack: 0"		Sump: 2"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset	
Invert 1	838.87'	0°	38"	8" DI	9"	Hole 12	12"	12"	8.5"	0"	
Invert 2	838.87'	180°	20"	8" DI	9"	Hole 12	12"	12"	8.5"	-18"	
Invert 3	838.87'	180°	56"	8" DI	9"	Hole 12	12"	12"	8.5"	18"	
Invert 4	838.17'	180°	38"	4" DI	4.75"	Hole 8	8"	8"	0"	0"	
Invert 5											

FIRST POUR (FLOOR):
5,907 LBS


SECOND POUR (WALLS):
12,456 LBS

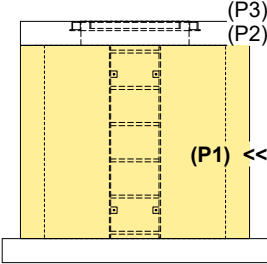

RIGHT-SIDE UP VIEW (int. dimensions)

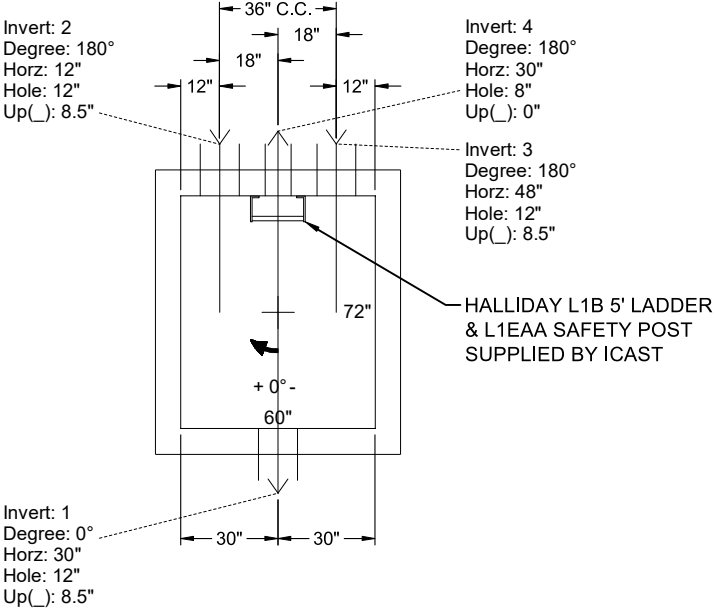

INSIDE WALL DIMENSIONS

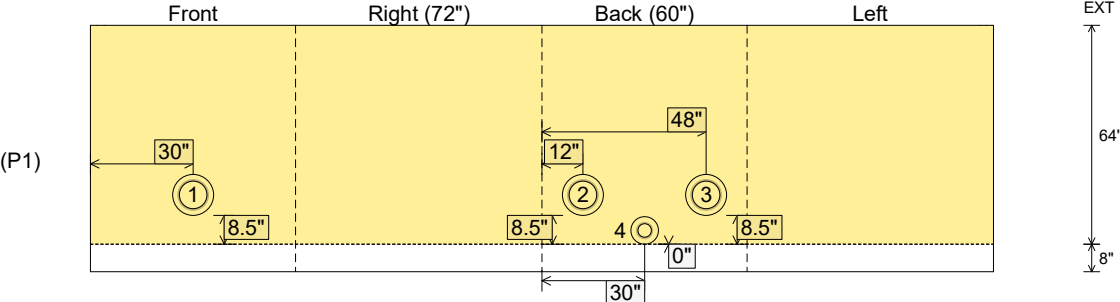

Coating (Int): Carboline Bitumastic 300M Coating (Ext):	Seam Up: Flat Seam Dn: n/a	Wall Thickness: 8" Floor Height: 8"	Height (Int): 64" Height (Ext): 72"	Weight (Net): 18363 lb Volume (Net): 4.69cu.yd
--	-------------------------------	--	--	---

Job Number:

26-1038

Job Name:

Perryville & Junction City WW
Improvements

Structure:

61038 (7)

Note:

This Structure Is To Receive An
Internal Coating of Carboline 300M
(Supplied By iCast)
