

Job Name: 26-1038 - Perryville & Junction City WW Improvements
Job Location: Danville, KY
Contractor: Connhurst, LLC

Plant: 100

4/27/2026 3:59:36 PM

Tech: Jared - A

PC: E. Bradley



Structure ID: 61038 (8)

P2 MH060TS13-48ECC

MH Transition Slab 48" Hole T/G



- P5) 24" - CASTING HEIGHT - 7"
P4) 48" - ECC CONE w/ 24" HOLE F/G - 30"
P3) 48" - MH RISER T/G - 36"
P2) 60" - MH Transition Slab 48" Hole T/G - 13"
P1) 60" - MH BASE T/n - 36"
1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212
1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.)
1) 60" - MH INVERT CHANNEL - FULL HEIGHT
1) CASTING - HOE MC-315 F/C Sanitary
1) 60" - Conseal CS-102 1.00" (Double)
2) 48" - Conseal CS-102 1.00" (Double)
3) PSX - 12-08 NYLO
9) MH Step ML-10-TDS-NCR - 10"

0 lb
2050 lb
2515 lb
1928 lb
6320 lb
0 lb
0 lb
2692 lb
258 lb
0 lb
0 lb
24 lb
0 lb

Structure Total: 15786 lb

Structure Notes:

1. PER ASTM C-478 SPECIFICATIONS
2. CONCRETE: 4,000 PSI AT 28 DAYS
3. REINFORCEMENT: #5 BAR @ 6" C.C. E.W. (GRADE 60) - 2" MIN. REBAR CLEARANCE (TYP)
4. HOE MC-315 FRAME & COVER "SANITARY" SUPPLIED BY ICAST
5. LIFTERS: 3 EA. WRA016 CONAC WIRE ROPE ANCHORS
6. TOP SURFACE TO RECEIVE FLOATED FINISH

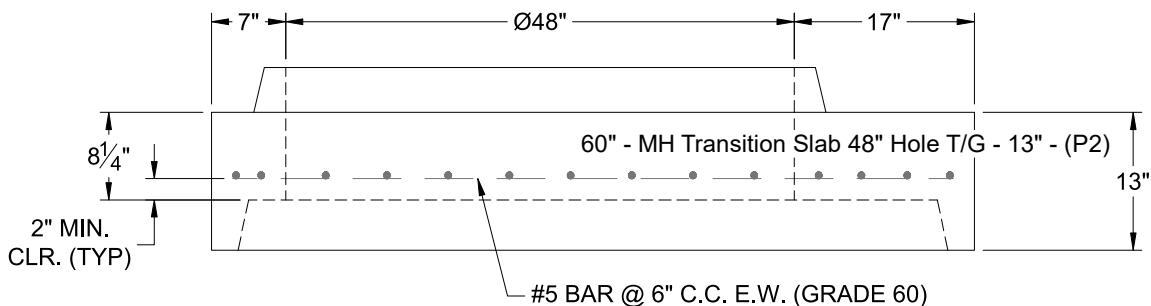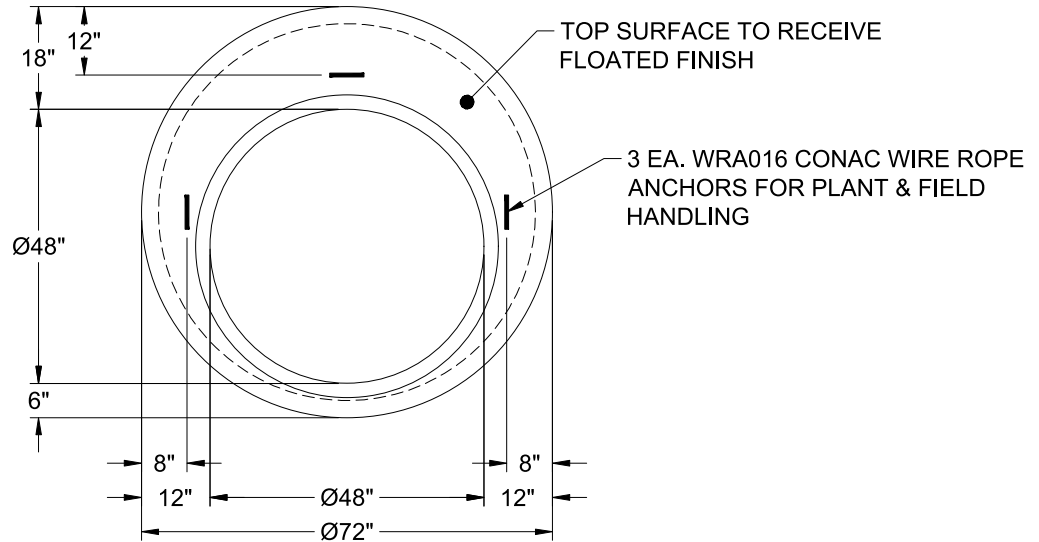

Coating (Int):
Coating (Ext):

Seam Up: Tongue
Seam Dn: Groove

Wall Thickness: 6"

Height (Ext): 13"

Weight (Net): 1928 lb
Volume (Net): 0.49cu.yd
