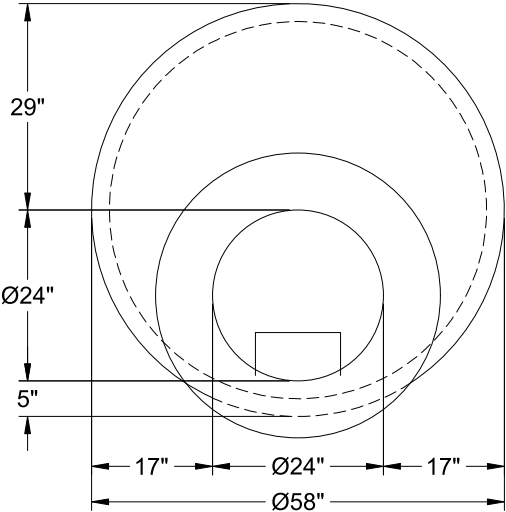



Job Name: 26-1038 - Perryville & Junction City WW Improvements Job Location: Danville, KY Contractor: Connhurst, LLC		Plant: 100 4/27/2026 3:59:36 PM	Tech: Jared - A PC: E. Bradley	
Structure ID: 61038 (8)				
P4 MH048CN30		ECC CONE w/ 24" HOLE F/G		
P5) 24" - CASTING HEIGHT - 7" P4) 48" - ECC CONE w/ 24" HOLE F/G - 30" P3) 48" - MH RISER T/G - 36" P2) 60" - MH Transition Slab 48" Hole T/G - 13" P1) 60" - MH BASE T/n - 36" 1) JOINT WRAP - 0.065"x6"x50' CONSEAL CS212 1) JOINT WRAP PRIMER - CONSEAL CS-75 (1 gal.) 1) 60" - MH INVERT CHANNEL - FULL HEIGHT 1) CASTING - HOE MC-315 F/C Sanitary 1) 60" - Conseal CS-102 1.00" (Double) 2) 48" - Conseal CS-102 1.00" (Double) 3) PSX - 12-08 NYLO 9) MH Step ML-10-TDS-NCR - 10"		0 lb 2050 lb 2515 lb 1928 lb 6320 lb 0 lb 0 lb 2692 lb 258 lb 0 lb 0 lb 24 lb 0 lb ----- Structure Total: 15786 lb	Structure Notes: 1. PER ASTM C-478 SPECIFICATIONS 2. CONCRETE: 4,000 PSI AT 28 DAYS 3. REINFORCEMENT: PER ASTM A615 4. STEPS REQUIRED 5. HOE MC-315 FRAME & COVER "SANITARY" SUPPLIED BY ICAST	
				
 48" - ECC CONE w/ 24" HOLE F/G - 30" - (P4)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 30"	Weight (Net): 2050 lb Volume (Net): 0.41cu.yd
