



Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply					Plant: 100 9/8/2026 9:08:38 AM		Tech: J. Horsley PC: E. Bradley			
Structure ID: SS2 (10)										
P1 MH048BA30CDARED					MH BASE w/ConBlock-CDA Red T/n					
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 1297 lb 1677 lb 3330 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 7760 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 567.51' Rim to Invert: 7.11' Slack: 2.32" Sump: 2" Step Position: 135°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	560.4'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	560.6'	270°	136.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										

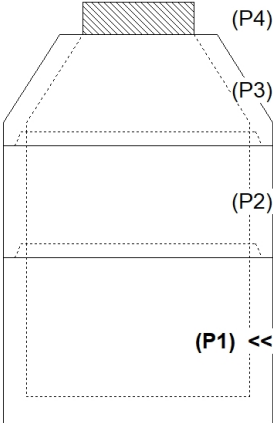


(P1) <<


RIGHT-SIDE UP VIEW (int. dimensions)

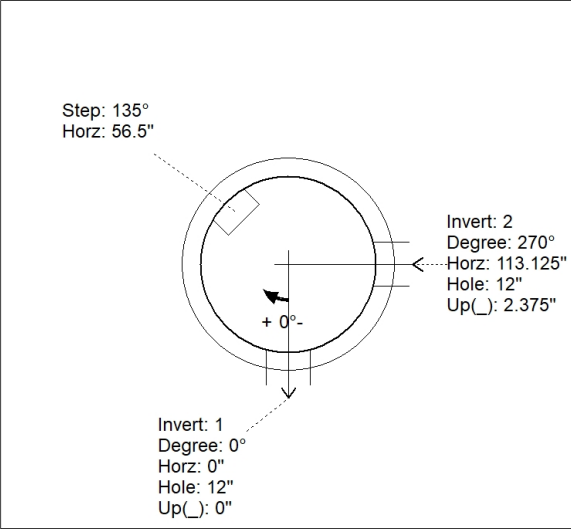

UPSIDE-DOWN VIEW (int. dimensions)

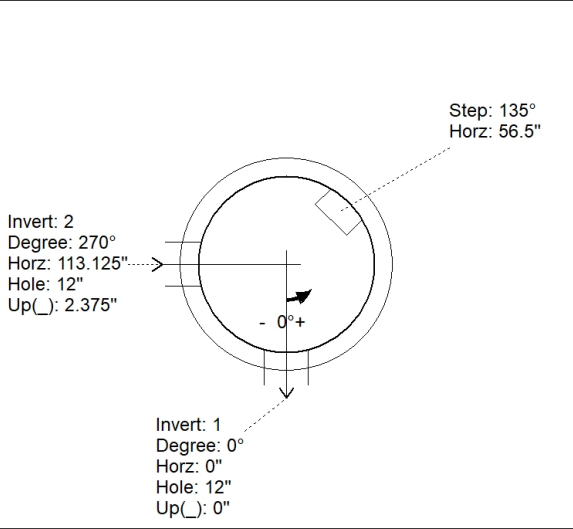


INSIDE WALL DIMENSIONS

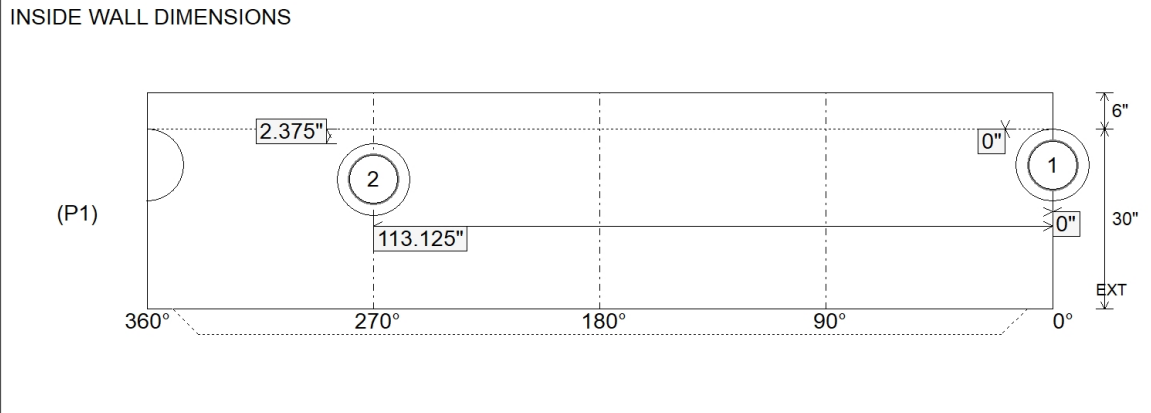


Coating (Int): Coating (Ext):	Seam Up: Tongue Seam Dn: n/a	Wall Thickness: 5" Floor Height: 6"	Height (Int): 30" Height (Ext): 36"	Weight (Net): 3330 lb Volume (Net): 0.85cu.yd
----------------------------------	---------------------------------	--	--	--

Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply					Plant: 100 9/8/2026 9:08:38 AM		Tech: J. Horsley PC: E. Bradley			
Structure ID: SS2 (10)										
P1A MH048BA30CDARED					MH BASE w/ConBlock-CDA Red T/n					
P4) 24" - CASTING HEIGHT - 7" P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 2) 48" - ConSeal CS-102 1.00" (Double) 1) 24" - ConSeal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 6) MH Step ML-10-TDS-NCR - 10"					0 lb 1297 lb 1677 lb 3330 lb 1440 lb 0 lb 0 lb 16 lb 0 lb ----- Structure Total: 7760 lb		Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.			
Rim: 567.51' Rim to Invert: 7.11' Slack: 2.32" Sump: 2" Step Position: 135°										
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up ()	Offset
Invert 1	560.4'	0°	0"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	0"	0"
Invert 2	560.6'	270°	136.625"	8" PVC SDR35	8.5"	PSX 12-08 NYLO	12"	12.129"	2.375"	0"
Invert 3										
Invert 4										
Invert 5										
Invert 6										
Invert 7										
Invert 8										


RIGHT-SIDE UP VIEW (int. dimensions)

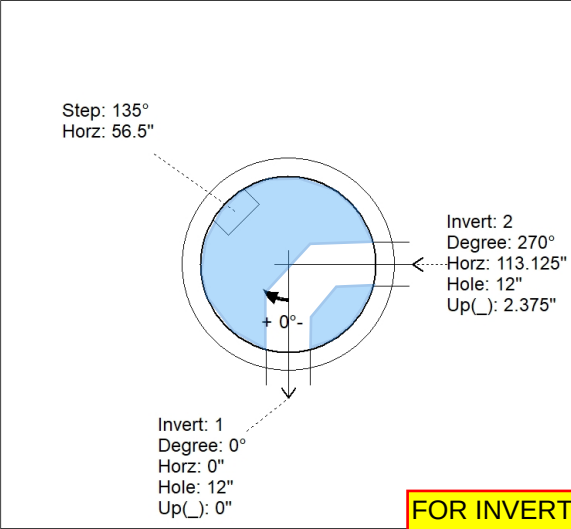

UPSIDE-DOWN VIEW (int. dimensions)

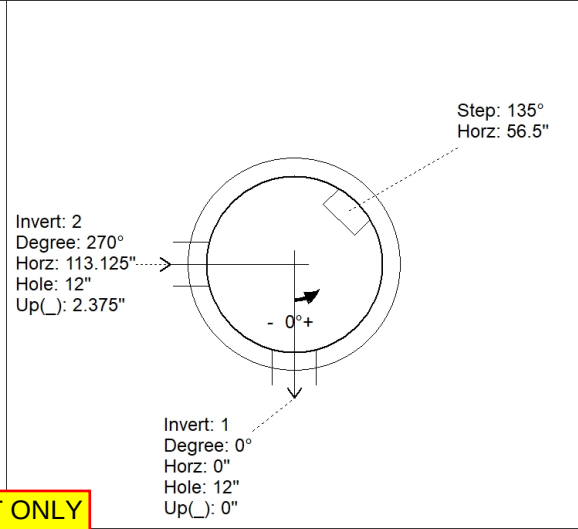


FOR INVERT ONLY

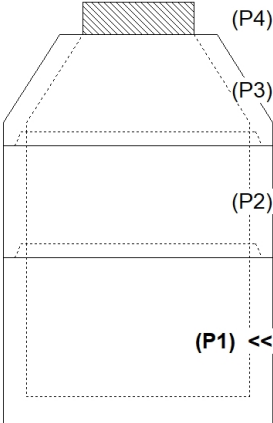

(P1) <<

INSIDE WALL DIMENSIONS

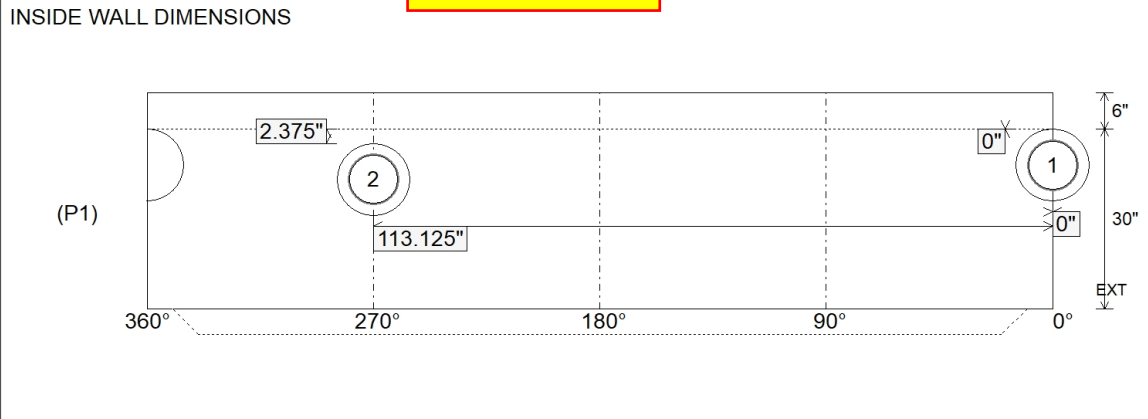

Coating (Int):	Seam Up: Tongue	Wall Thickness: 5"	Height (Int): 30"	Weight (Net): 3330 lb
Coating (Ext):	Seam Dn: n/a	Floor Height: 6"	Height (Ext): 36"	Volume (Net): 0.85cu.yd
