

Job Name: 26-1057 - The Courtside Enclave Final SP  
Job Location: Antioch, TN  
Contractor: Hayes Pipe Supply

Plant: 100

9/8/2026 9:10:08 AM

Tech: J. Horsley

PC: E. Bradley



## Structure ID: SS2 (10)

### P3 MH048CCN24CDARED

### CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G

- P4) 24" - CASTING HEIGHT - 7"  
P3) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24"  
P2) 48" - MH RISER w/ConBlock-CDA Red T/G - 24"  
P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30"  
1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT  
2) 48" - ConSeal CS-102 1.00" (Double)  
1) 24" - ConSeal CS-102 1.00" (Double)  
2) PSX - 12-08 NYLO  
6) MH Step ML-10-TDS-NCR - 10"


Structure Total: 7760 lb

#### Structure Notes:


1. PER ASTM C478 SPECIFICATIONS.
2. CONCRETE = 4,000 PSI AT 28 DAYS.
3. ADMIXTURE = CONBLOCK CDA RED.
4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR).

REINFORCING PER ASTM A615 (GRADE 60).

- CONE (As .12)
- RISER/WALLS (As .12)
- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

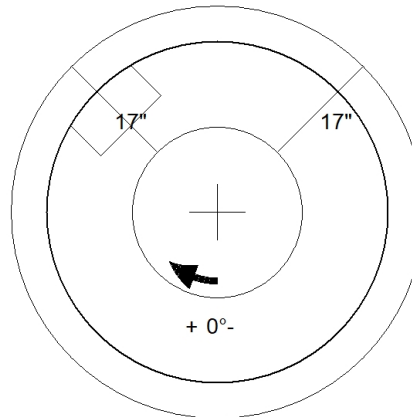

48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" - (P3)



Coating (Int):  
Coating (Ext):

Seam Up: Flat  
Seam Dn: Groove

Wall Thickness: 5"

Height (Ext): 24"

Weight (Net): 1297 lb  
Volume (Net): 0.33cu.yd
