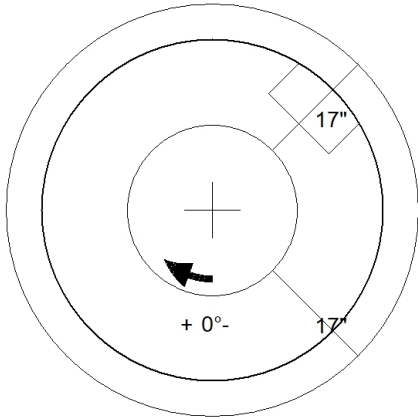



Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply		Plant: 100 9/8/2026 9:10:08 AM	Tech: J. Horsley PC: E. Bradley	
Structure ID: SS3 (11)				
P2 MH048CCN24CDARED		CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G		
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 30" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 2) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 1297 lb 3330 lb 1440 lb 0 lb 0 lb 0 lb 16 lb 0 lb ----- 6286 lb Structure Total:	<u>Structure Notes:</u> . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR). . REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Groove	Wall Thickness: 5"	Height (Ext): 24"	Weight (Net): 1297 lb Volume (Net): 0.33cu.yd
