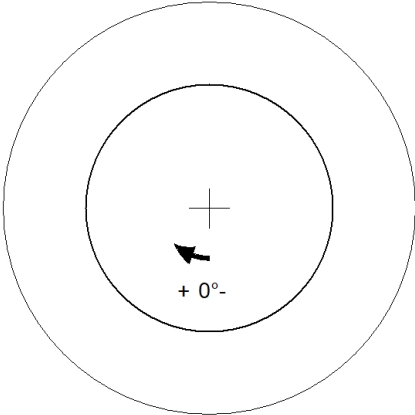


Job Name: 26-1057 - The Courtside Enclave Final SP		Plant: 100	Tech: J. Horsley	
Job Location: Antioch, TN		9/8/2026 9:10:09 AM	PC: E. Bradley	
Contractor: Hayes Pipe Supply				
Structure ID: SS5 (13)				
P3 GR3CDARED		GRADE RING w/ConBlock-CDA Red F/F		
P4) 24" - CASTING HEIGHT - 7" P3) 24" - GRADE RING w/ConBlock-CDA Red F/F - 3" P2) 48" - CON CONE w/24" HOLE, w/ConBlock-CDA Red F/G - 24" P1) 48" - MH BASE w/ConBlock-CDA Red T/n - 24" 1) 48" - MH INVERT CHANNEL w/ConBlock-CDA Red - FULL HEIGHT 1) 48" - Conseal CS-102 1.00" (Double) 1) 24" - Conseal CS-102 1.00" (Double) 1) PSX - 12-08 NYLO 4) MH Step ML-10-TDS-NCR - 10"		0 lb 202 lb 1297 lb 2959 lb 1440 lb 0 lb 0 lb 8 lb 0 lb ----- 5906 lb Structure Total:	Structure Notes: 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,000 PSI AT 28 DAYS. 3. ADMIXTURE = CONBLOCK CDA RED. 4. CASTING (JBS-1150 F/C) SUPPLIED BY CONTRACTOR). REINFORCING PER ASTM A615 (GRADE 60). - CONE (As .12) - RISER/WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
24" - GRADE RING w/ConBlock-CDA Red F/F - 3" - (P3)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 8"	Height (Ext): 3"	Weight (Net): 202 lb Volume (Net): 0.05cu.yd
