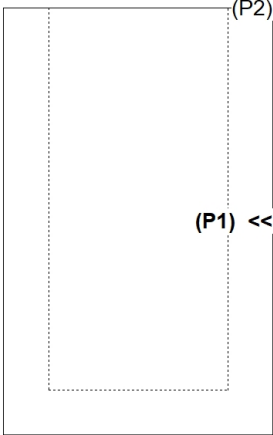
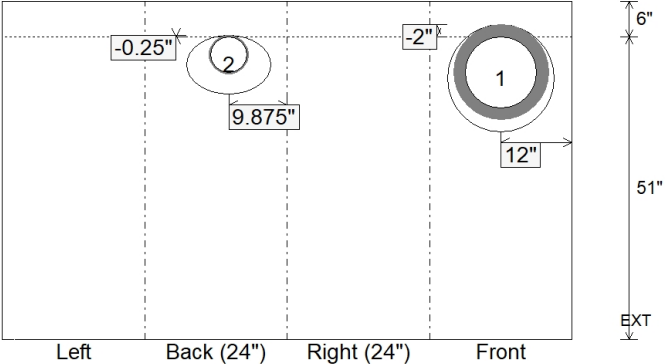


Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply					Plant: 100 9/8/2026 9:08:36 AM		Tech: J. Horsley PC: E. Bradley				
Structure ID: ST1 (3)											
P1 BX24240606VF		BOX BASE 6inW, 6inF, Variable Ht F/n									
P2) 24" x 24" - CASTING HEIGHT - 0" P1) 24" x 24" - BOX BASE 6inW, 6inF, Variable Ht F/n - 51" 1) 24" x 24" - Conseal CS-102 1.00" 1) Hole - 18 1) Hole - 10					0 lb 3550 lb 0 lb 0 lb 0 lb Structure Total: 3550 lb		<u>Structure Notes:</u> 1. PER ASTM C913 SPECIFICATIONS. 2. CONCRETE = 4,500 PSI AT 28 DAYS. 3. TRASHRACK SUPPLIED BY CONTRACTOR. .. REINFORCING PER ASTM A615 (GRADE 60). - WALLS (As .31) #5 BARS AT 12" C.C.E.W. - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.				
Rim: 567.75'		Rim to Invert: 4.25'		Slack: 0"		Sump: 0"		Step Position:			
Position	Elev	Angle	Ext. (cw)	Pipe	Pipe OD	Connector	Hole	Horz Size	Up (_)	Offset	
Invert 1	563.5'	0°	18"	12" RCP B WALL	16"	Hole 18	18"	18"	-2"	0"	
Invert 2	563.5'	225°	21.875"	6" PVC SCH40	6.625"	Hole 10	10"	14.142"	-0.25"	-10"	
Invert 3											
Invert 4											
Invert 5											
Invert 6											
Invert 7											
Invert 8											
RIGHT-SIDE UP VIEW (int. dimensions) UPSIDE-DOWN VIEW (int. dimenions) INSIDE WALL DIMENSIONS											
  											
Coating (Int): Coating (Ext):				Seam Up: Flat Seam Dn: n/a		Wall Thickness: 6" Floor Height: 6"		Height (Int): 51" Height (Ext): 57"		Weight (Net): 3550 lb Volume (Net): 0.91cu.yd	
