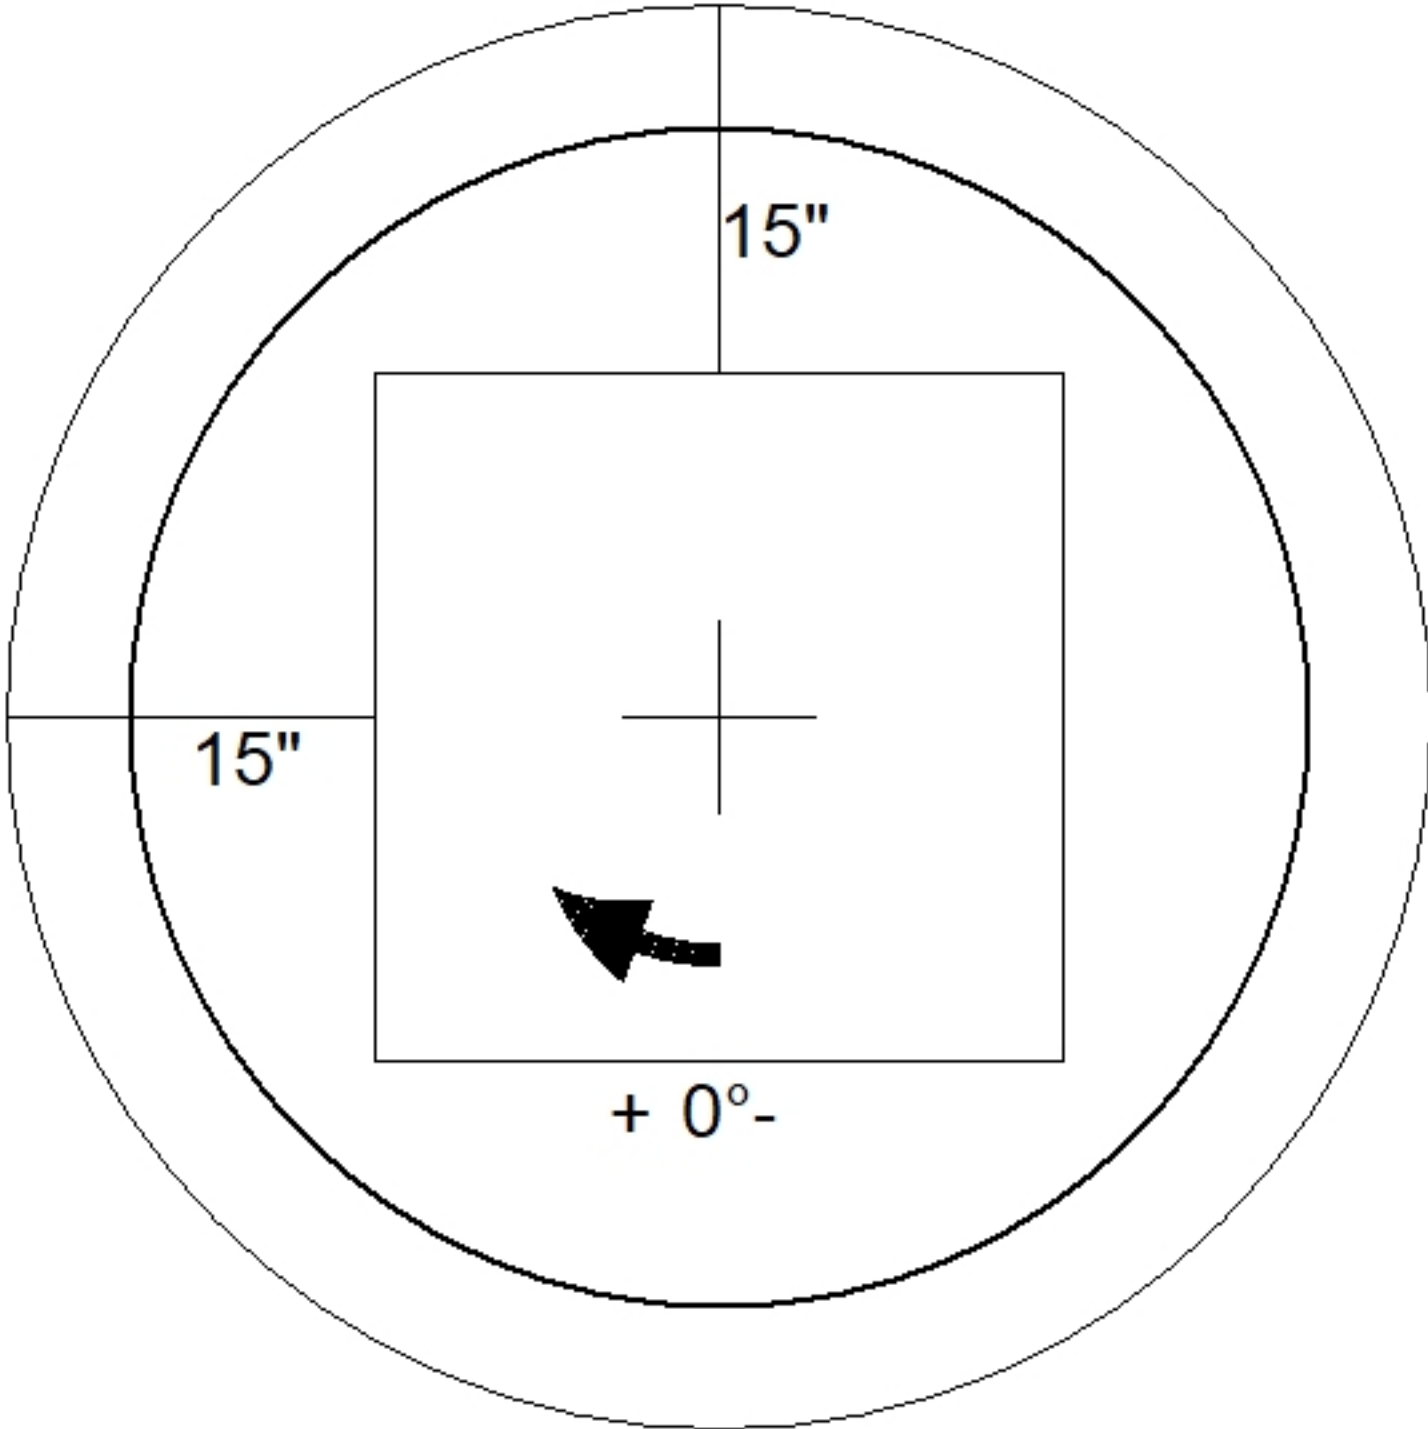


Job Name: 26-1057 - The Courtside Enclave Final SP Job Location: Antioch, TN Contractor: Hayes Pipe Supply		Plant: 100 9/9/2026 1:09:07 PM	Tech: J. Horsley PC: E. Bradley	
Structure ID: ST3 (5)				
P2 MH048LD07-28SQ		MH FLAT TOP w/28"x28" Hole F/F		
P3) 28" x 28" - CASTING HEIGHT - 6" P2) 48" - MH FLAT TOP w/28"x28" Hole F/F - 7" P1) 48" - MH BASE Custom Ht F/n - 46" 1) 48" - Conseal CS-102 1.00" 2) Hole - 22 4) MH Step ML-10-TDS-NCR - 10"		0 lb 1091 lb 4214 lb 0 lb 0 lb 0 lb ----- Structure Total: 5306 lb	<u>Structure Notes:</u> . 1. PER ASTM C478 SPECIFICATIONS. 2. CONCRETE = 4,00 PSI AT 28 DAYS. 3. CASTING (JBS 4310 F/G) SUPPLIED BY CONTRACTOR. . REINFORCING PER ASTM A615 (GRADE 60). - TOP SLAB = H2O LOADING. - WALLS (As .12) - FLOOR (As .31) #5 BARS AT 12" C.C.E.W.	
				
48" - MH FLAT TOP w/28"x28" Hole F/F - 7" - (P2)				
Coating (Int): Coating (Ext):	Seam Up: Flat Seam Dn: Flat	Wall Thickness: 5"	Height (Ext): 7"	Weight (Net): 1091 lb Volume (Net): 0.28cu.yd
