

Contractor: Hayes Pipe Supply

Plant: 100




Slack: 0.09"


- FLOOR (As .31) #5 BARS AT 12" C.C.E.W.

P3) 28" x 28" - CASTING HEIGHT - 6"
P2) 48" - MH FLAT TOP w/28"x28" Hole F/G - 12"
P1) 48" - MH BASE T/n - 42"
1) 48" - Conseal CS-102 1.00"
2) Hole - 22
3) MH Step ML-10-TDS-NCR - 10"


Structure Total: 5303 lb

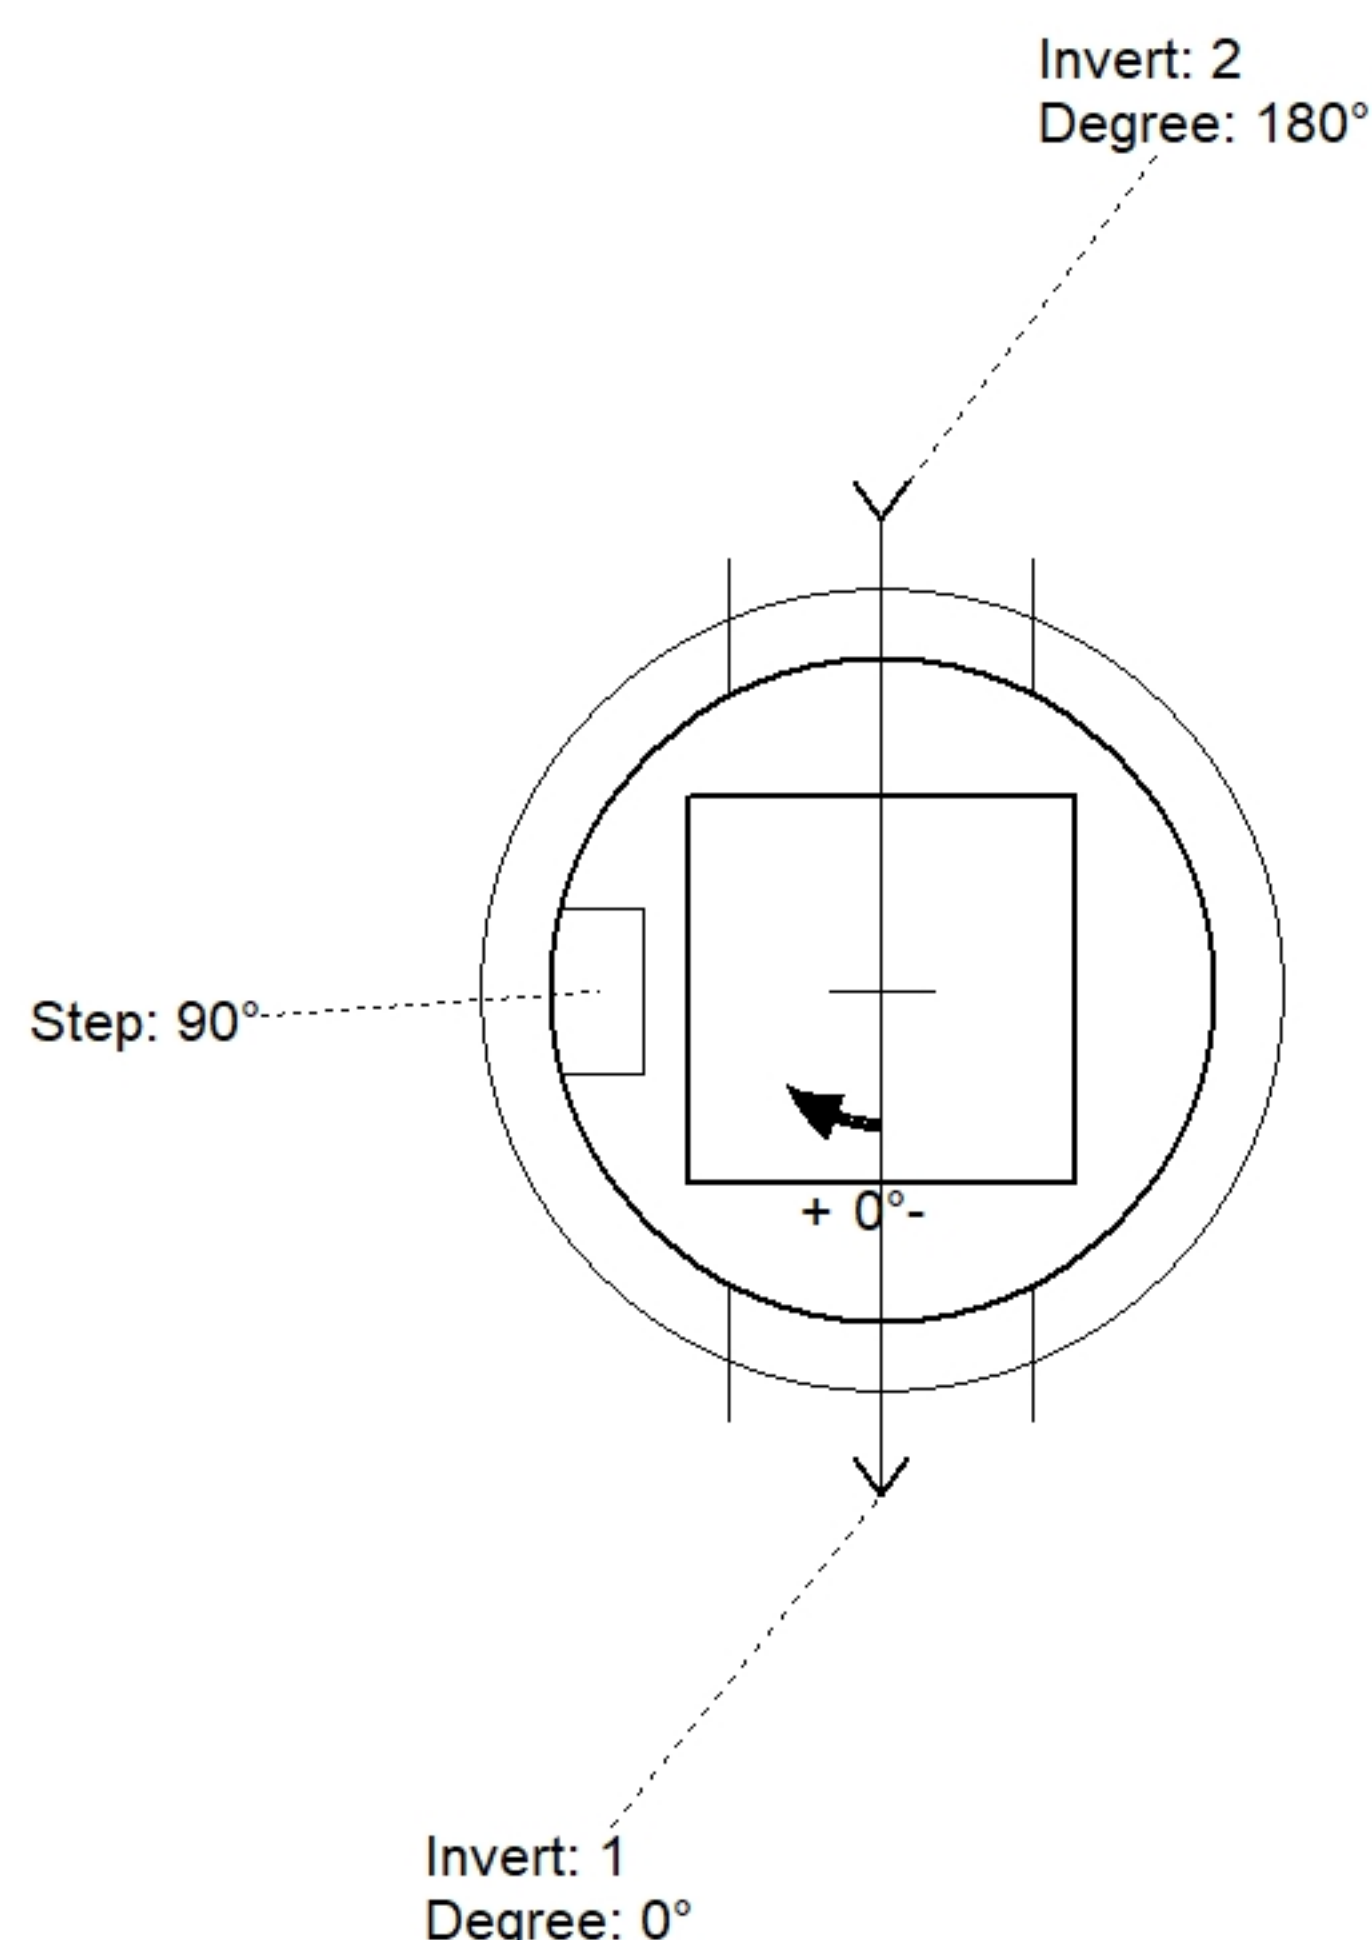

Position	Elev	Angle	Pipe	Pipe OD	Hole	Connector	Up (⌵)	Ref
Rim	579.52'							
Reducer								
Invert 1	574.7'	0°	15" RCP B WALL	19.5"	22"	Hole 22	0"	P1
Invert 2	574.8'	180°	15" RCP B WALL	19.5"	22"	Hole 22	1.25"	P1
Invert 3								
Invert 4								
Invert 5								
Invert 6								
Invert 7								
Invert 8								

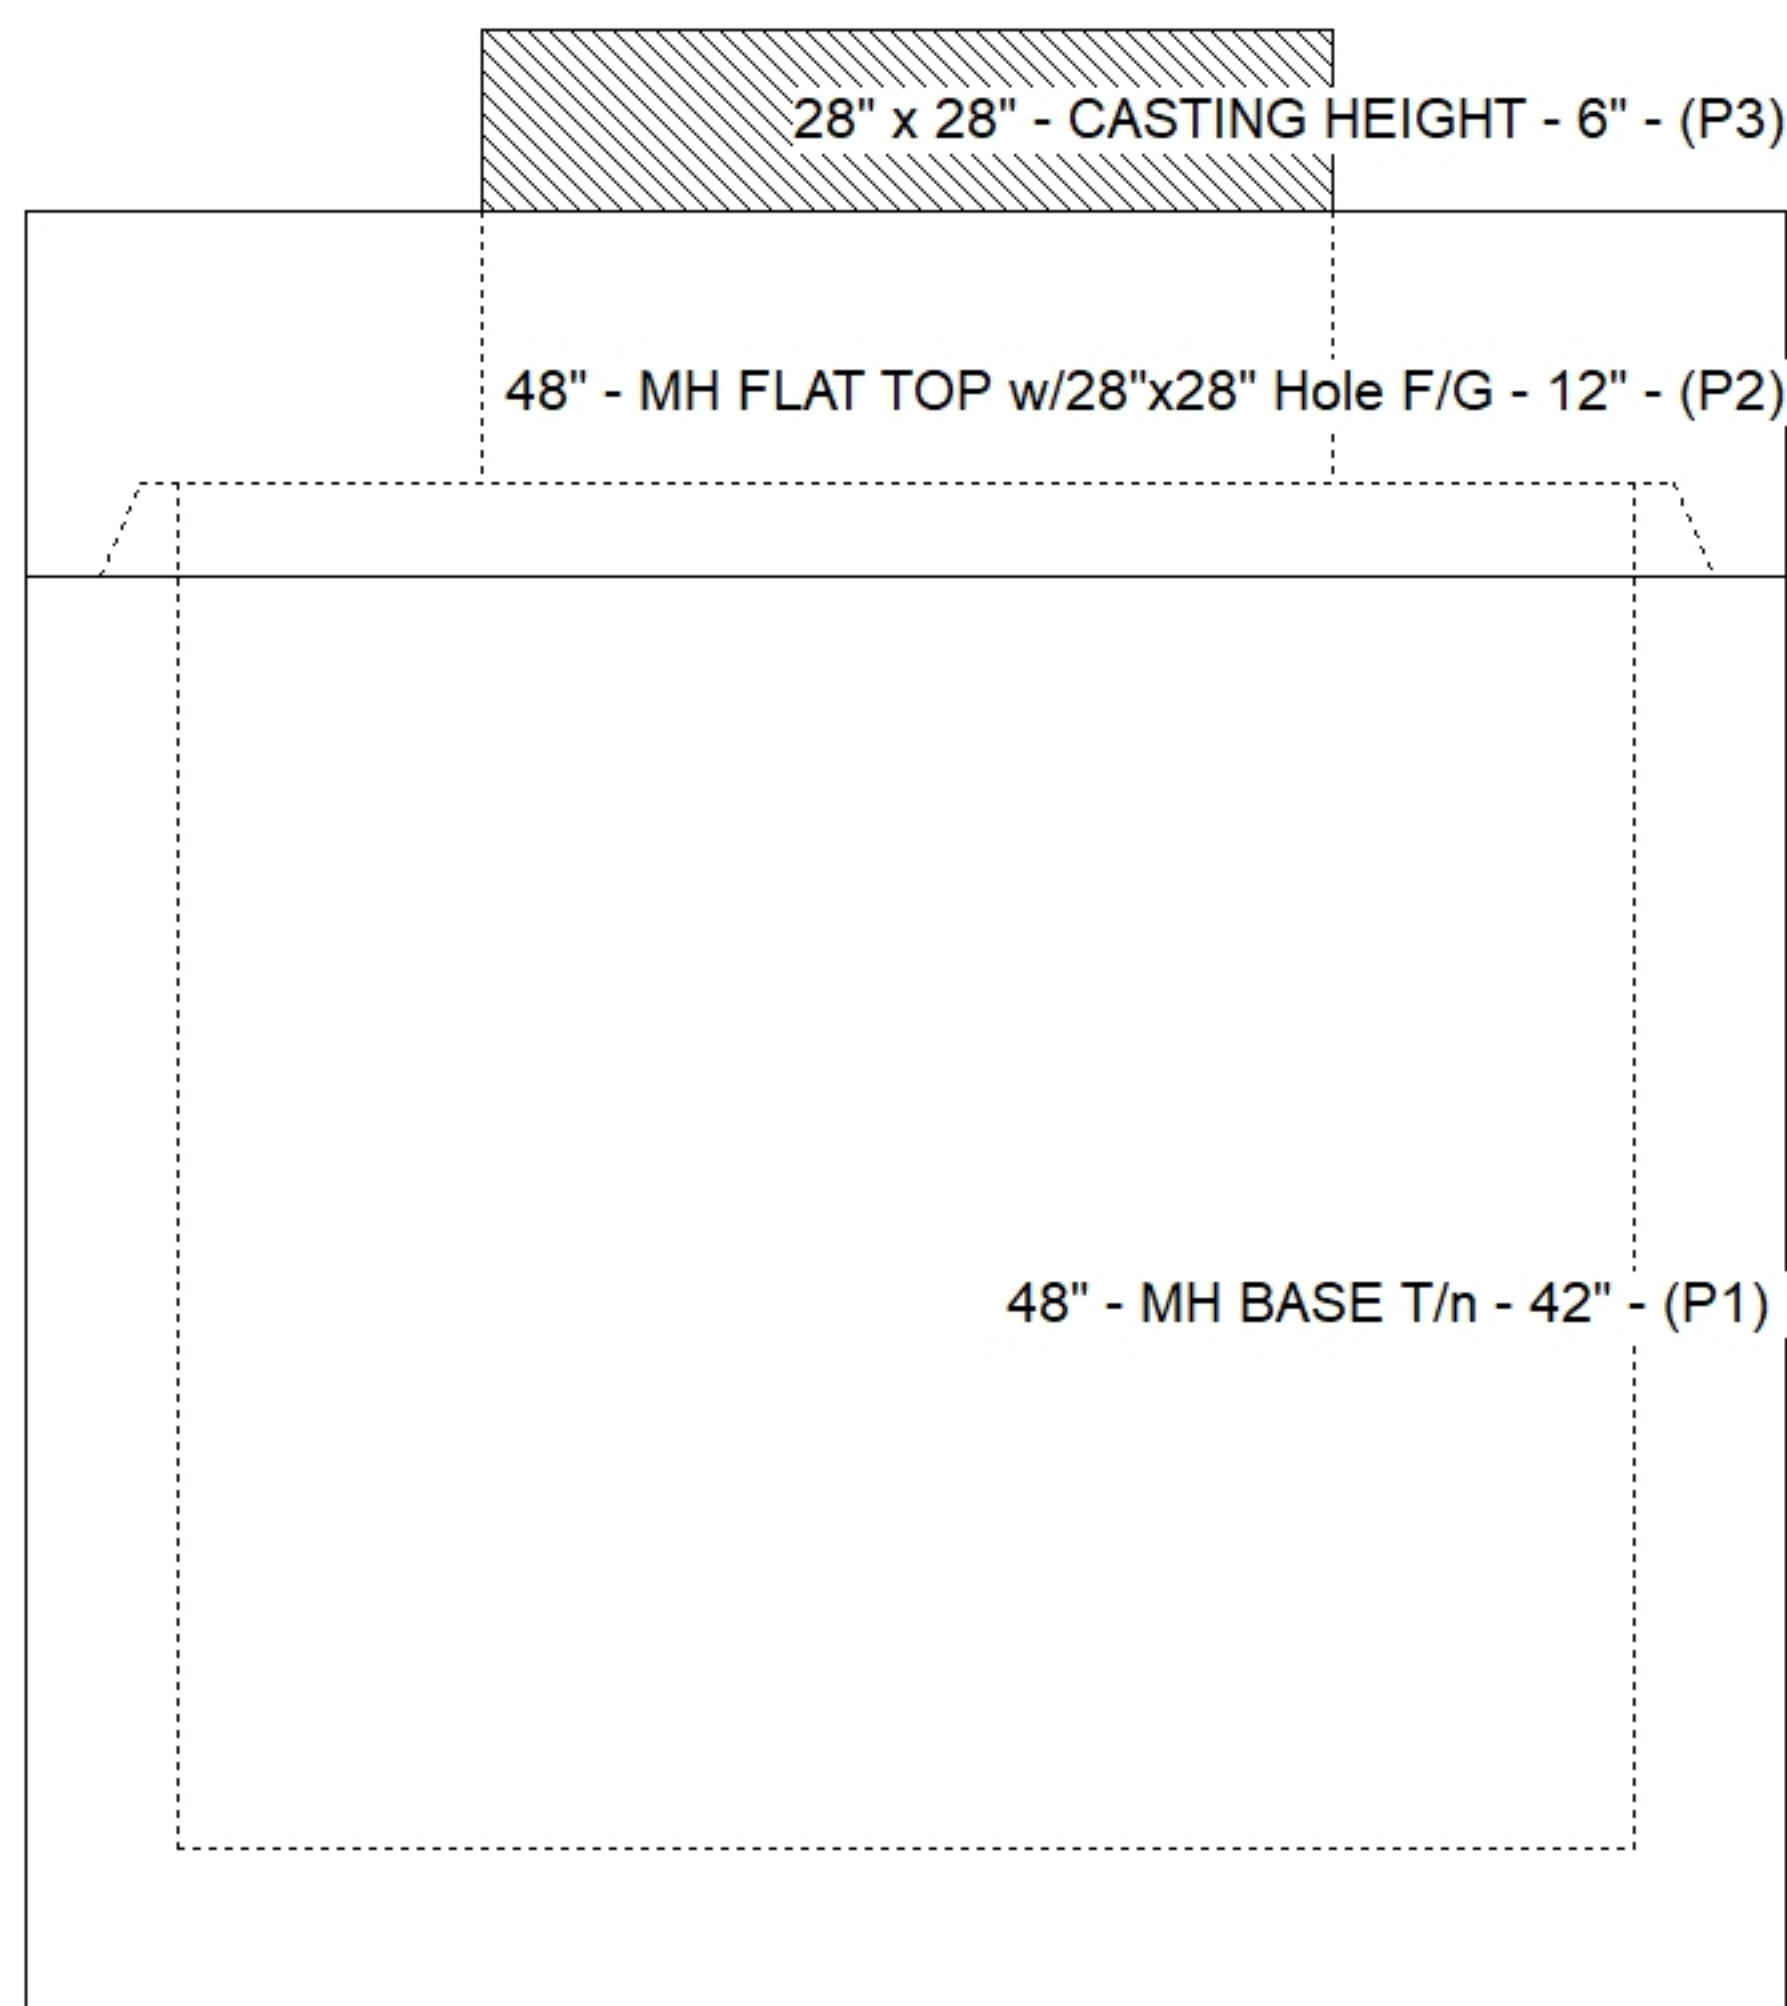

Cast (Int. Dim.) - Interior Dimensions

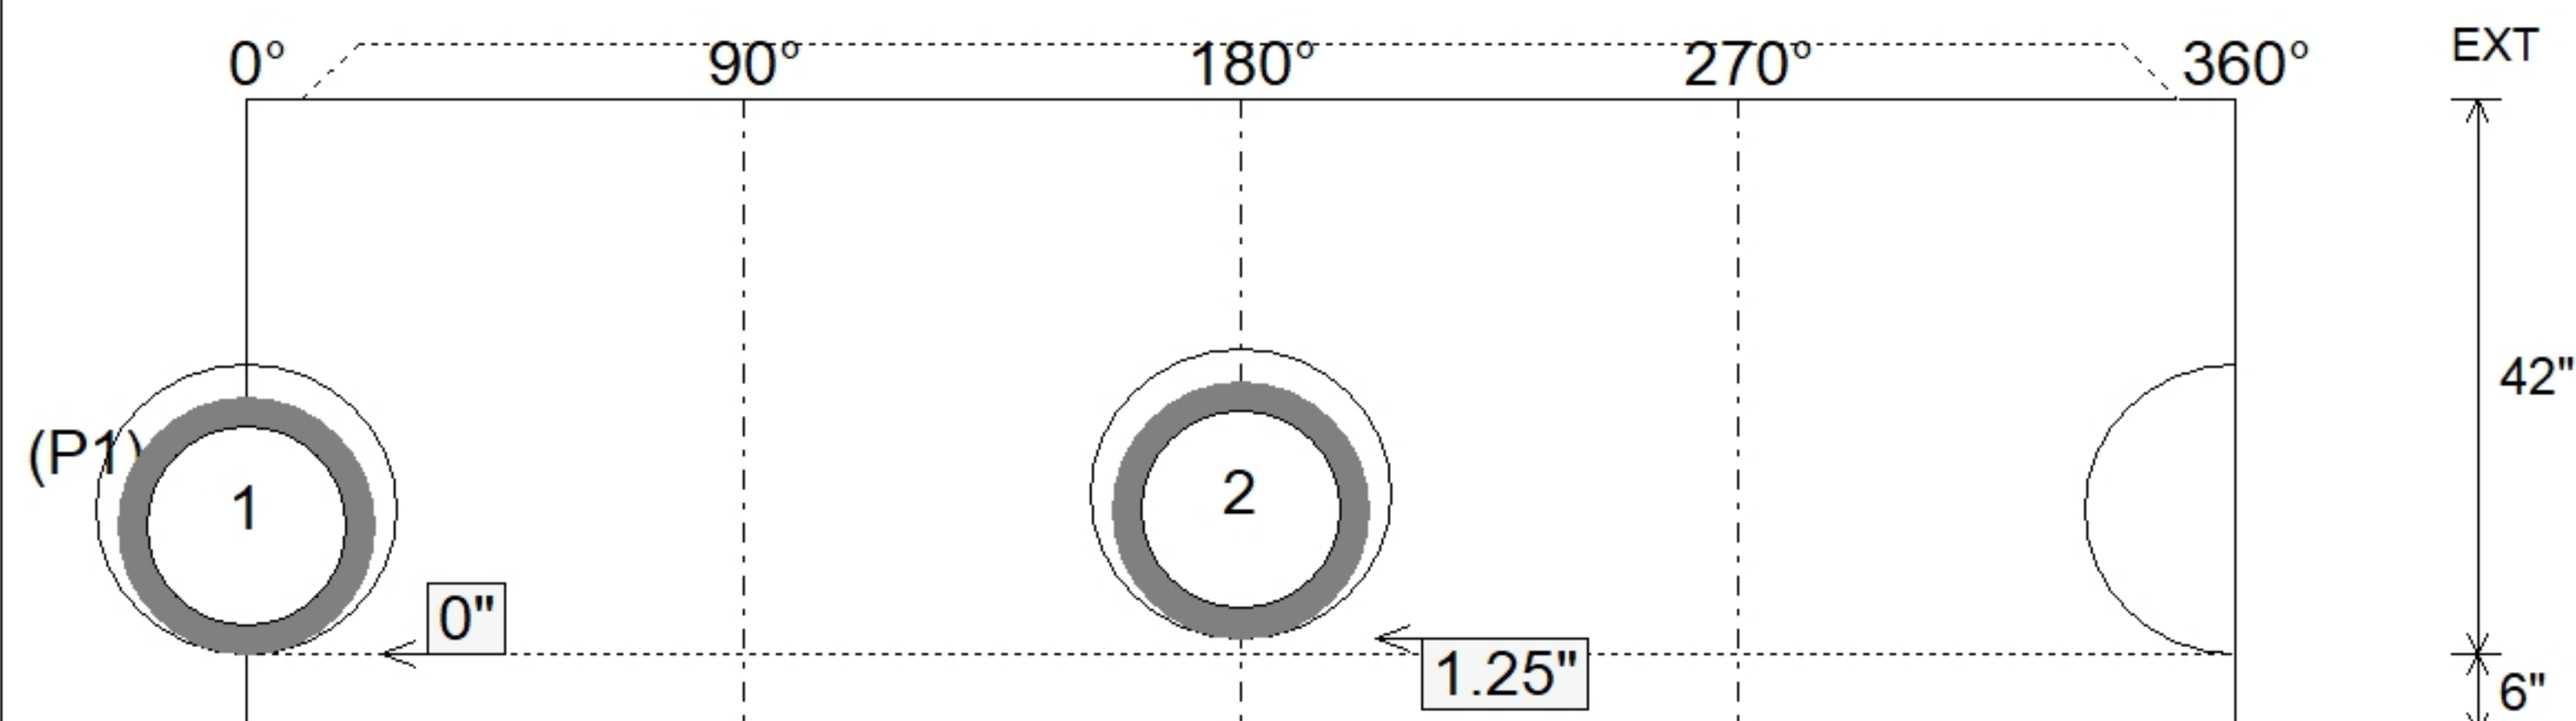

SUBMITTAL
APPROVED BY:
